




















ID	Task Mode	WBS	Task Name	Duration	Start	Finish	Predecessors	Feb 28, '21							Mar 7, '21							Mar 14, '21							Mar 21, '21							Mar 28, '21																				
								S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T																
1		1	Cadence Bank Parking garage	340.5 days	Tue 3/2/21	Tue 6/21/22																																																		
2		1.1	Project awarded	1 day	Tue 3/2/21	Tue 3/2/21																																																		
3		1.2	Preconstruction (Division 000000)	48 days	Tue 3/2/21	Thu 5/6/21																																																		
4		1.2.1	Contract agreement	2 days	Tue 3/2/21	Wed 3/3/21																																																		
5		1.2.2	Contract plan flip	3 days	Tue 3/2/21	Thu 3/4/21																																																		
6		1.2.3	Shop Drawings reinforcing steel	10 days	Thu 3/4/21	Wed 3/17/21																																																		
7		1.2.4	Shop Drawing precast panel	18 days	Tue 3/2/21	Thu 3/25/21																																																		
8		1.2.5	Shop Drawing elevators	6 days	Tue 3/2/21	Tue 3/9/21																																																		
9		1.2.6	Shop drawing for site utilities	7 days	Tue 3/2/21	Wed 3/10/21																																																		
10		1.2.7	Shop drawing review	10 days	Thu 3/18/21	Wed 3/31/21																																																		
11		1.2.8	Building drawings	35 days	Tue 3/2/21	Mon 4/19/21																																																		
12		1.2.9	Building permit	13 days	Tue 4/20/21	Thu 5/6/21	11																																																	
13		1.2.10	Meet about budget	2 days	Tue 3/2/21	Wed 3/3/21																																																		
14		1.2.11	Signed insurance documents	1 day	Tue 3/2/21	Tue 3/2/21																																																		
15		1.2.12	Go over safety plan	2 days	Tue 3/2/21	Wed 3/3/21																																																		
16		1.2.13	Initial schedule	12 days	Tue 3/2/21	Wed 3/17/21																																																		
17		1.2.14	Drawings approved	1 day	Tue 4/20/21	Tue 4/20/21	11																																																	
18		1.2.15	Permit approved	1 day	Wed 4/21/21	Wed 4/21/21	17																																																	
19		1.2.16	Subcontractor bid	30 days	Tue 3/2/21	Mon 4/12/21																																																		
20		1.2.17	Subcontractor award date	1 day	Tue 4/13/21	Tue 4/13/21	19																																																	
21		1.3	Sitework (Division 010000)	42.25 days	Wed 4/14/21	Fri 6/11/21																																																		
22		1.3.1	Mobilize job trailer	16 days	Wed 4/14/21	Wed 5/5/21	20																																																	
23		1.3.2	Insert jobsite fence	1 day	Thu 5/6/21	Thu 5/6/21	22																																																	
24		1.3.3	Put up jobsite signs	0.5 days	Fri 5/7/21	Fri 5/7/21	23																																																	
25		1.3.4	Insert barricades as needed	0.5 days	Fri 5/7/21	Fri 5/7/21	24																																																	
26		1.3.5	Locate utilities	2 days	Thu 5/6/21	Fri 5/7/21	22																																																	
27		1.3.6	Bust up asphalt parking lot	6 days	Mon 5/10/21	Mon 5/17/21	26																																																	
28		1.3.7	Excavate Retaining wall	6 days	Tue 5/18/21	Tue 5/25/21	27																																																	
29		1.3.8	Excavate Side walk	4 days	Wed 5/26/21	Mon 5/31/21	28																																																	
30		1.3.9	Haul off excess materials	4 days	Tue 5/18/21	Fri 5/21/21	27																																																	
31		1.3.10	Relocate utilities as needed	6 days	Mon 5/24/21	Mon 5/31/21	30																																																	
32		1.3.11	Relocate chiller utilities	4 days	Wed 5/26/21	Mon 5/31/21	28																																																	
33		1.3.12	Install irrigation sleeves	4 days	Mon 5/24/21	Thu 5/27/21	30																																																	
34		1.3.13	Demolish chiller building	0.75 days	Tue 6/1/21	Tue 6/1/21	31																																																	
35		1.3.14	Install temporary 60T chiller	7.5 days	Tue 6/1/21	Fri 6/11/21	34																																																	
36		1.3.15	Locate elevations of retail space	1 day	Tue 6/1/21	Tue 6/1/21	32																																																	
37		1.3.16	Locate elevations of parking deck	1 day	Tue 6/1/21	Tue 6/1/21	32																																																	
38		1.3.17	Grade site to elevation	4 days	Wed 6/2/21	Mon 6/7/21	37																																																	

Project: Parking garage schedu
Date: Sun 4/11/21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	WBS	Task Name	Duration	Start	Finish	Predecessors	Feb 28, '21							Mar 7, '21							Mar 14, '21							Mar 21, '21							Mar 28, '21																	
								S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T													
39	→	1.3.18	Install storm drains	4 days	Wed 5/26/21	Mon 5/31/21	28																																														
40	→	1.3.19	Backfill over storm drains	1 day	Tue 6/1/21	Tue 6/1/21	39																																														
41	→	1.3.20	Reroute water line to retail section	4 days	Wed 5/26/21	Mon 5/31/21	28																																														
42	→	1.3.21	Rough mechanical/plumbing	2 days	Tue 6/8/21	Wed 6/9/21	38																																														
43	→	1.3.22	Rough in electrical	2 days	Tue 6/8/21	Wed 6/9/21	38																																														
44	→	1.3.23	Rough in plumbing/elec. Inspection	1 day	Thu 6/10/21	Thu 6/10/21	43																																														
45	→	1.4	Foundation (Division 033000)	39 days	Fri 6/11/21	Wed 8/4/21																																															
46	→	1.4.1	Survey column location	1 day	Fri 6/11/21	Fri 6/11/21	44,38																																														
47	→	1.4.2	Soil testing	10 days	Mon 6/14/21	Fri 6/25/21	46																																														
48	→	1.4.3	Bore holes for piles	7 days	Mon 6/28/21	Tue 7/6/21	47																																														
49	→	1.4.4	Pour bell shaped columns	14 days	Wed 7/7/21	Mon 7/26/21	48																																														
50	→	1.4.5	Compact soil	2 days	Tue 7/27/21	Wed 7/28/21	49																																														
51	→	1.4.6	Top soil with limestone rock	1 day	Thu 7/29/21	Thu 7/29/21	50																																														
52	→	1.4.7	Commercial termite treating	1 day	Fri 7/30/21	Fri 7/30/21	51																																														
53	→	1.4.8	Insert below slab moisture barrier	1 day	Mon 8/2/21	Mon 8/2/21	52																																														
54	→	1.4.9	Insert elevator damp proofing	0.5 days	Tue 8/3/21	Tue 8/3/21	53																																														
55	→	1.4.10	Form/Pour Ground level slab for parking deck	5 days	Thu 7/29/21	Wed 8/4/21	63																																														
56	→	1.4.11	Form work for retail slab	2.5 days	Thu 7/29/21	Mon 8/2/21	63																																														
57	→	1.4.12	Pour Ground level slab for retail	1 day	Mon 8/2/21	Tue 8/3/21	56																																														
58	→	1.4.13	Form elevator pit	0.5 days	Tue 7/27/21	Tue 7/27/21	49																																														
59	→	1.4.14	Pour Elevator pit	0.5 days	Tue 7/27/21	Tue 7/27/21	58																																														
60	→	1.4.15	Form Stairwell Pit	1 day	Tue 7/27/21	Tue 7/27/21	49																																														
61	→	1.4.16	Pour Stairwell pit	1 day	Wed 7/28/21	Wed 7/28/21	60																																														
62	→	1.4.17	Form Stairwell pit	1 day	Tue 7/27/21	Tue 7/27/21	49																																														
63	→	1.4.18	Pour Stairwell Pit	1 day	Wed 7/28/21	Wed 7/28/21	62																																														
64	→	1.5	Retail system (Division 034000)	30 days	Thu 7/29/21	Wed 9/8/21																																															
65	→	1.5.1	Set precast insulated concrete panels	8 days	Thu 7/29/21	Mon 8/9/21	63																																														
66	→	1.5.2	Rough in mechanical systems	10 days	Tue 8/10/21	Mon 8/23/21	65																																														
67	→	1.5.3	Rough electrical systems	14 days	Tue 8/10/21	Fri 8/27/21	65																																														
68	→	1.5.4	Rough in plumbing systems	8 days	Mon 8/30/21	Wed 9/8/21	67																																														
69	→	1.6	Structural	66 days	Tue 8/10/21	Tue 11/9/21																																															
70	→	1.6.1	Place horizontal beams span 1 floor P1	2 days	Tue 8/10/21	Wed 8/11/21	65																																														
71	→	1.6.2	Place horizontal beams span 2 floor P1	2 days	Thu 8/12/21	Fri 8/13/21	70																																														
72	→	1.6.3	Place horizontal beams span 3 floor P1	2 days	Mon 8/16/21	Tue 8/17/21	71																																														
73	→	1.6.4	Place horizontal beams span 1 floor P2	2 days	Wed 8/18/21	Thu 8/19/21	72																																														
74	→	1.6.5	Place horizontal beams span 2 floor P2	2 days	Fri 8/20/21	Mon 8/23/21	73																																														
75	→	1.6.6	Place horizontal beams span 3 floor P2	2 days	Tue 8/24/21	Wed 8/25/21	74																																														
76	→	1.6.7	Place horizontal beams span 1 floor P3	2 days	Thu 8/26/21	Fri 8/27/21	75																																														

Project: Parking garage schedu
Date: Sun 4/11/21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	WBS	Task Name	Duration	Start	Finish	Predecessors	Feb 28, '21							Mar 7, '21							Mar 14, '21							Mar 21, '21							Mar 28, '21										
								S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T						
77	➔	1.6.8	Place horizontal beams span 2 floor P3	2 days	Mon 8/30/21	Tue 8/31/21	76																																							
78	➔	1.6.9	Place horizontal beams span 3 floor P3	2 days	Wed 9/1/21	Thu 9/2/21	77																																							
79	➔	1.6.10	Set span 1 double Ts P1	4 days	Fri 9/3/21	Wed 9/8/21	78																																							
80	➔	1.6.11	Insert temporary railing	1 day	Thu 9/9/21	Thu 9/9/21	79																																							
81	➔	1.6.12	Set span 2 double Ts P1	4 days	Fri 9/10/21	Wed 9/15/21	180																																							
82	➔	1.6.13	Insert temporary railing	1 day	Thu 9/16/21	Thu 9/16/21	81																																							
83	➔	1.6.14	Set span 3 double Ts P1	4 days	Fri 9/17/21	Wed 9/22/21	182																																							
84	➔	1.6.15	Insert temporary railing	1 day	Thu 9/23/21	Thu 9/23/21	83																																							
85	➔	1.6.16	Set span 1 double Ts P2	4 days	Fri 9/24/21	Wed 9/29/21	184																																							
86	➔	1.6.17	Insert temporary railing	1 day	Thu 9/30/21	Thu 9/30/21	85																																							
87	➔	1.6.18	Set span span 2 double Ts P2	4 days	Fri 10/1/21	Wed 10/6/21	186																																							
88	➔	1.6.19	Insert temporary railing	1 day	Thu 10/7/21	Thu 10/7/21	87																																							
89	➔	1.6.20	Set span 3 double Ts P2	4 days	Fri 10/8/21	Wed 10/13/21	188																																							
90	➔	1.6.21	Insert temporary railing	1 day	Thu 10/14/21	Thu 10/14/21	189																																							
91	➔	1.6.22	Set span 1 double Ts P3	4 days	Fri 10/15/21	Wed 10/20/21	190																																							
92	➔	1.6.23	Insert temporary railing	1 day	Thu 10/21/21	Thu 10/21/21	191																																							
93	➔	1.6.24	Set span 2 double Ts P3	4 days	Fri 10/22/21	Wed 10/27/21	192																																							
94	➔	1.6.25	Insert temporary railing	1 day	Thu 10/28/21	Thu 10/28/21	193																																							
95	➔	1.6.26	Set span 3 double Ts P3	4 days	Fri 10/29/21	Wed 11/3/21	194																																							
96	➔	1.6.27	Insert temporary railing	1 day	Thu 11/4/21	Thu 11/4/21	195																																							
97	➔	1.6.28	Reinforce/Pour span 1 topping P1	3 days	Fri 9/10/21	Tue 9/14/21	80																																							
98	➔	1.6.29	Reinforce/Pour span 2 topping P1	3 days	Fri 9/17/21	Tue 9/21/21	82																																							
99	➔	1.6.30	Reinforce/Pour span 3 topping P1	3 days	Fri 9/24/21	Tue 9/28/21	84																																							
100	➔	1.6.31	Reinforce/Pour span 1 topping P2	3 days	Fri 10/1/21	Tue 10/5/21	86																																							
101	➔	1.6.32	Reinforce/Pour span 2 topping P2	3 days	Fri 10/8/21	Tue 10/12/21	188																																							
102	➔	1.6.33	Reinforce/Pour span 3 topping P2	3 days	Fri 10/15/21	Tue 10/19/21	190																																							
103	➔	1.6.34	Reinforce/Pour span 1 topping P3	3 days	Fri 10/22/21	Tue 10/26/21	192																																							
104	➔	1.6.35	Reinforce/Pour span 2 topping P3	3 days	Fri 10/29/21	Tue 11/2/21	194																																							
105	➔	1.6.36	Reinforce/Pour span 3 topping P3	3 days	Fri 11/5/21	Tue 11/9/21	196																																							
106	➔	1.7	Elevator/Stairs (Division 142000)	36 days	Thu 11/4/21	Thu 12/23/21																																								
107	➔	1.7.1	Set up scaffoldings	1 day	Thu 11/4/21	Thu 11/4/21	195																																							
108	➔	1.7.2	Formwork for Elevator shaft P1	1 day	Fri 11/5/21	Fri 11/5/21	107																																							
109	➔	1.7.3	Pour shaft P1	2 days	Mon 11/8/21	Tue 11/9/21	108																																							
110	➔	1.7.4	Formwork for Elevator shaft P2	1 day	Wed 11/10/21	Wed 11/10/21	109																																							
111	➔	1.7.5	Pour shaft P2	2 days	Thu 11/11/21	Fri 11/12/21	110																																							
112	➔	1.7.6	Formwork for Elevator shaft P3	1 day	Mon 11/15/21	Mon 11/15/21	111																																							
113	➔	1.7.7	Pour shaft P3	2 days	Tue 11/16/21	Wed 11/17/21	112																																							
114	➔	1.7.8	Set up scaffolding	1 day	Thu 11/18/21	Thu 11/18/21	113																																							

Project: Parking garage schedu
Date: Sun 4/11/21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	WBS	Task Name	Duration	Start	Finish	Predecessors	Feb 28, '21							Mar 7, '21							Mar 14, '21							Mar 21, '21							Mar 28, '21						
								S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T		
115	➔	1.7.9	Pour stairwell pit	2 days	Fri 11/19/21	Mon 11/22/21	114																																			
116	➔	1.7.10	Formwork for stairwell shaft P1	1 day	Tue 11/23/21	Tue 11/23/21	115																																			
117	➔	1.7.11	Pour shaft P1	2 days	Wed 11/24/21	Thu 11/25/21	116																																			
118	➔	1.7.12	Formwork for stairwell shaft P2	1 day	Fri 11/26/21	Fri 11/26/21	117																																			
119	➔	1.7.13	Pour shaft P2	2 days	Mon 11/29/21	Tue 11/30/21	118																																			
120	➔	1.7.14	Formwork for stairwell shaft P3	1 day	Wed 12/1/21	Wed 12/1/21	119																																			
121	➔	1.7.15	Pour shaft P3	2 days	Thu 12/2/21	Fri 12/3/21	120																																			
122	➔	1.7.16	Insert and secure stair system	2 days	Mon 12/6/21	Tue 12/7/21	121																																			
123	➔	1.7.17	Set up scaffolding	1 day	Wed 12/8/21	Wed 12/8/21	122																																			
124	➔	1.7.18	Formwork for stairwell shaft P1	1 day	Thu 12/9/21	Thu 12/9/21	123																																			
125	➔	1.7.19	Pour shaft P1	2 days	Fri 12/10/21	Mon 12/13/21	124																																			
126	➔	1.7.20	Formwork for stairwell shaft P2	1 day	Tue 12/14/21	Tue 12/14/21	125																																			
127	➔	1.7.21	Pour shaft P2	2 days	Wed 12/15/21	Thu 12/16/21	126																																			
128	➔	1.7.22	Formwork for stairwell shaft P3	1 day	Fri 12/17/21	Fri 12/17/21	127																																			
129	➔	1.7.23	Pour shaft P3	2 days	Mon 12/20/21	Tue 12/21/21	128																																			
130	➔	1.7.24	Insert and secure stair system	2 days	Wed 12/22/21	Thu 12/23/21	129																																			
131	➔	1.8	Cladding (Division 034000)	32.5 days	Fri 12/24/21	Tue 2/8/22																																				
132	➔	1.8.1	Insert and attach precast panels	26.5 days	Fri 12/24/21	Mon 1/31/22	130																																			
133	➔	1.8.2	Install live awning system	6 days	Mon 1/31/22	Tue 2/8/22	132																																			
134	➔	1.9	Mechanical/Electrical (Division 230000/260000)	89 days	Mon 1/31/22	Fri 6/3/22																																				
135	➔	1.9.1	Run conduit for lights	9 days	Mon 1/31/22	Fri 2/11/22	132																																			
136	➔	1.9.2	Run conduit for elevator	1 day	Mon 1/31/22	Tue 2/1/22	132																																			
137	➔	1.9.3	Install A/C system for retail	3 days	Tue 2/1/22	Fri 2/4/22	136																																			
138	➔	1.9.4	Run conduit fire suppression system	2 days	Fri 2/4/22	Tue 2/8/22	137																																			
139	➔	1.9.5	Run conduit for parking lot control system	3 days	Tue 2/8/22	Fri 2/11/22	138																																			
140	⏏	➔	1.9.6	Pull wires to all parking deck locations	9 days	Fri 2/11/22	Mon 5/23/22	139																																		
141	➔	1.9.7	Run retail electrical	3 days	Mon 5/23/22	Thu 5/26/22	140																																			
142	➔	1.9.8	Run conduit and wire for solar panels	4 days	Thu 5/26/22	Wed 6/1/22	141																																			
143	➔	1.9.9	Electrical inspection	1 day	Wed 6/1/22	Thu 6/2/22	142																																			
144	➔	1.9.10	Fire suppression inspection	1 day	Thu 6/2/22	Fri 6/3/22	143																																			
145	➔	1.10	Plumbing (Division 220000)	12 days	Fri 6/3/22	Tue 6/21/22																																				
146	➔	1.10.1	Run plumbing for fire suppression	12 days	Fri 6/3/22	Tue 6/21/22	144																																			
147	➔	1.11	Dampproofing all locations (Division 071000)	216.5 days	Tue 8/10/21	Wed 6/8/22																																				
148	➔	1.11.1	Bituminous dampproofing	3 days	Tue 8/10/21	Thu 8/12/21	62,65																																			
149	➔	1.11.2	Sheet waterproofing	2 days	Tue 8/10/21	Wed 8/11/21	62,65																																			
150	➔	1.11.3	Firestopping stairwells, elevators, mech/elec ro	3 days	Fri 6/3/22	Wed 6/8/22	143,144																																			
151	➔	1.12	Exterior improvements (Division 032000)	9 days	Tue 2/8/22	Mon 2/21/22																																				
152	➔	1.12.1	Rough grade retail roadside staircase	2 days	Tue 2/8/22	Thu 2/10/22	133																																			


Project: Parking garage schedu
Date: Sun 4/11/21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			


ID	Task Mode	WBS	Task Name	Duration	Start	Finish	Predecessors	Feb 28, '21							Mar 7, '21							Mar 14, '21							Mar 21, '21							Mar 28, '21						
								S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T		
153		1.12.2	Form retail roadside staircase	5 days	Thu 2/10/22	Thu 2/17/22	152																																			
154		1.12.3	Pour retail roadside retail staircase	2 days	Thu 2/17/22	Mon 2/21/22	153																																			
155		1.12.4	Lay Bermuda sod	1 day	Thu 2/17/22	Fri 2/18/22	168																																			
156		1.13	Finishes (Division 310000/130000/079513/0841)	296.5 days	Tue 3/2/21	Wed 4/20/21																																				
157		1.13.1	Pedestrian and vehicular traffic markings	3 days	Mon 2/21/22	Thu 2/24/22	154																																			
158		1.13.2	Painting signage	2 days	Thu 2/24/22	Mon 2/28/22	157																																			
159		1.13.3	Striping	2 days	Mon 2/28/22	Wed 3/2/22	158																																			
160		1.13.4	Install hollow metal door hardware	5 days	Wed 3/2/22	Wed 3/9/22	159																																			
161		1.13.5	Install/adjust metal hollow doors	2 days	Wed 3/9/22	Fri 3/11/22	160																																			
162		1.13.6	Insert parking control fabricated booth	3 days	Wed 3/9/22	Mon 3/14/22	160																																			
163		1.13.7	Install elevators	7 days	Mon 3/14/22	Wed 3/23/22	162																																			
164		1.13.8	Joint sealants	1.5 days	Wed 3/23/22	Thu 3/24/22	163																																			
165		1.13.9	Expansion joint filler	1.5 days	Wed 3/23/22	Thu 3/24/22	163																																			
166		1.13.10	Gutters and downspouts	2 days	Fri 3/25/22	Mon 3/28/22	165																																			
167		1.13.11	Insert storefronts for retail	4 days	Tue 2/8/22	Mon 2/14/22	133																																			
168		1.13.12	Install metal stud framing	3 days	Mon 2/14/22	Thu 2/17/22	167																																			
169		1.13.13	Install interior insulation	1 day	Thu 2/17/22	Fri 2/18/22	168																																			
170		1.13.14	Gypsum board install, mud/sand finsh	3 days	Fri 2/18/22	Wed 2/23/22	169																																			
171		1.13.15	Acoustical ceilings	6 days	Wed 2/23/22	Thu 3/3/22	170																																			
172		1.13.16	Insert toilets and toilet accessories	0.5 days	Thu 3/3/22	Thu 3/3/22	171																																			
173		1.13.17	Fire extinguisher cabinets	0.5 days	Fri 3/4/22	Fri 3/4/22	172																																			
174		1.13.18	Install elevator cab finishes	2 days	Fri 3/4/22	Tue 3/8/22	173																																			
175		1.13.19	Insert solar panels on P3	14 days	Tue 3/8/22	Mon 3/28/22	174																																			
176		1.13.20	Final Inspection	1 day	Mon 3/28/22	Tue 3/29/22	175																																			
177		1.13.21	Certificate of occupancy	0 days	Tue 3/29/22	Tue 3/29/22	176																																			
178		1.13.22	Punch list	8 days	Tue 3/29/22	Fri 4/8/22	177																																			
179		1.13.23	Weather buffer	12 days	Tue 3/2/21	Wed 3/17/21																																				
180		1.13.24	Attach wood system to elevators, sidewalls, storefront	17 days	Mon 3/28/22	Wed 4/20/22	175																																			
181		1.13.25	Plant trees	2 days	Mon 3/28/22	Wed 3/30/22	175																																			
182		1.13.26	Plant shrubs	2 days	Mon 3/28/22	Wed 3/30/22	175																																			
183		1.13.27	Install irrigation systems	4 days	Tue 3/2/21	Fri 3/5/21																																				
184		1.13.28	Repave necessary roads after project finish date	3 days	Tue 3/2/21	Thu 3/4/21																																				
185		1.13.29	Repour sidewalk	1.5 days	Tue 3/2/21	Wed 3/3/21																																				

Project: Parking garage schedu
Date: Sun 4/11/21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

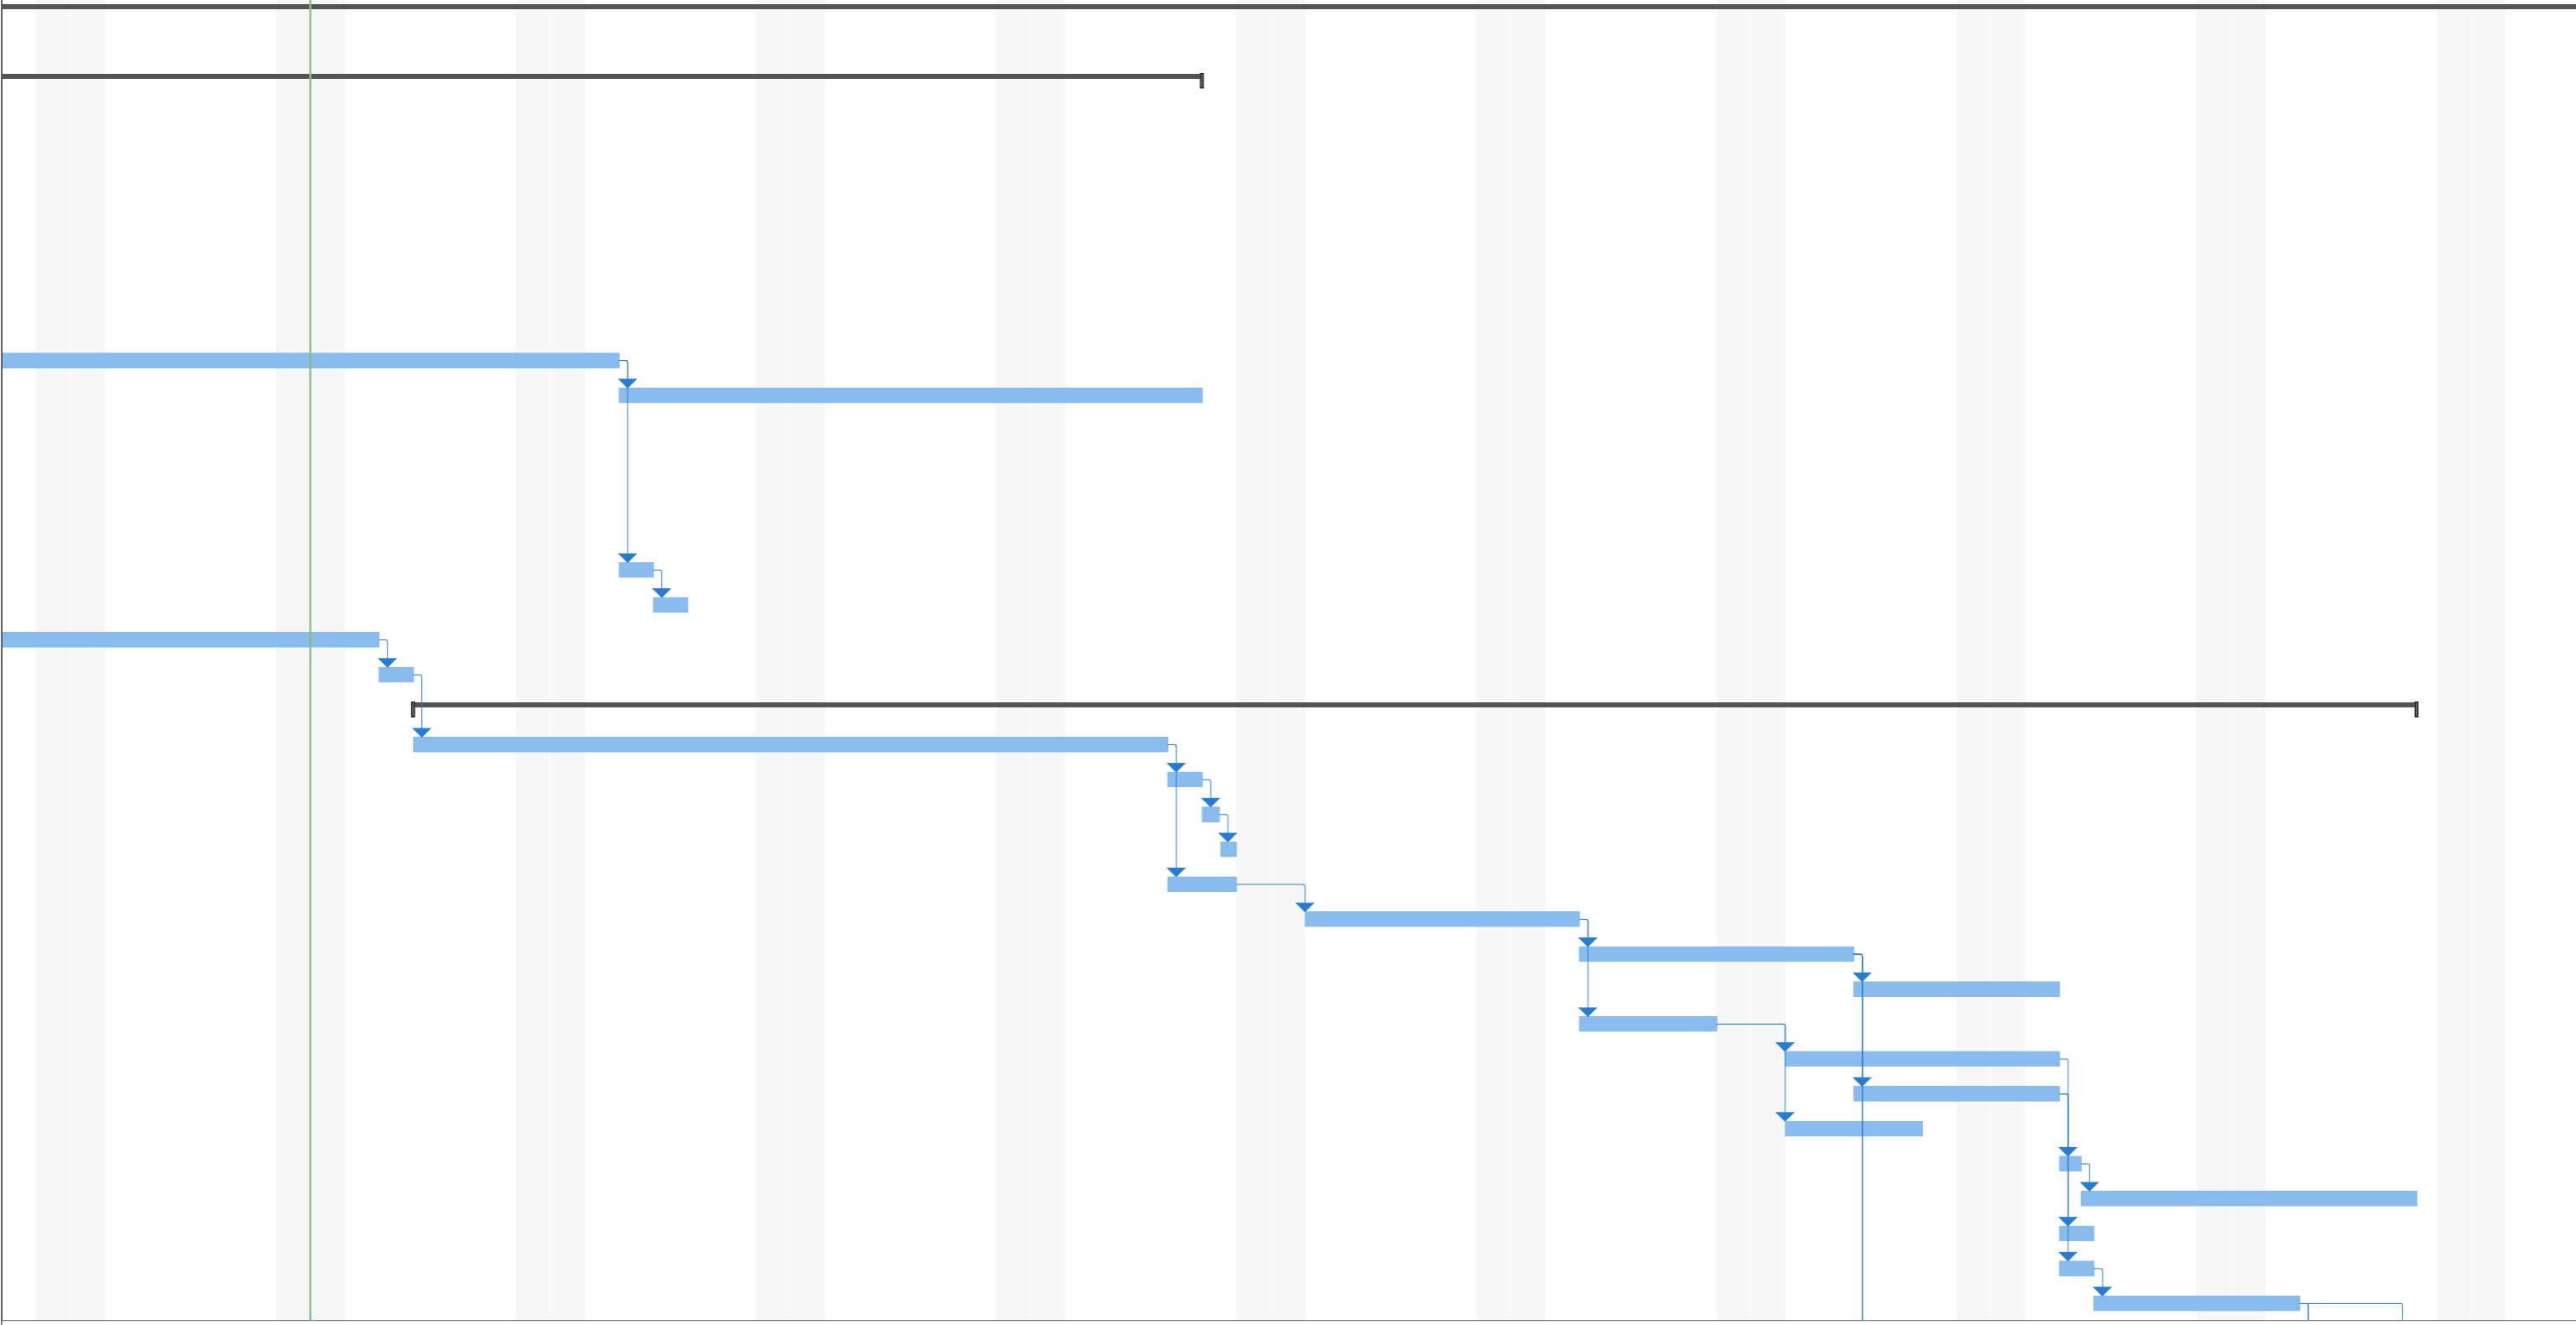


Project: Parking garage schedu Date: Sun 4/11/21	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

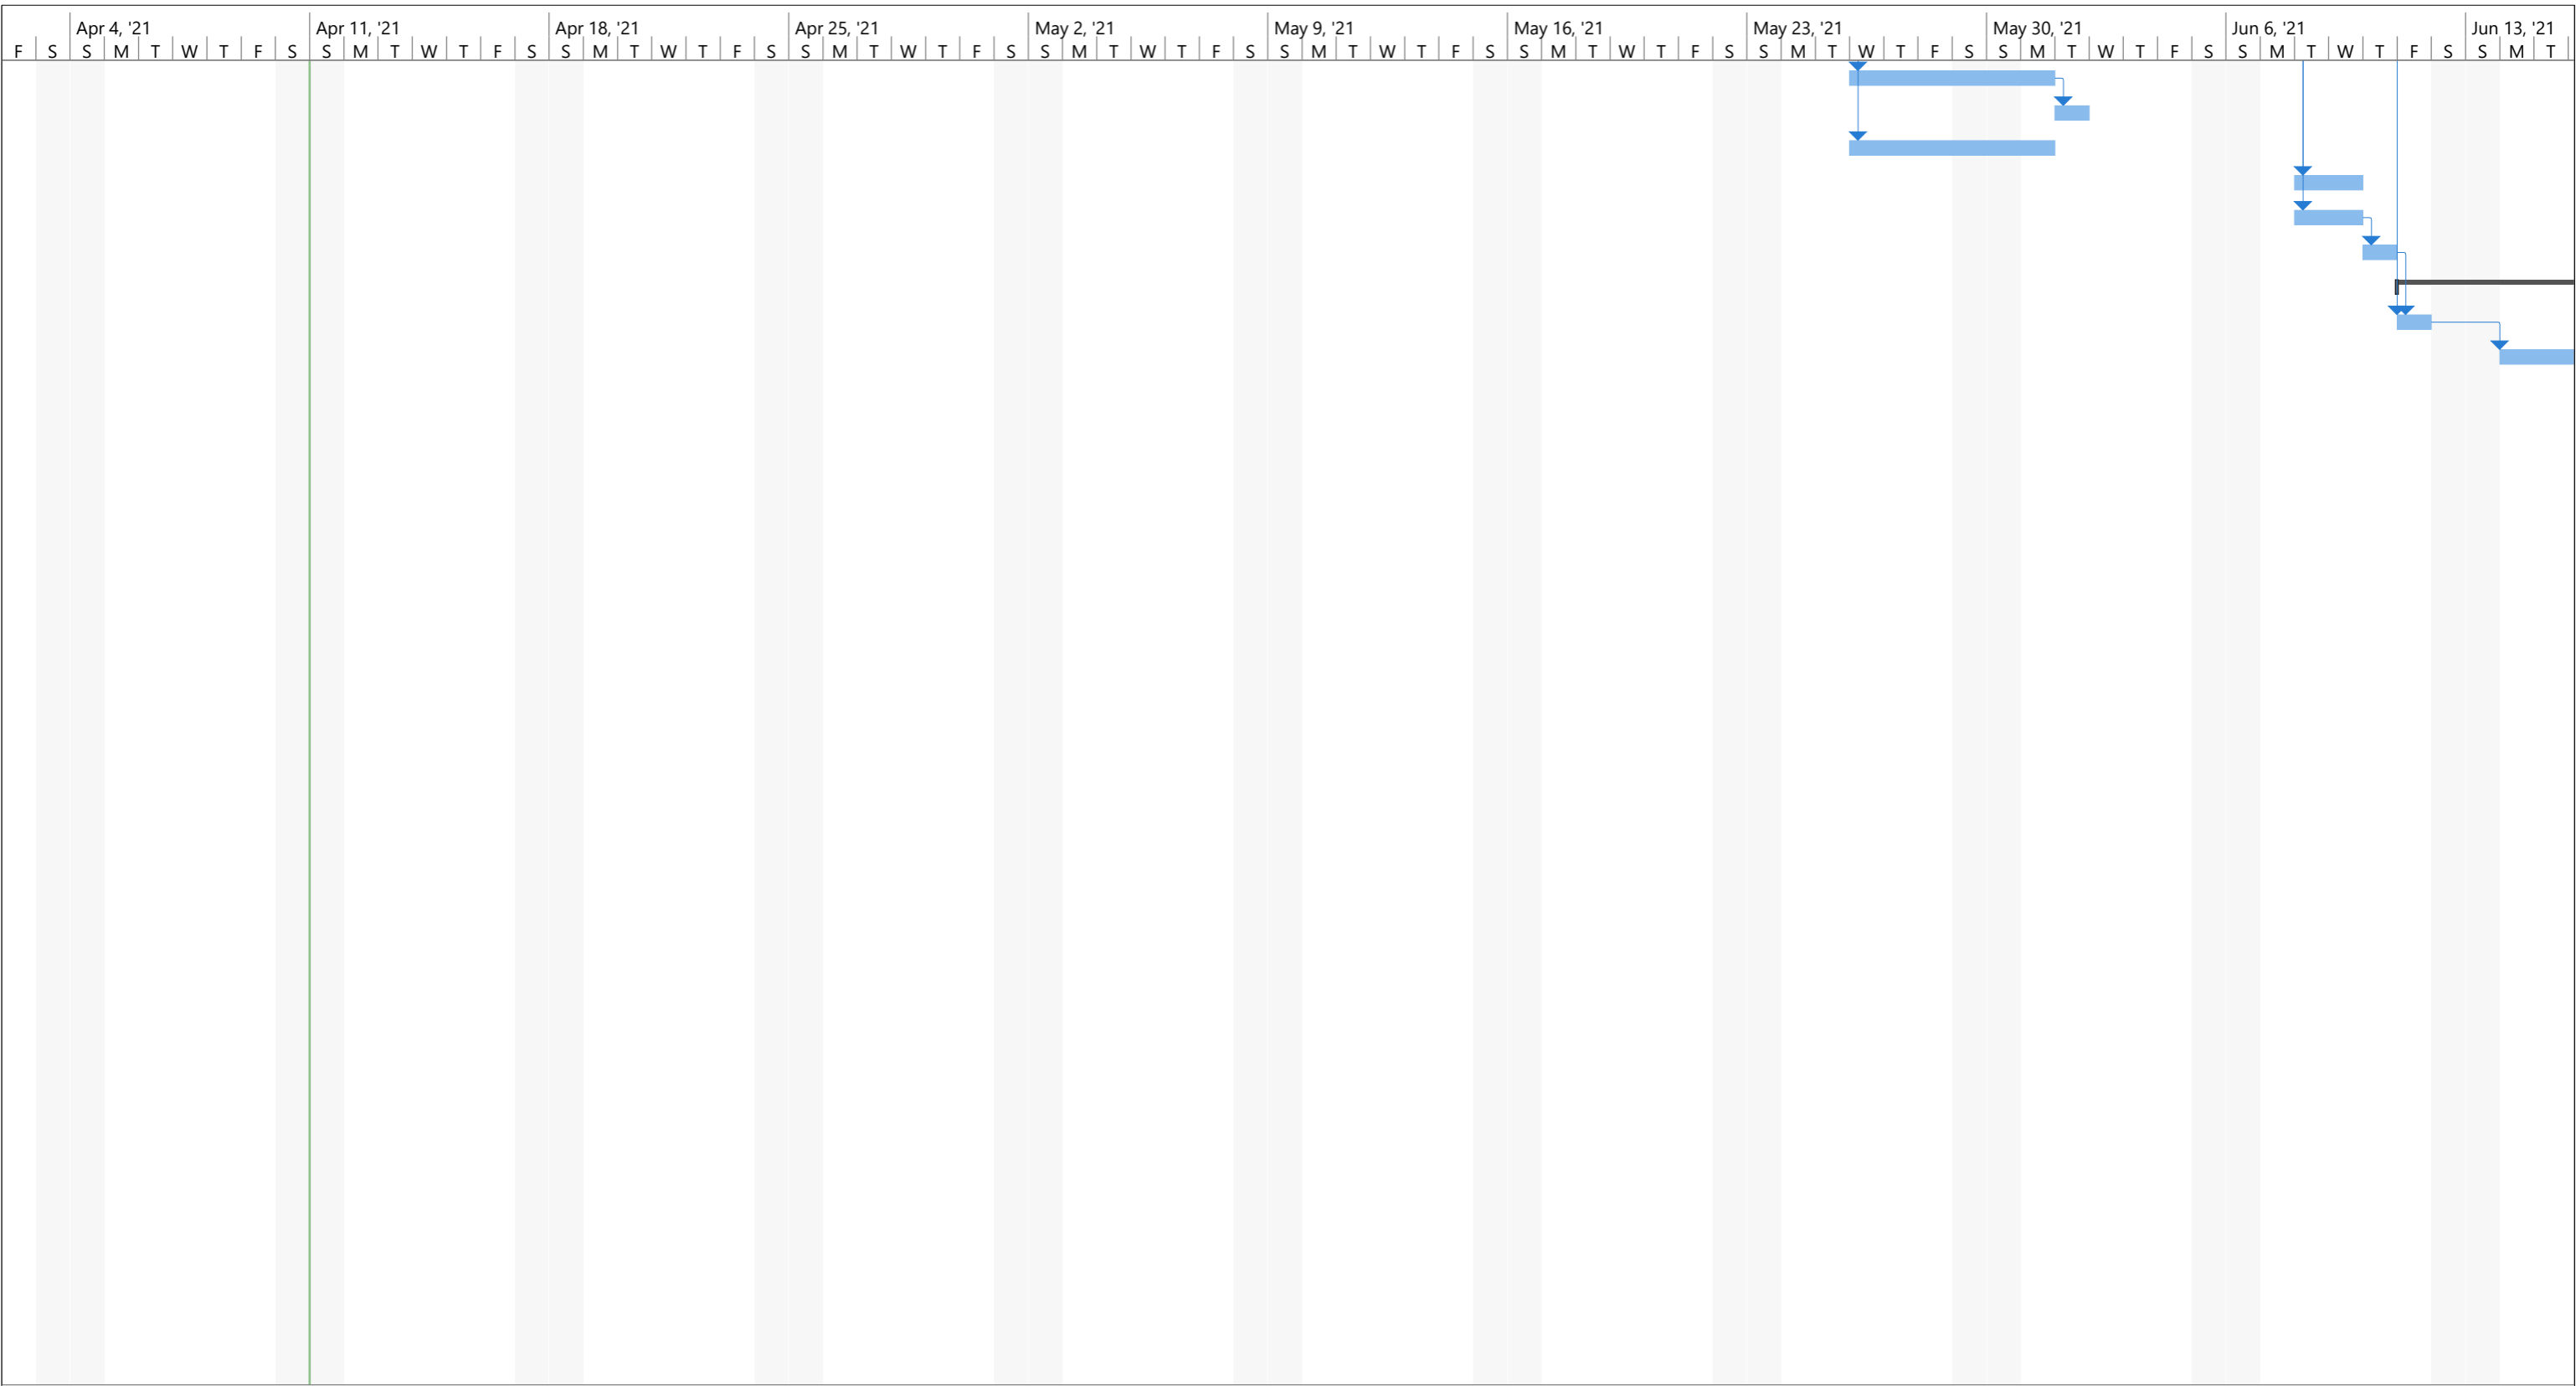


Project: Parking garage schedu
Date: Sun 4/11/21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

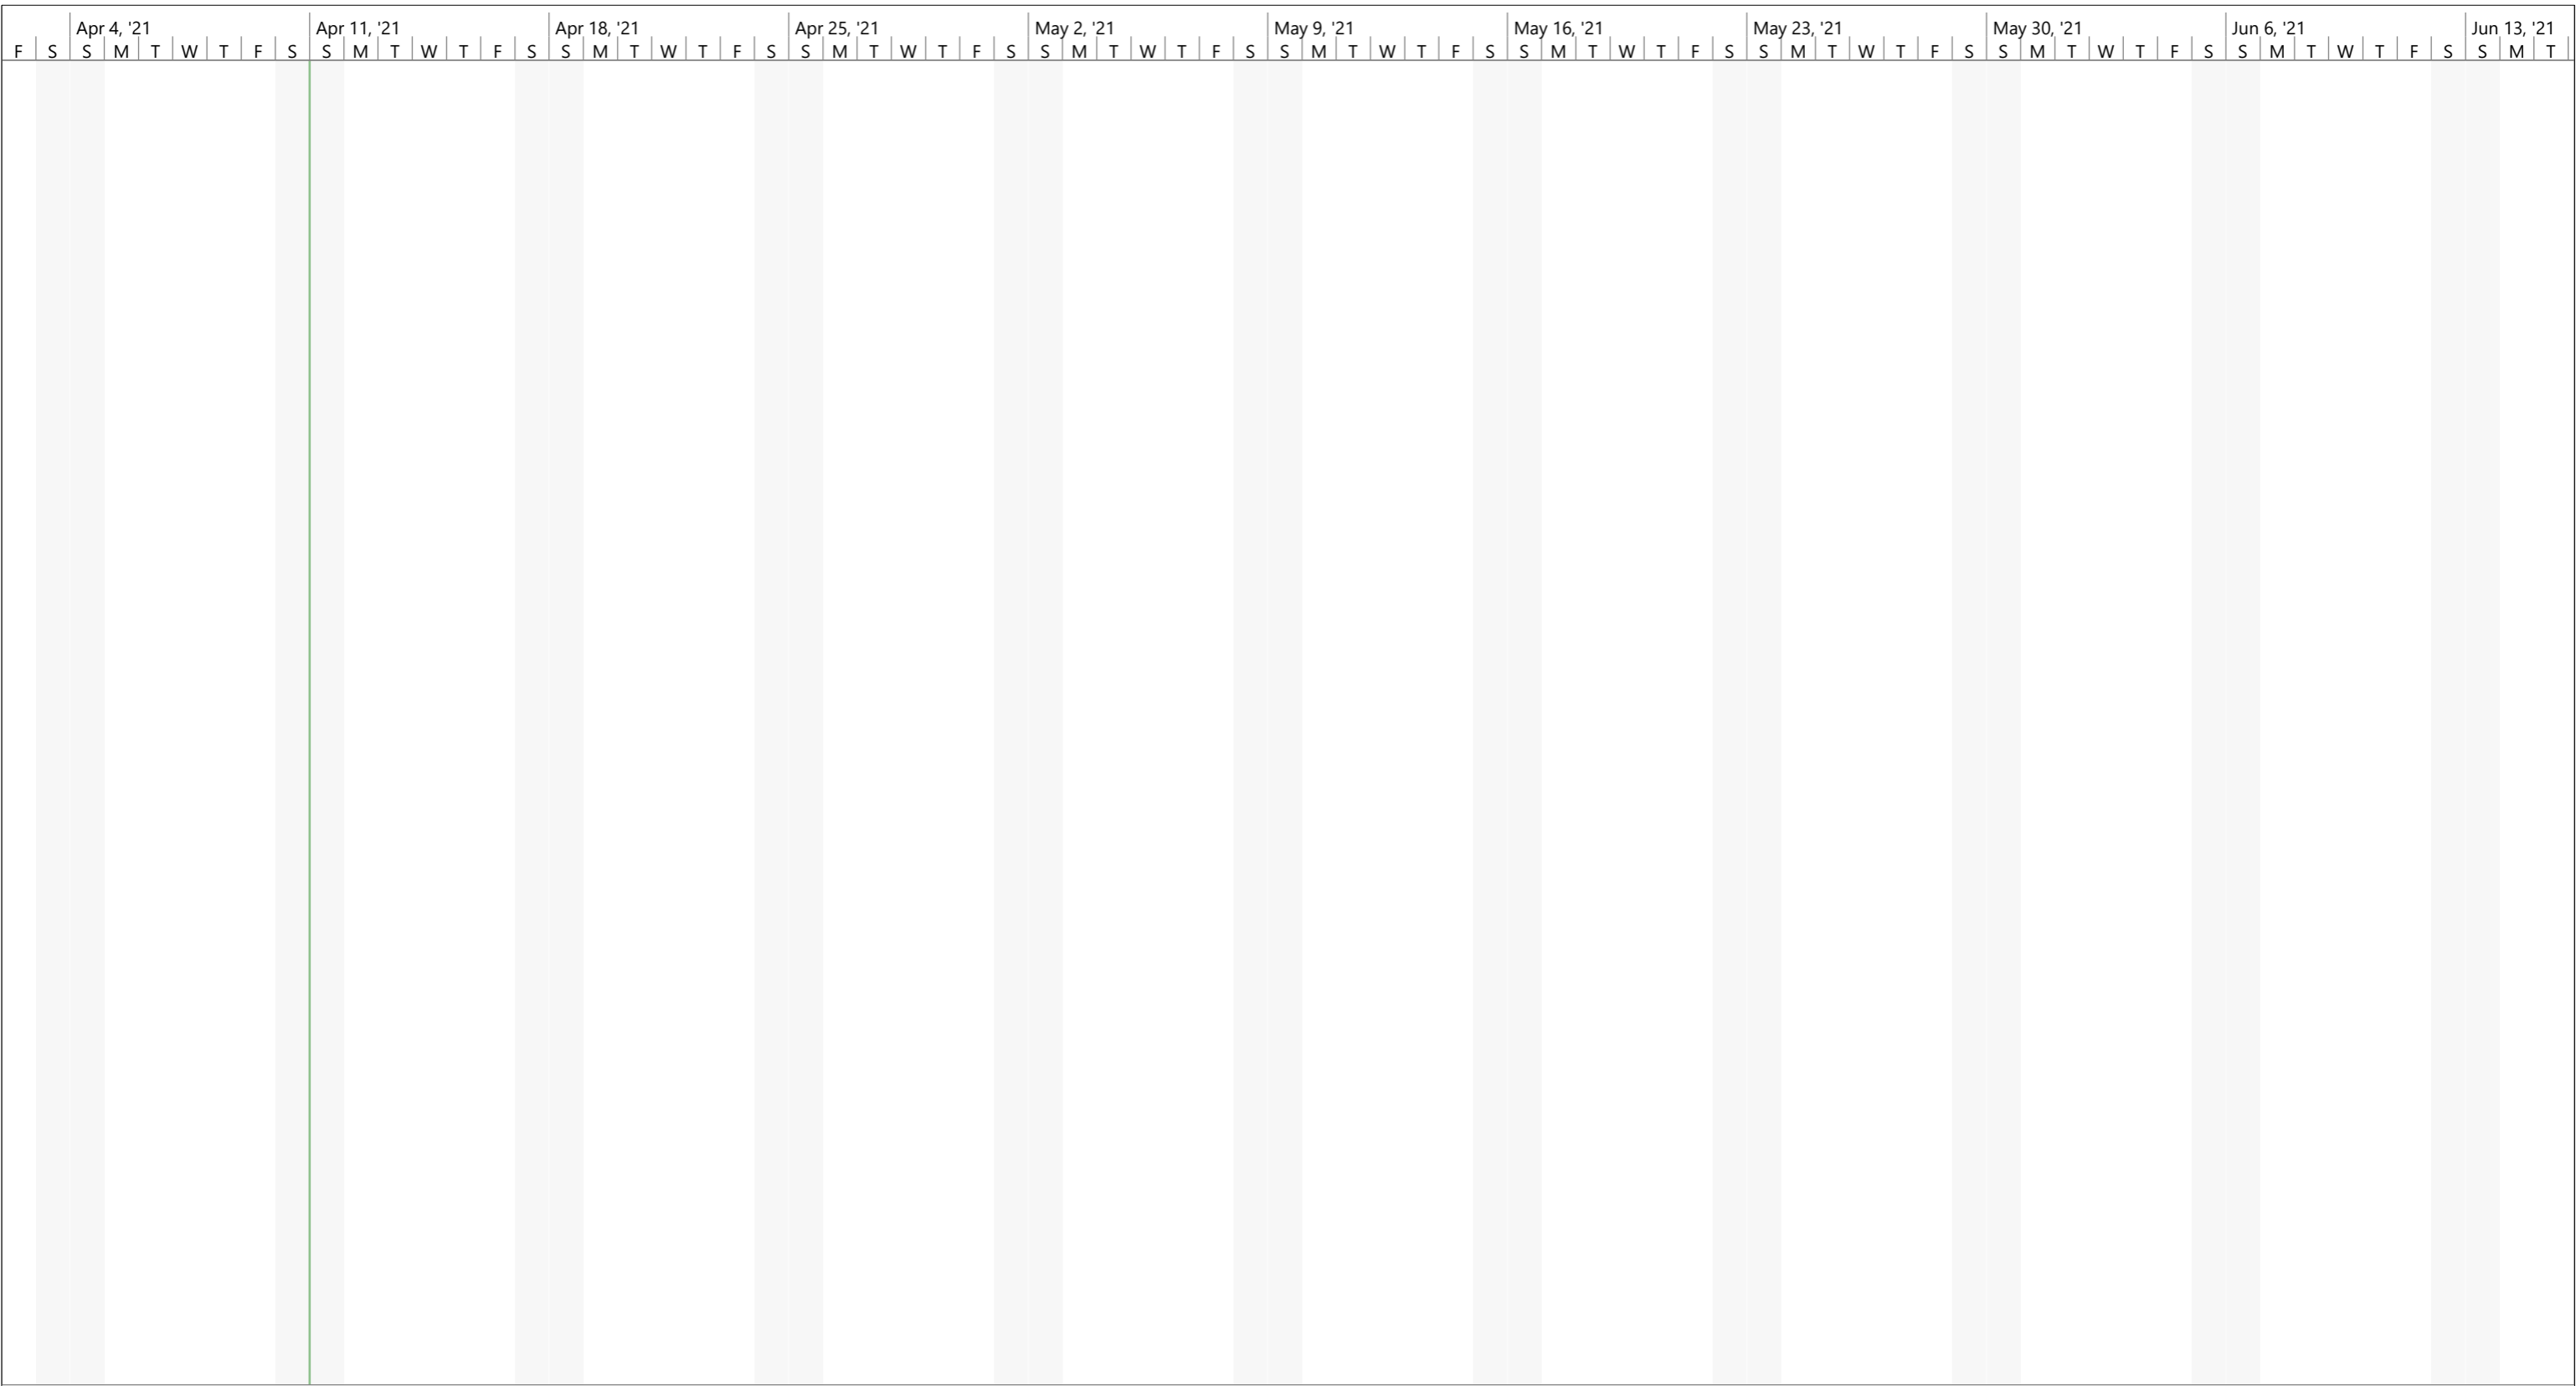


Project: Parking garage schedu
Date: Sun 4/11/21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

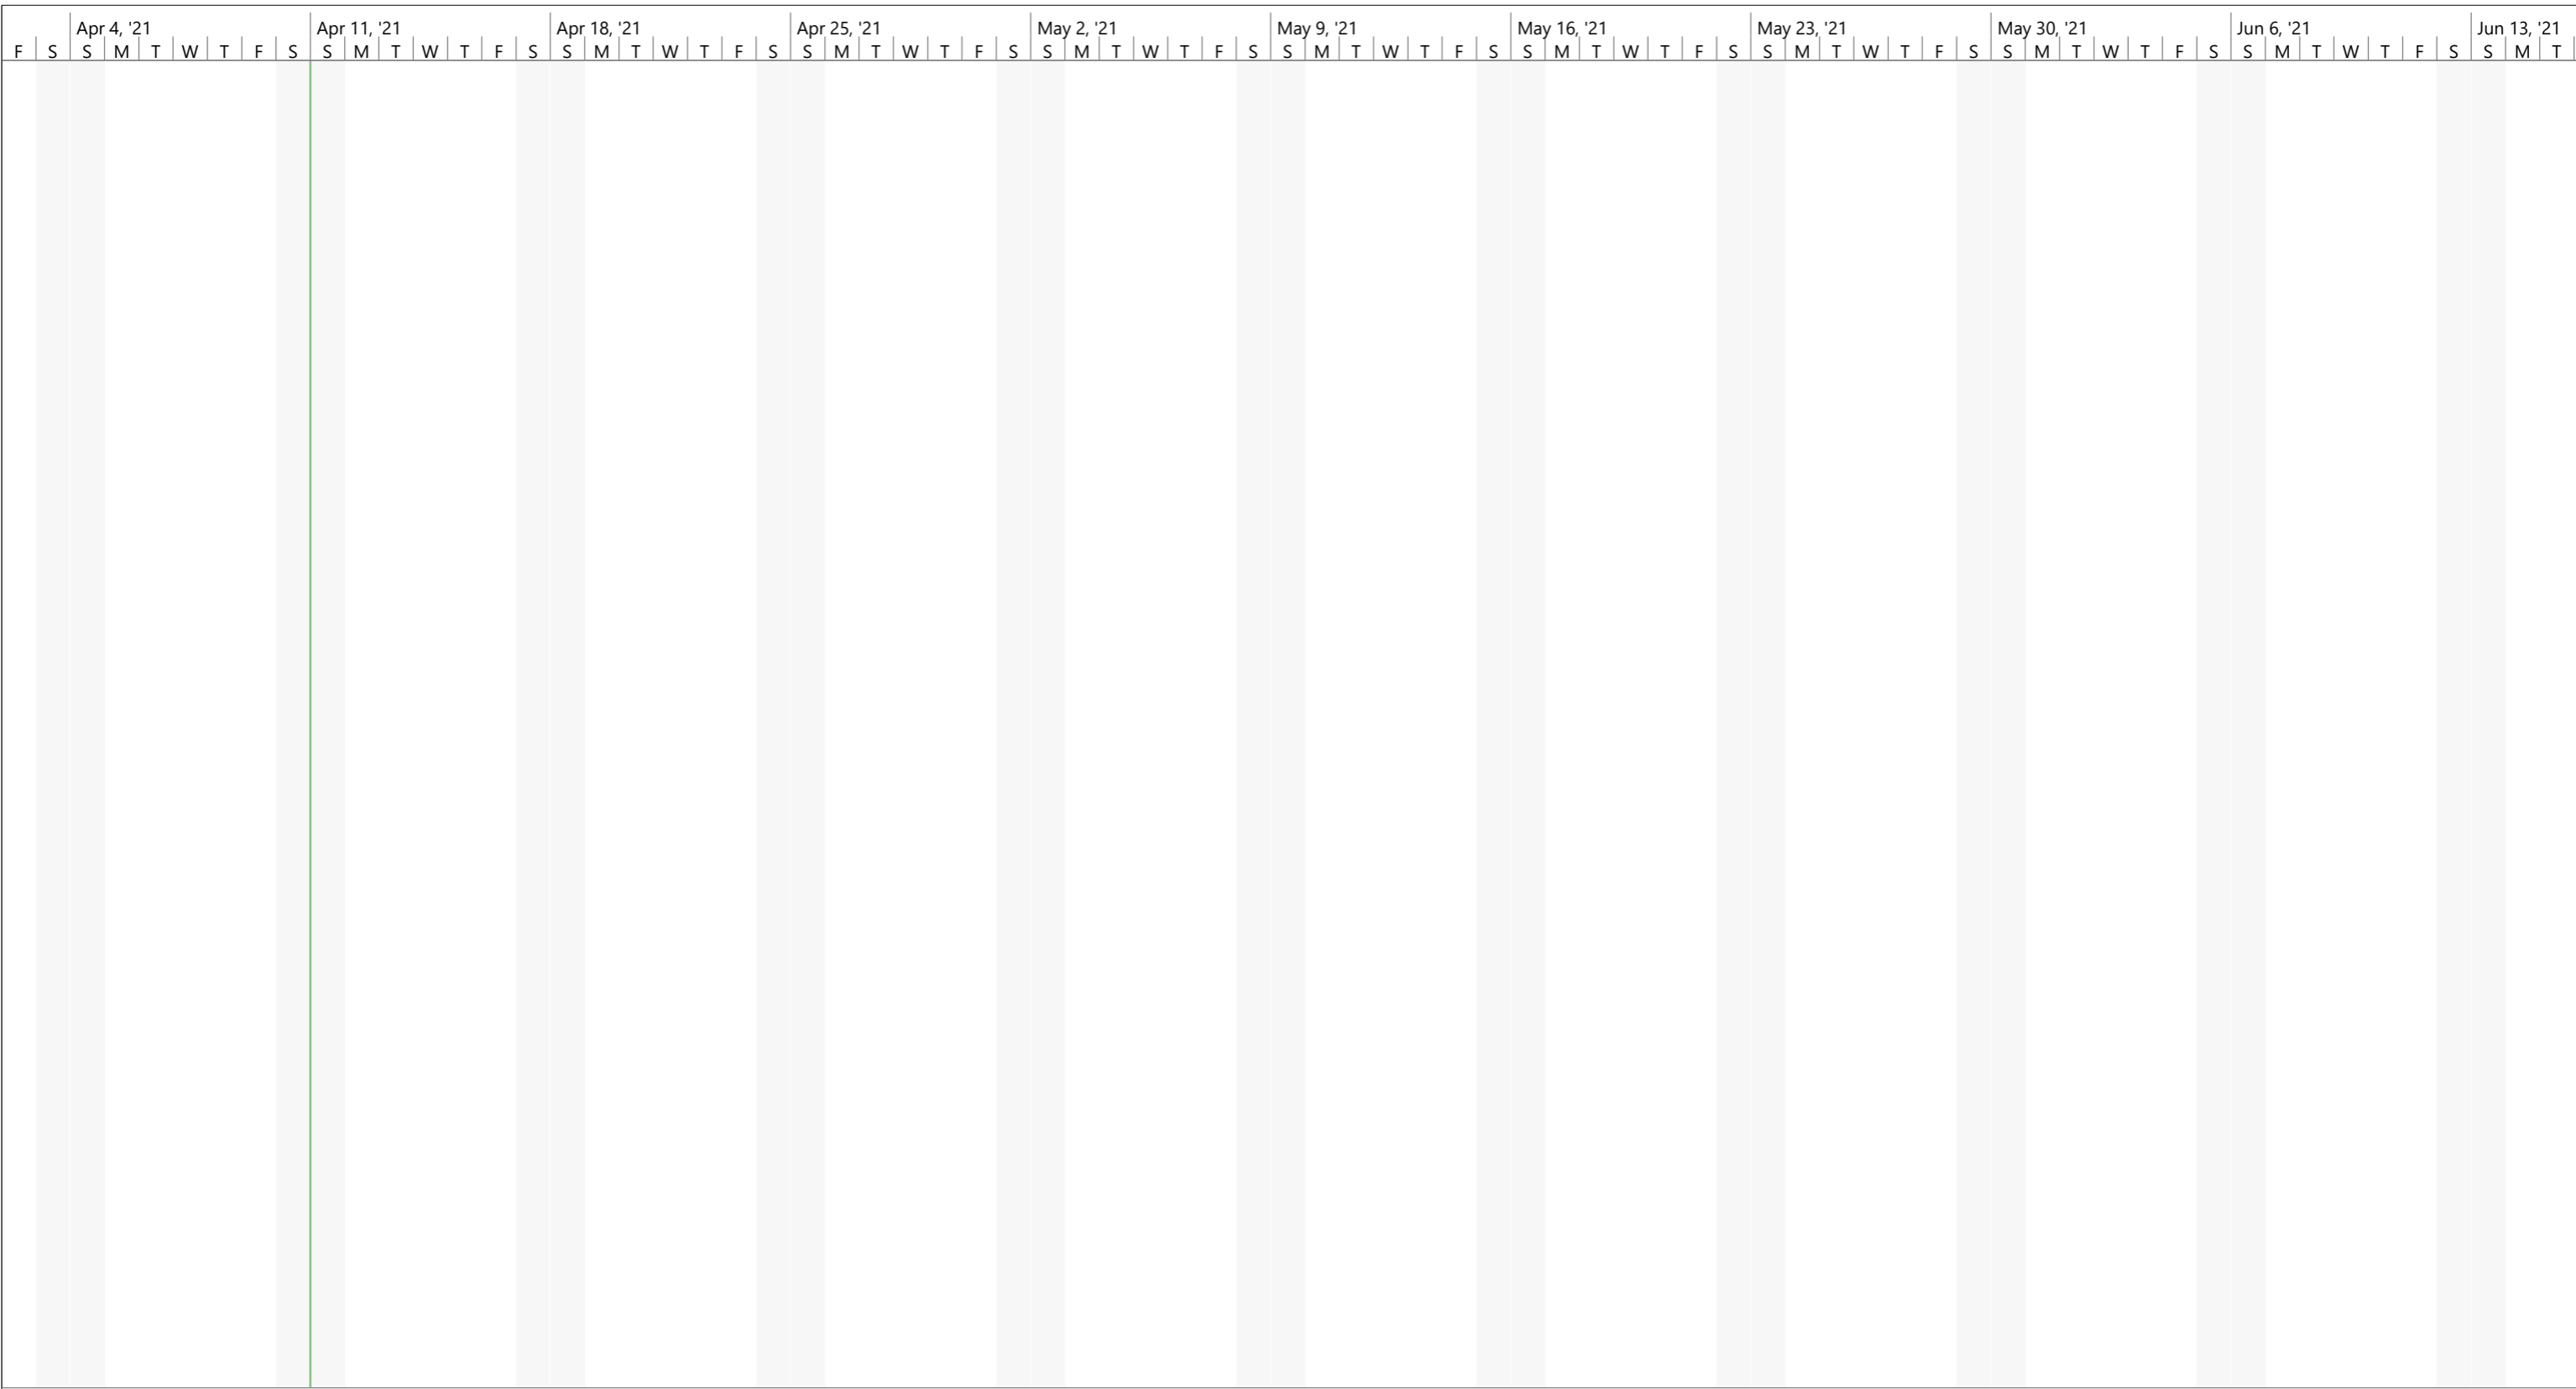


Project: Parking garage schedu
Date: Sun 4/11/21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

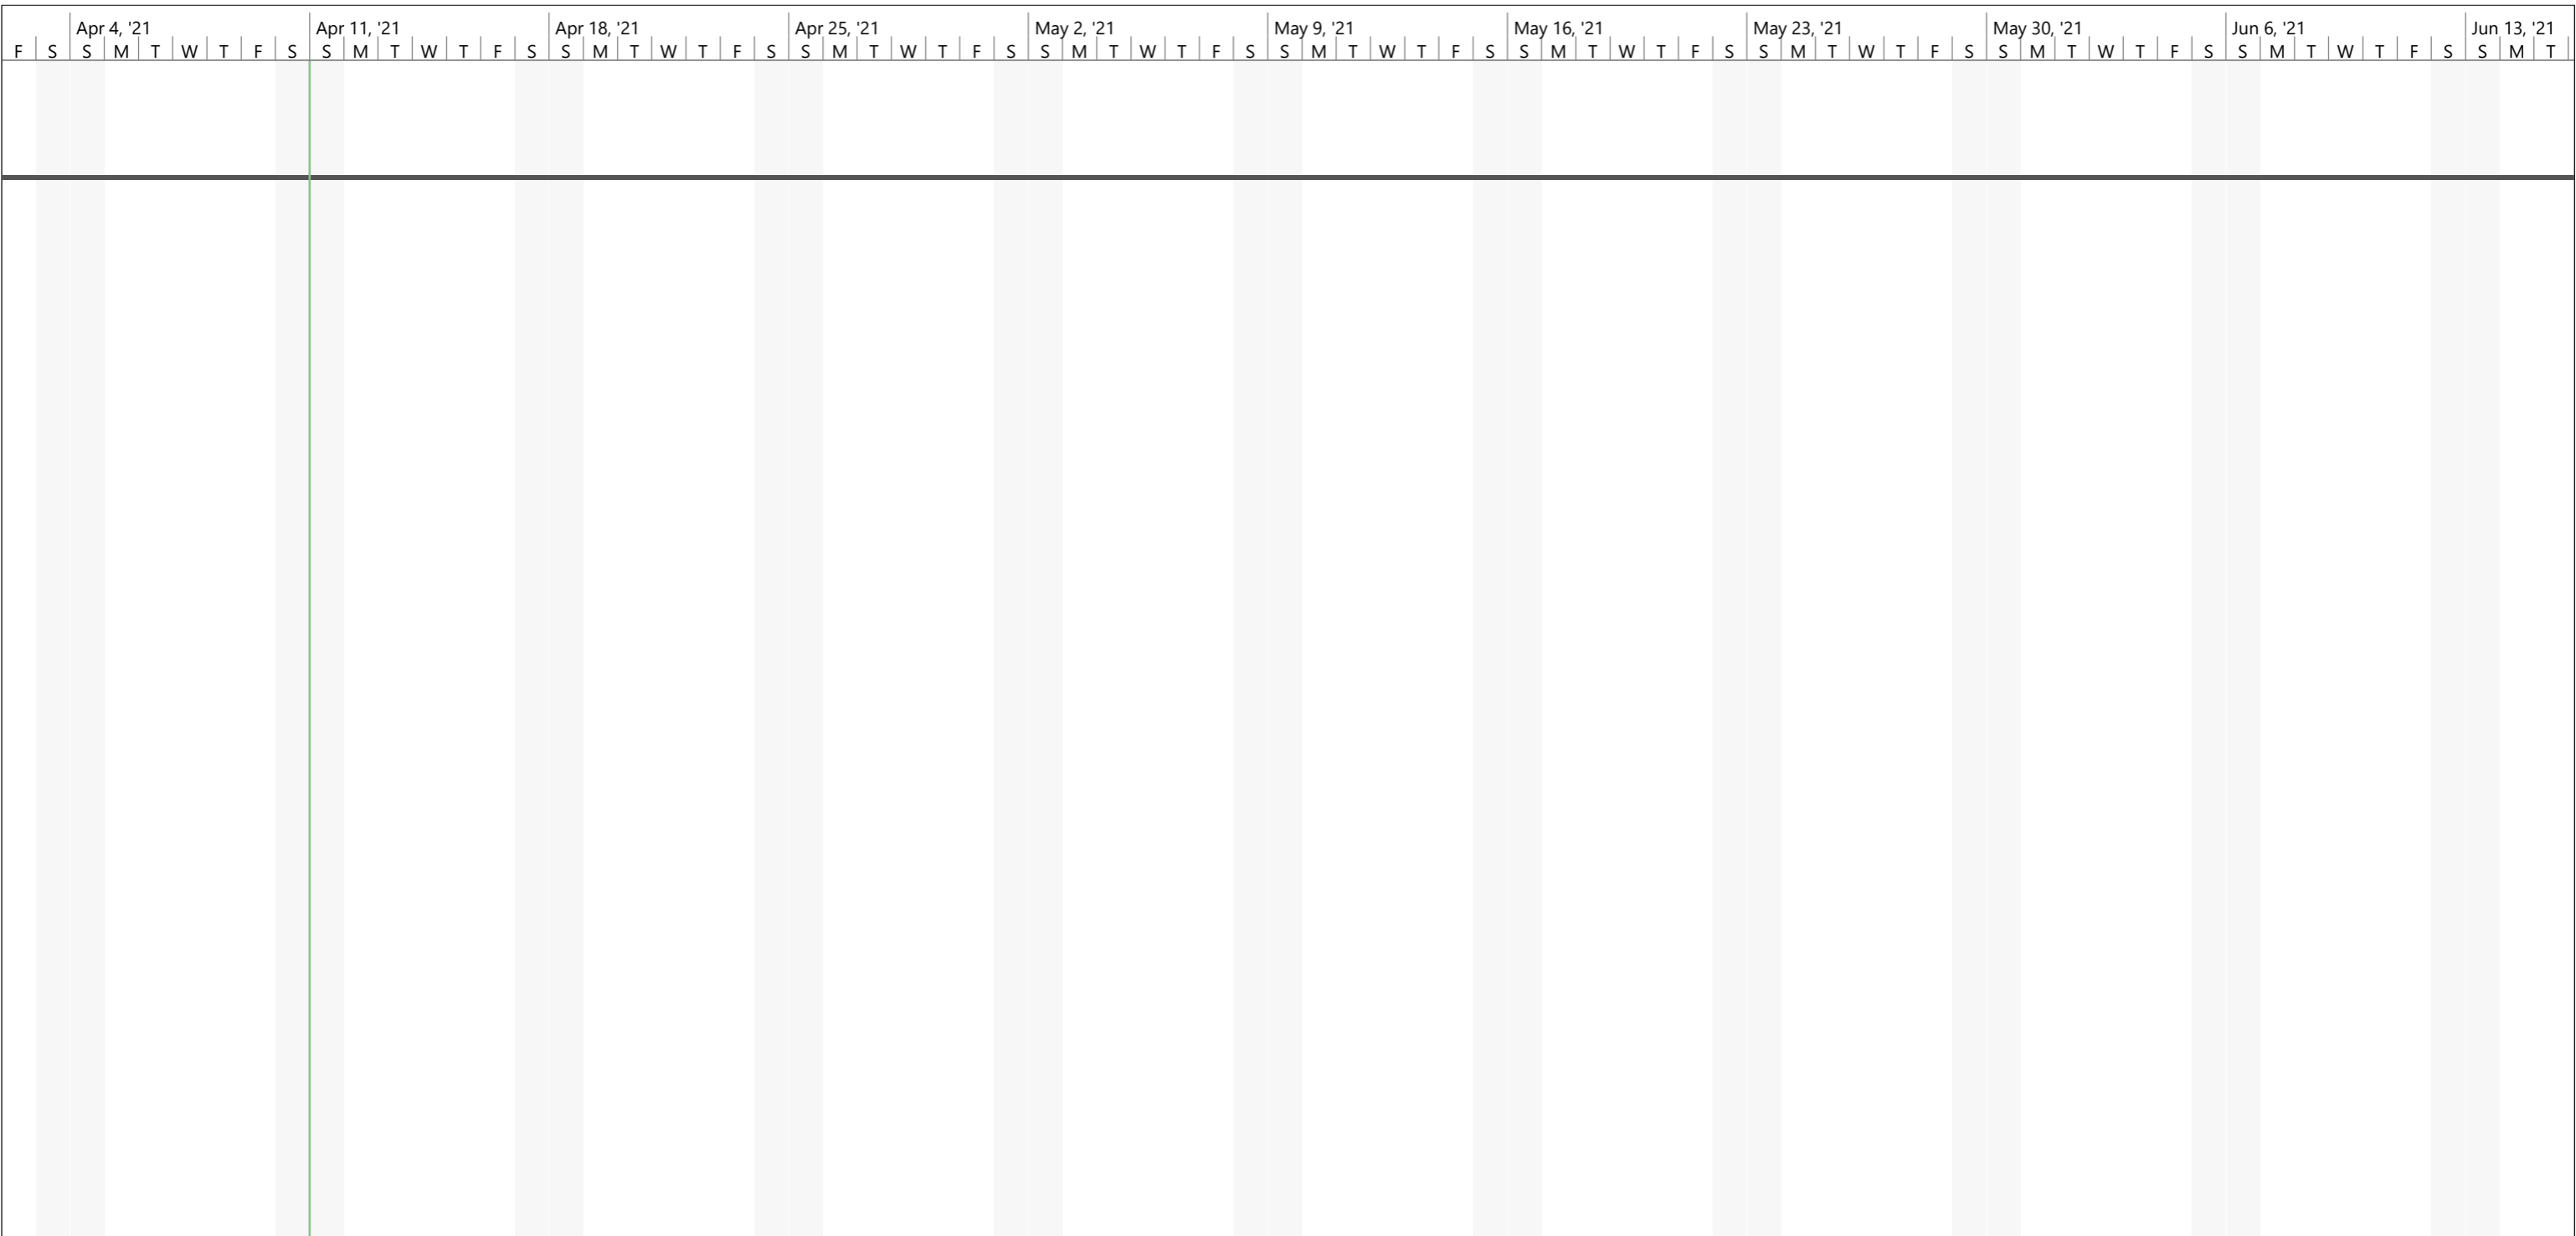


Project: Parking garage schedu
Date: Sun 4/11/21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

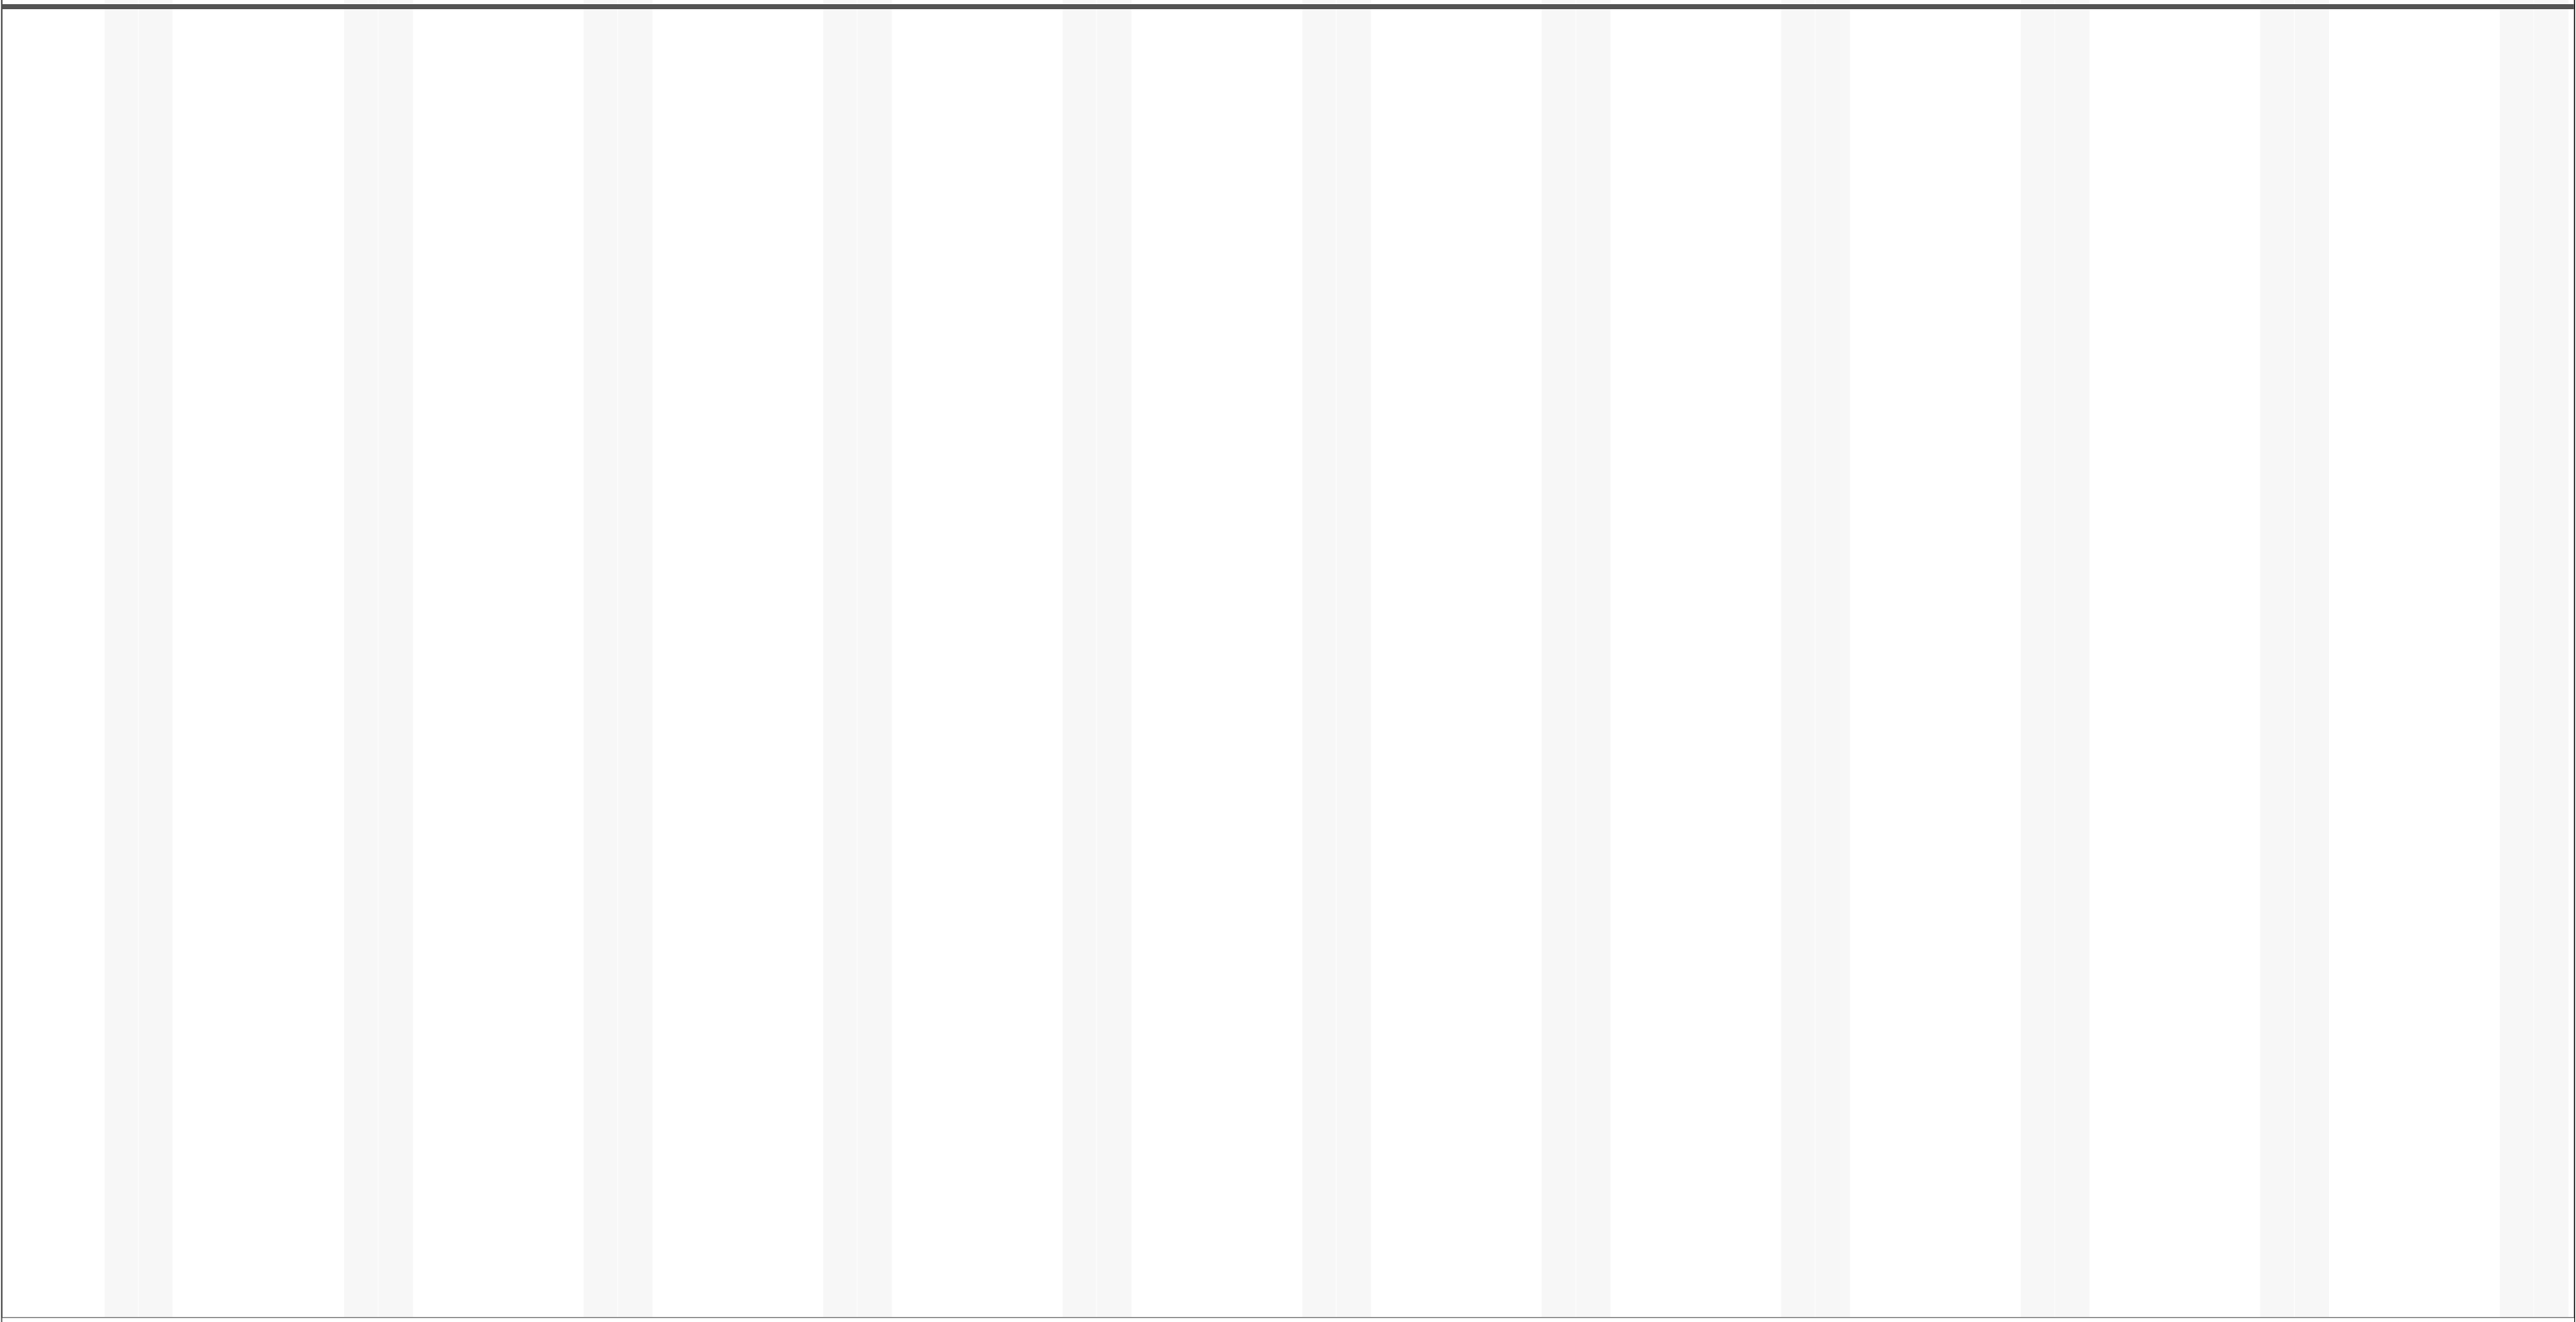


Project: Parking garage schedu Date: Sun 4/11/21	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

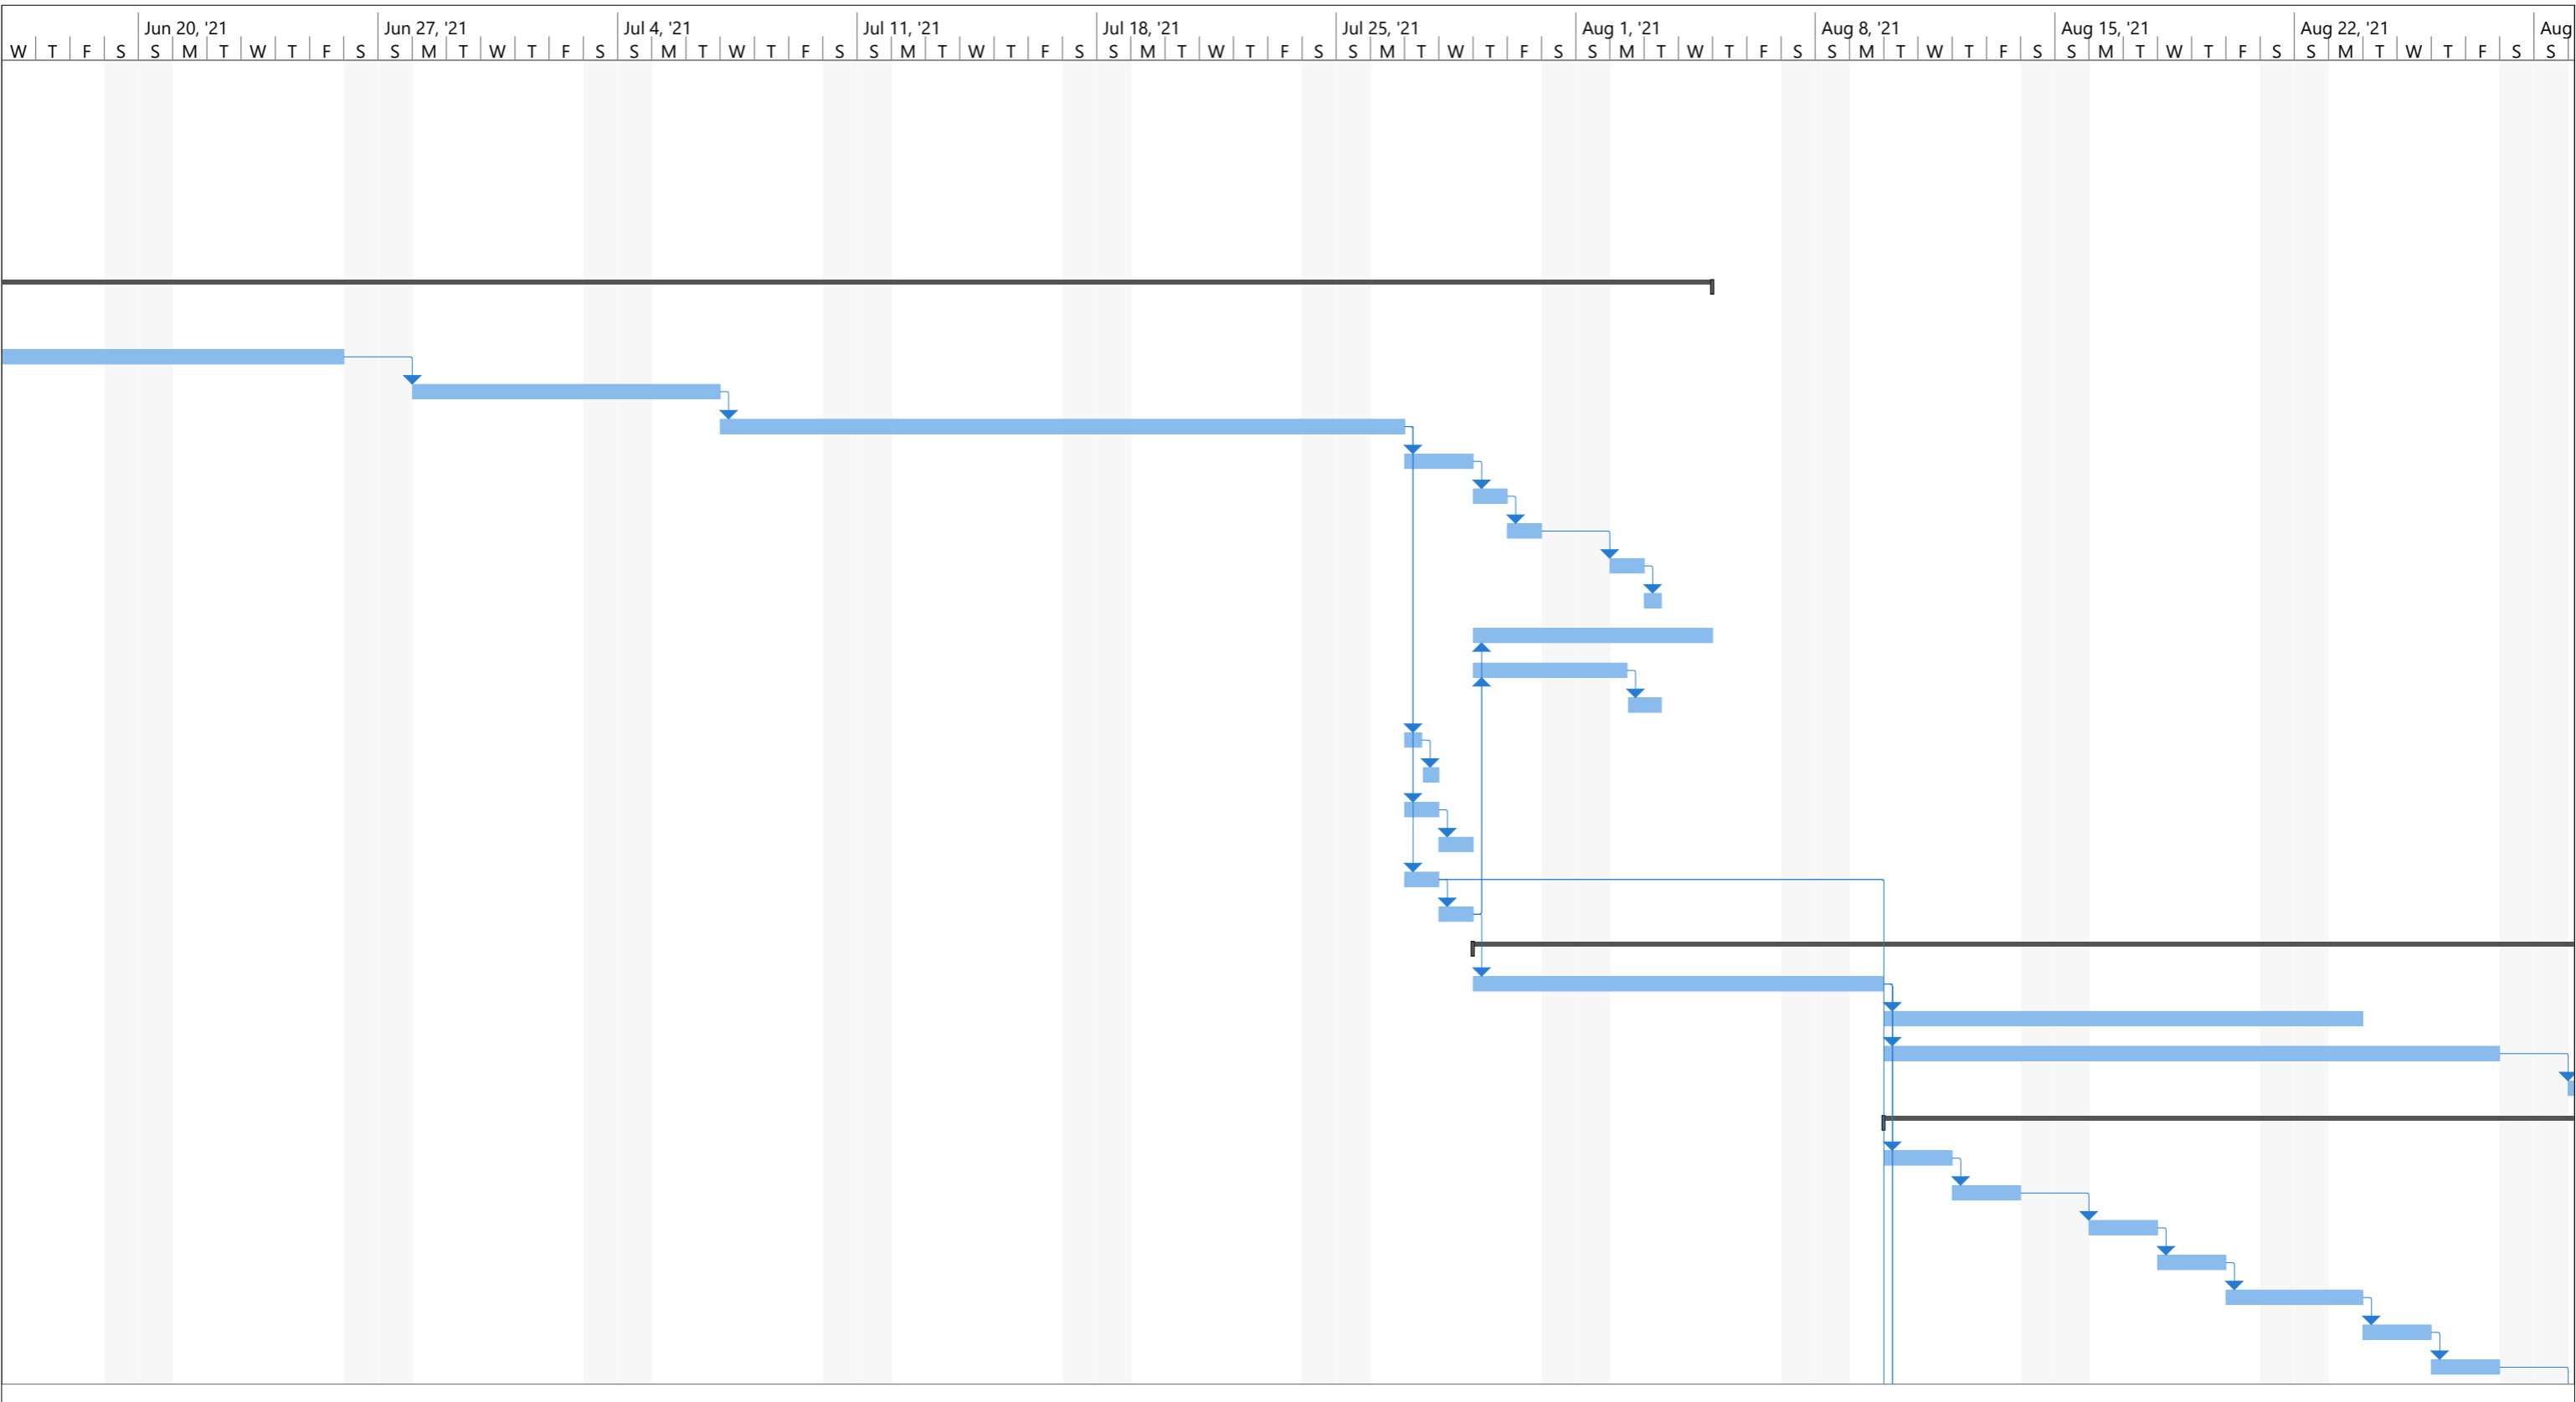


Project: Parking garage schedu
Date: Sun 4/11/21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

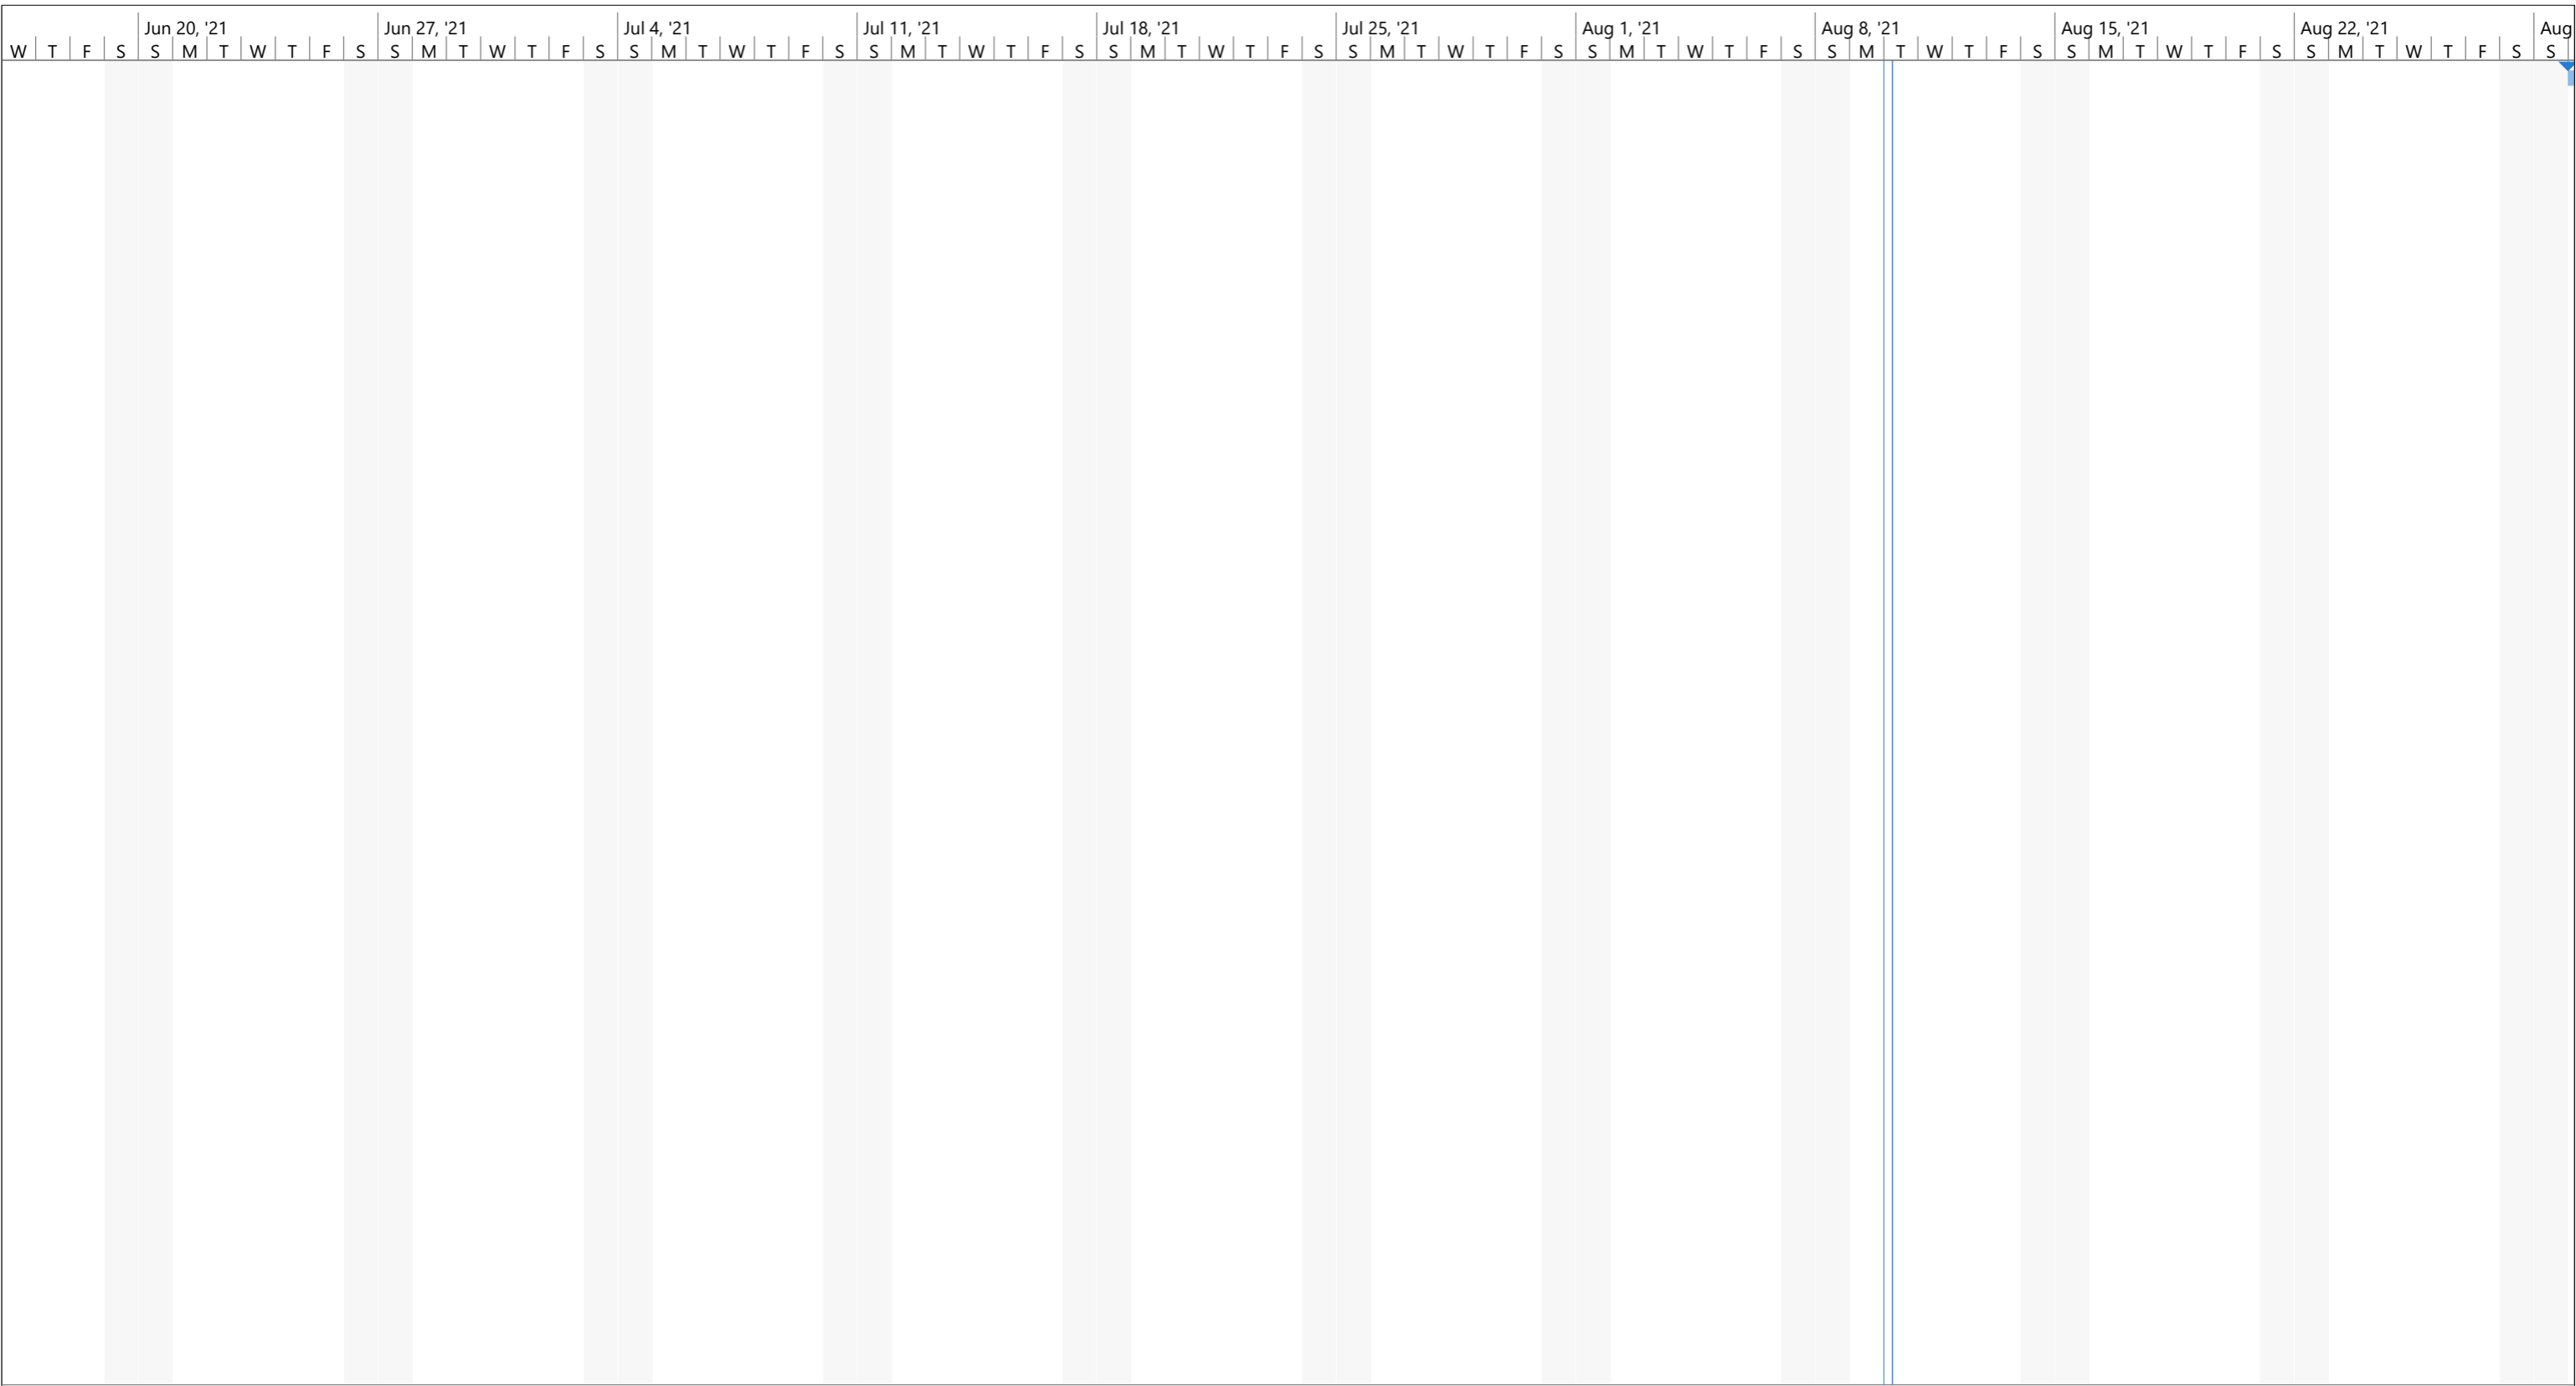


Project: Parking garage schedu
Date: Sun 4/11/21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

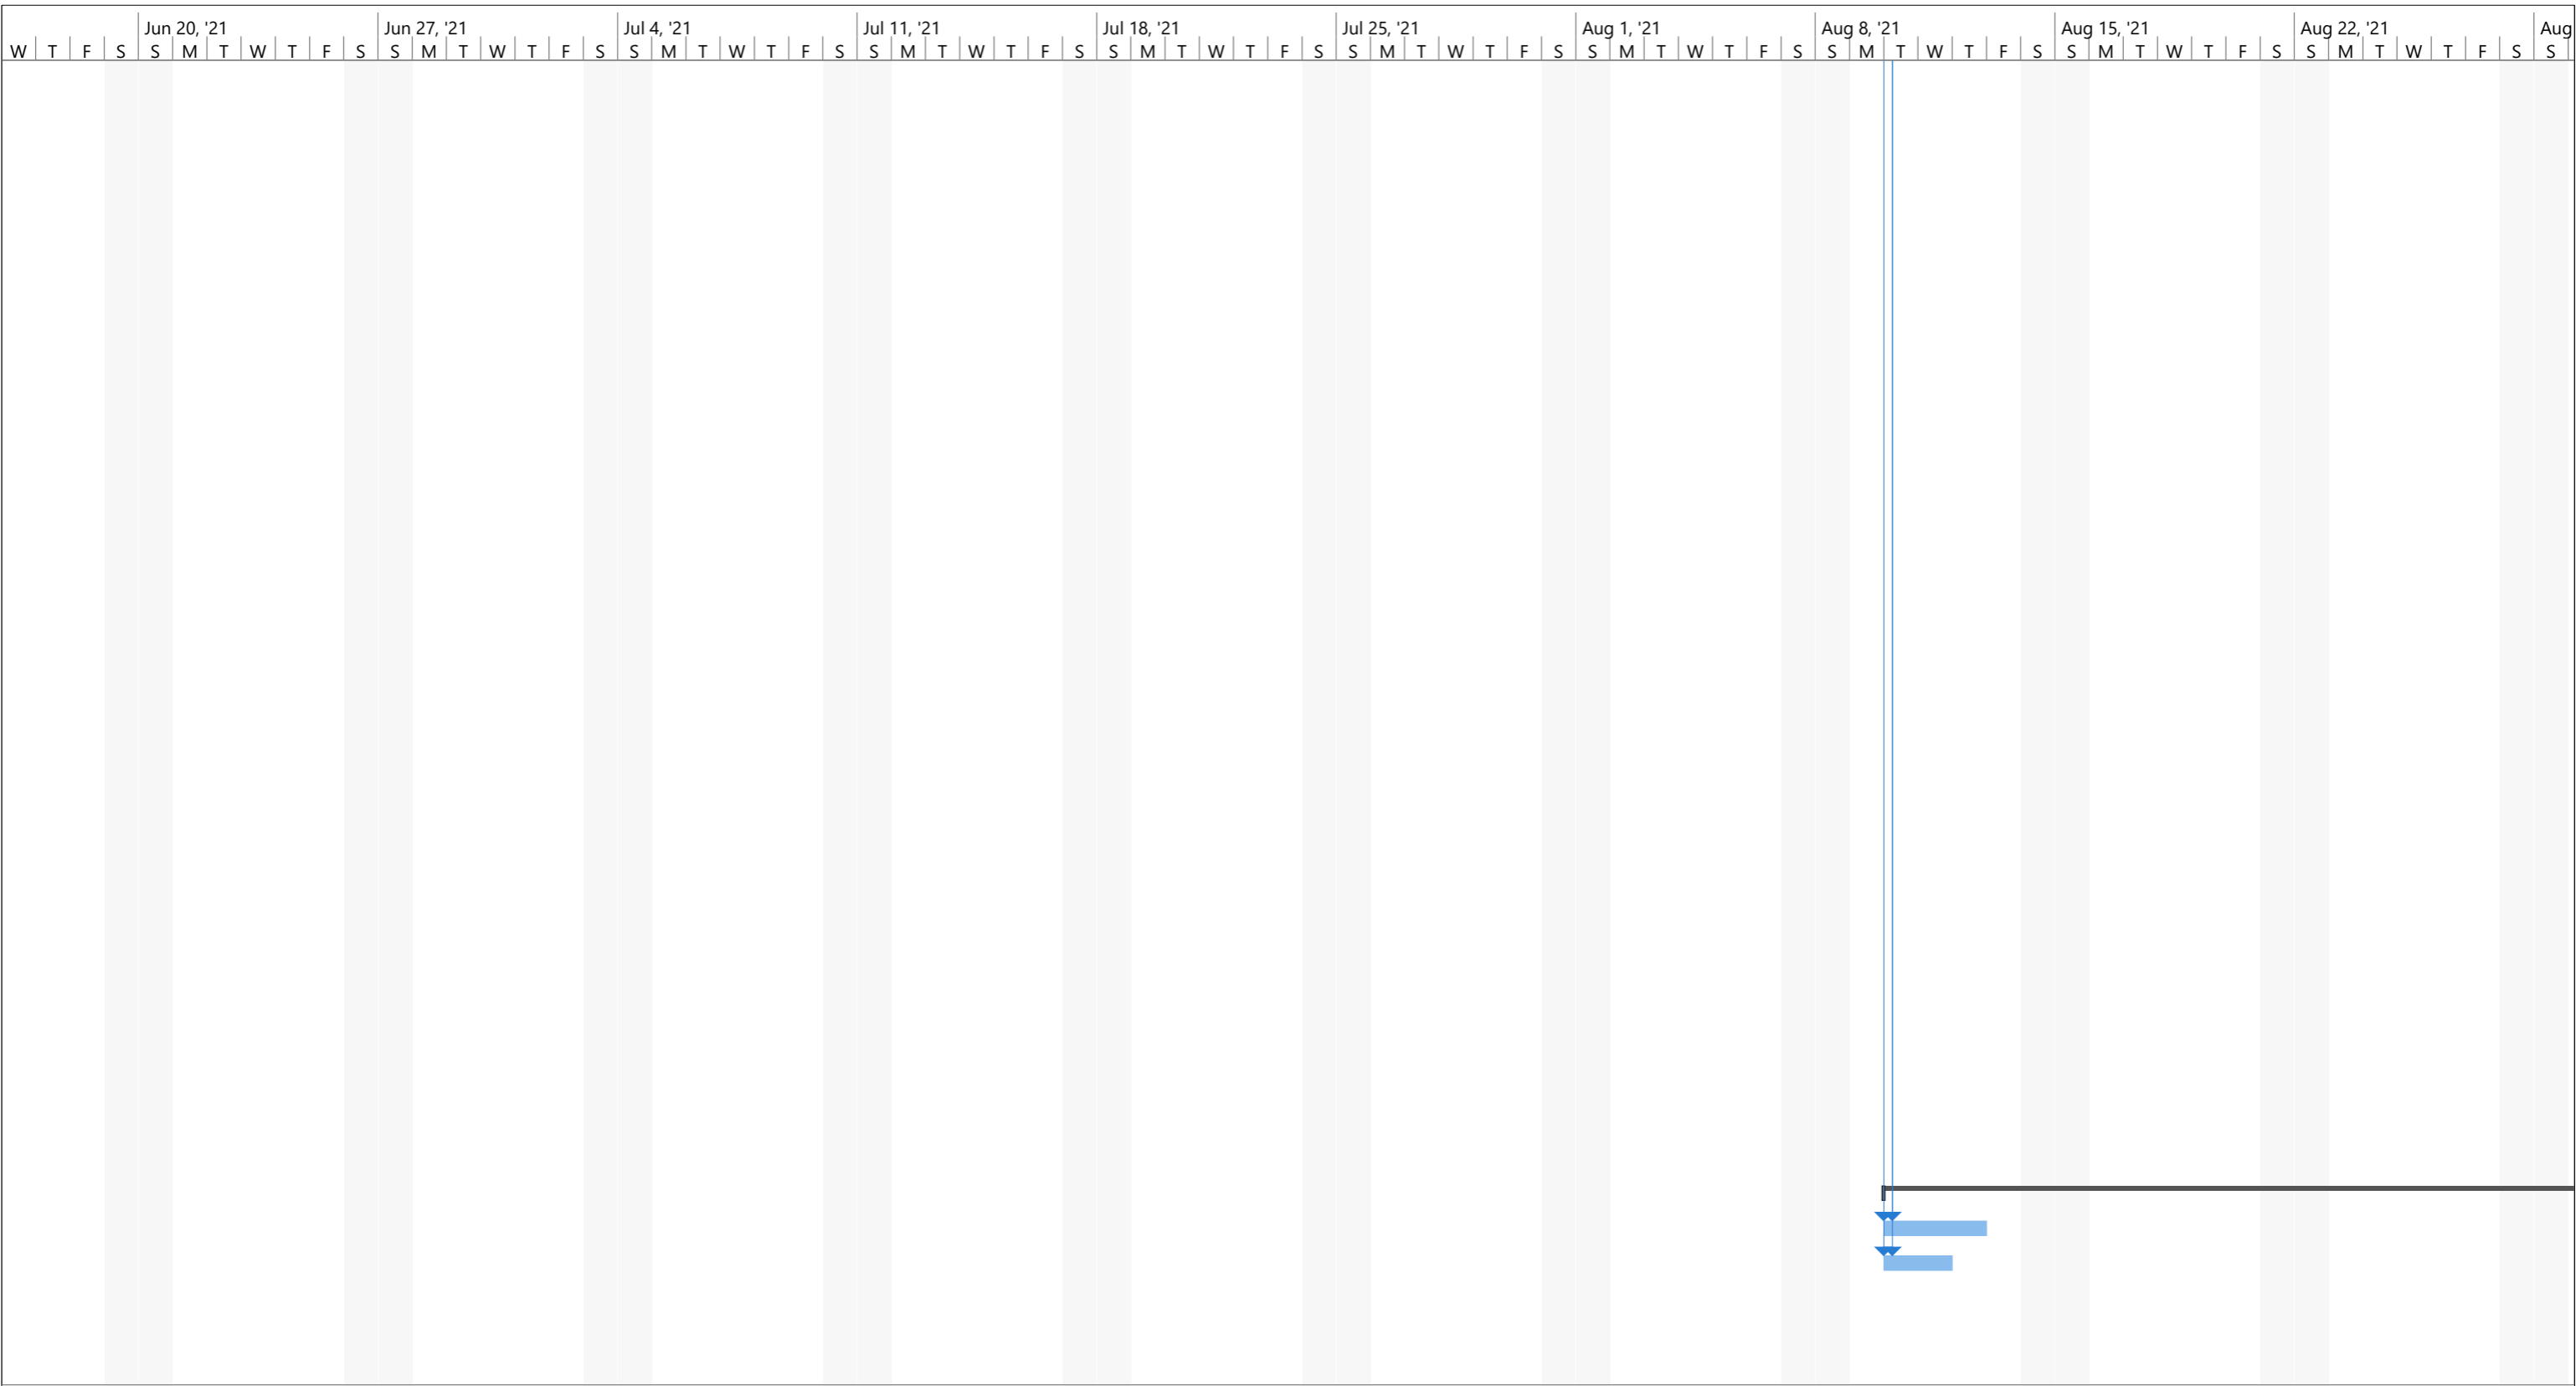


Project: Parking garage schedu
Date: Sun 4/11/21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

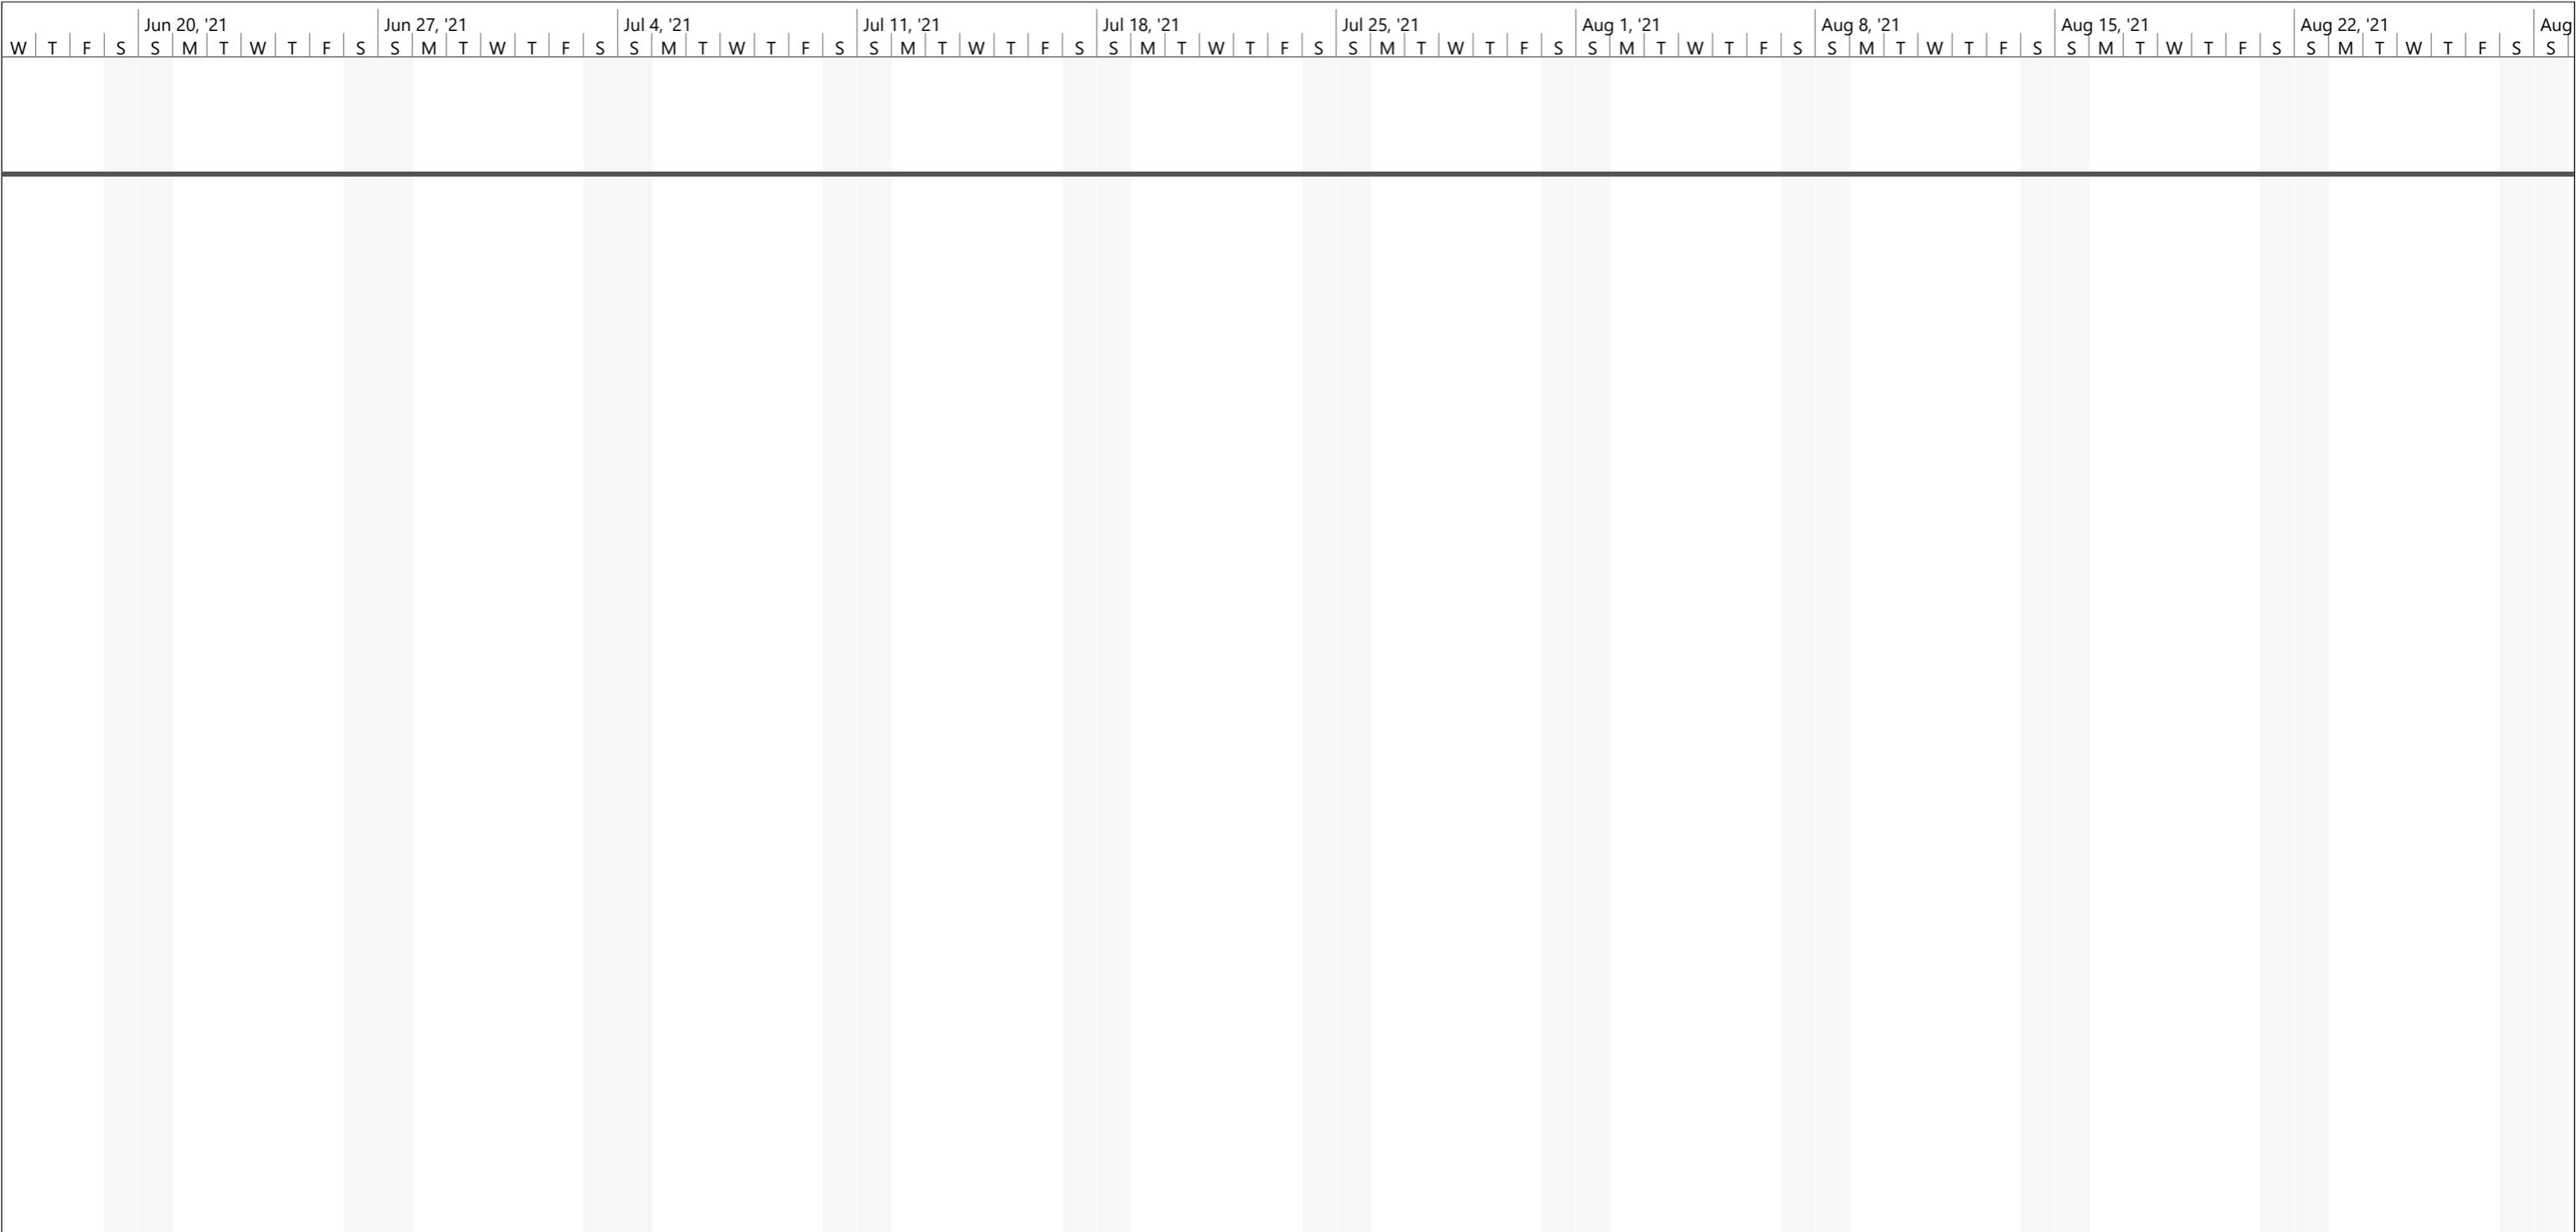

Project: Parking garage schedu
Date: Sun 4/11/21


Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

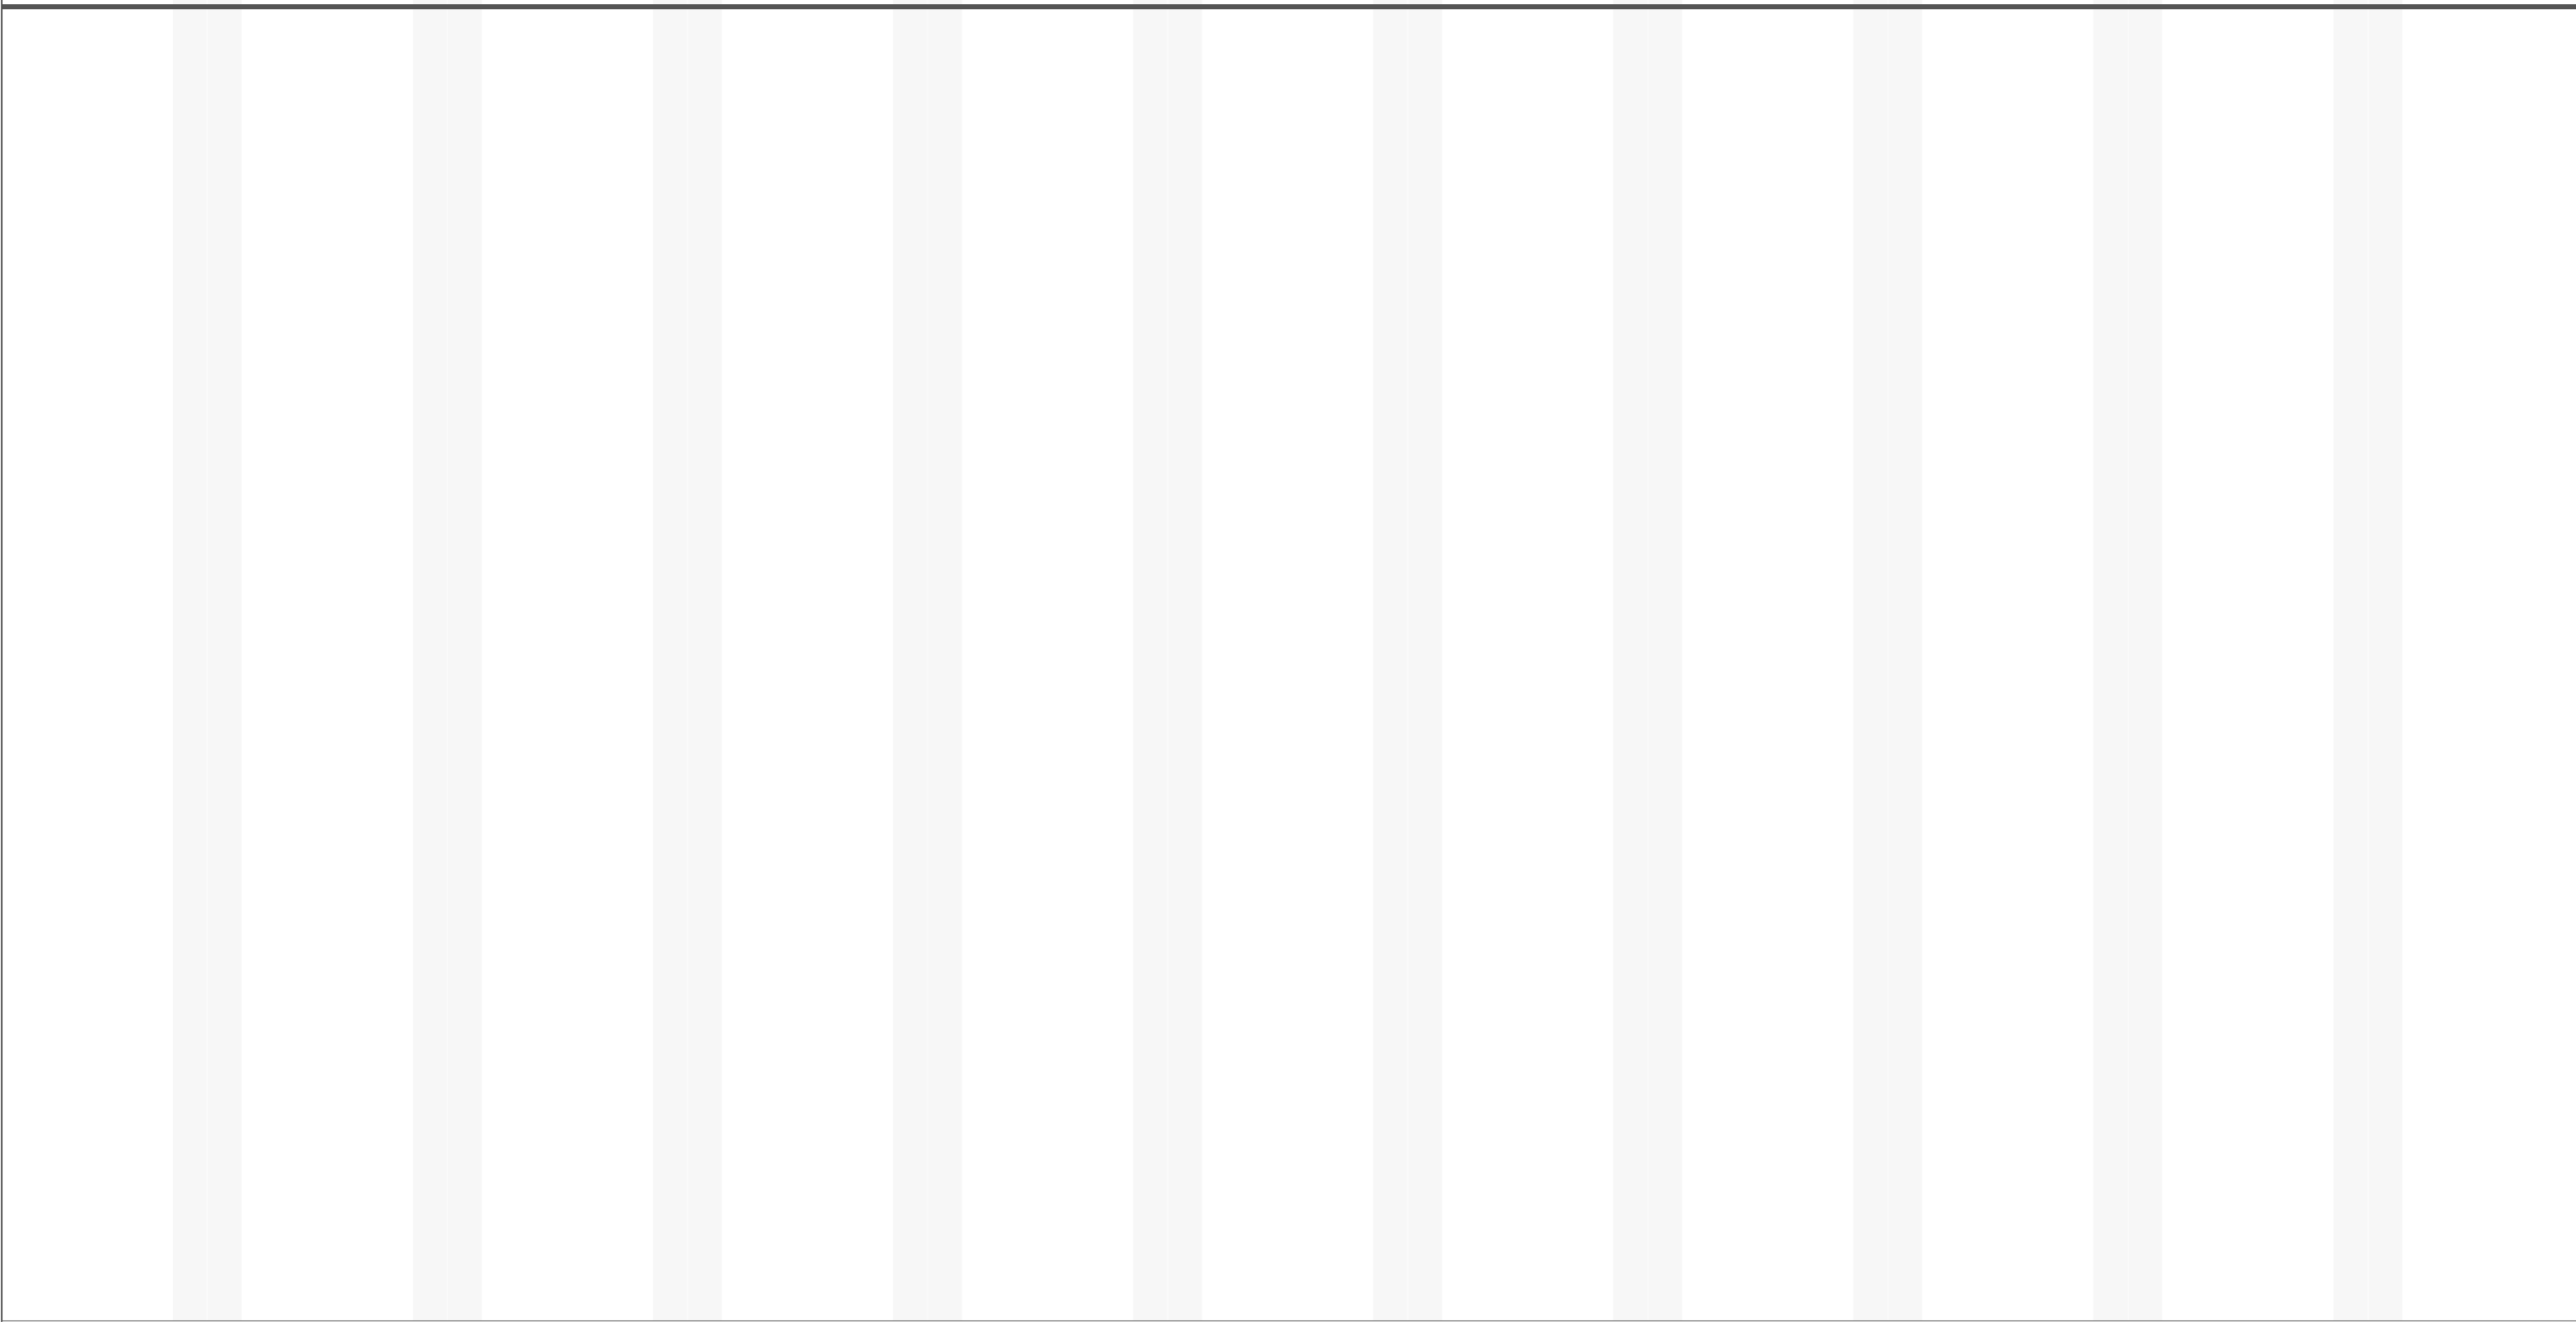


Project: Parking garage schedu
 Date: Sun 4/11/21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

29, '21 | Sep 5, '21 | Sep 12, '21 | Sep 19, '21 | Sep 26, '21 | Oct 3, '21 | Oct 10, '21 | Oct 17, '21 | Oct 24, '21 | Oct 31, '21 | Nov 7, '21
M | T | W | T | F | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S | S | M | T | W | T | F | S

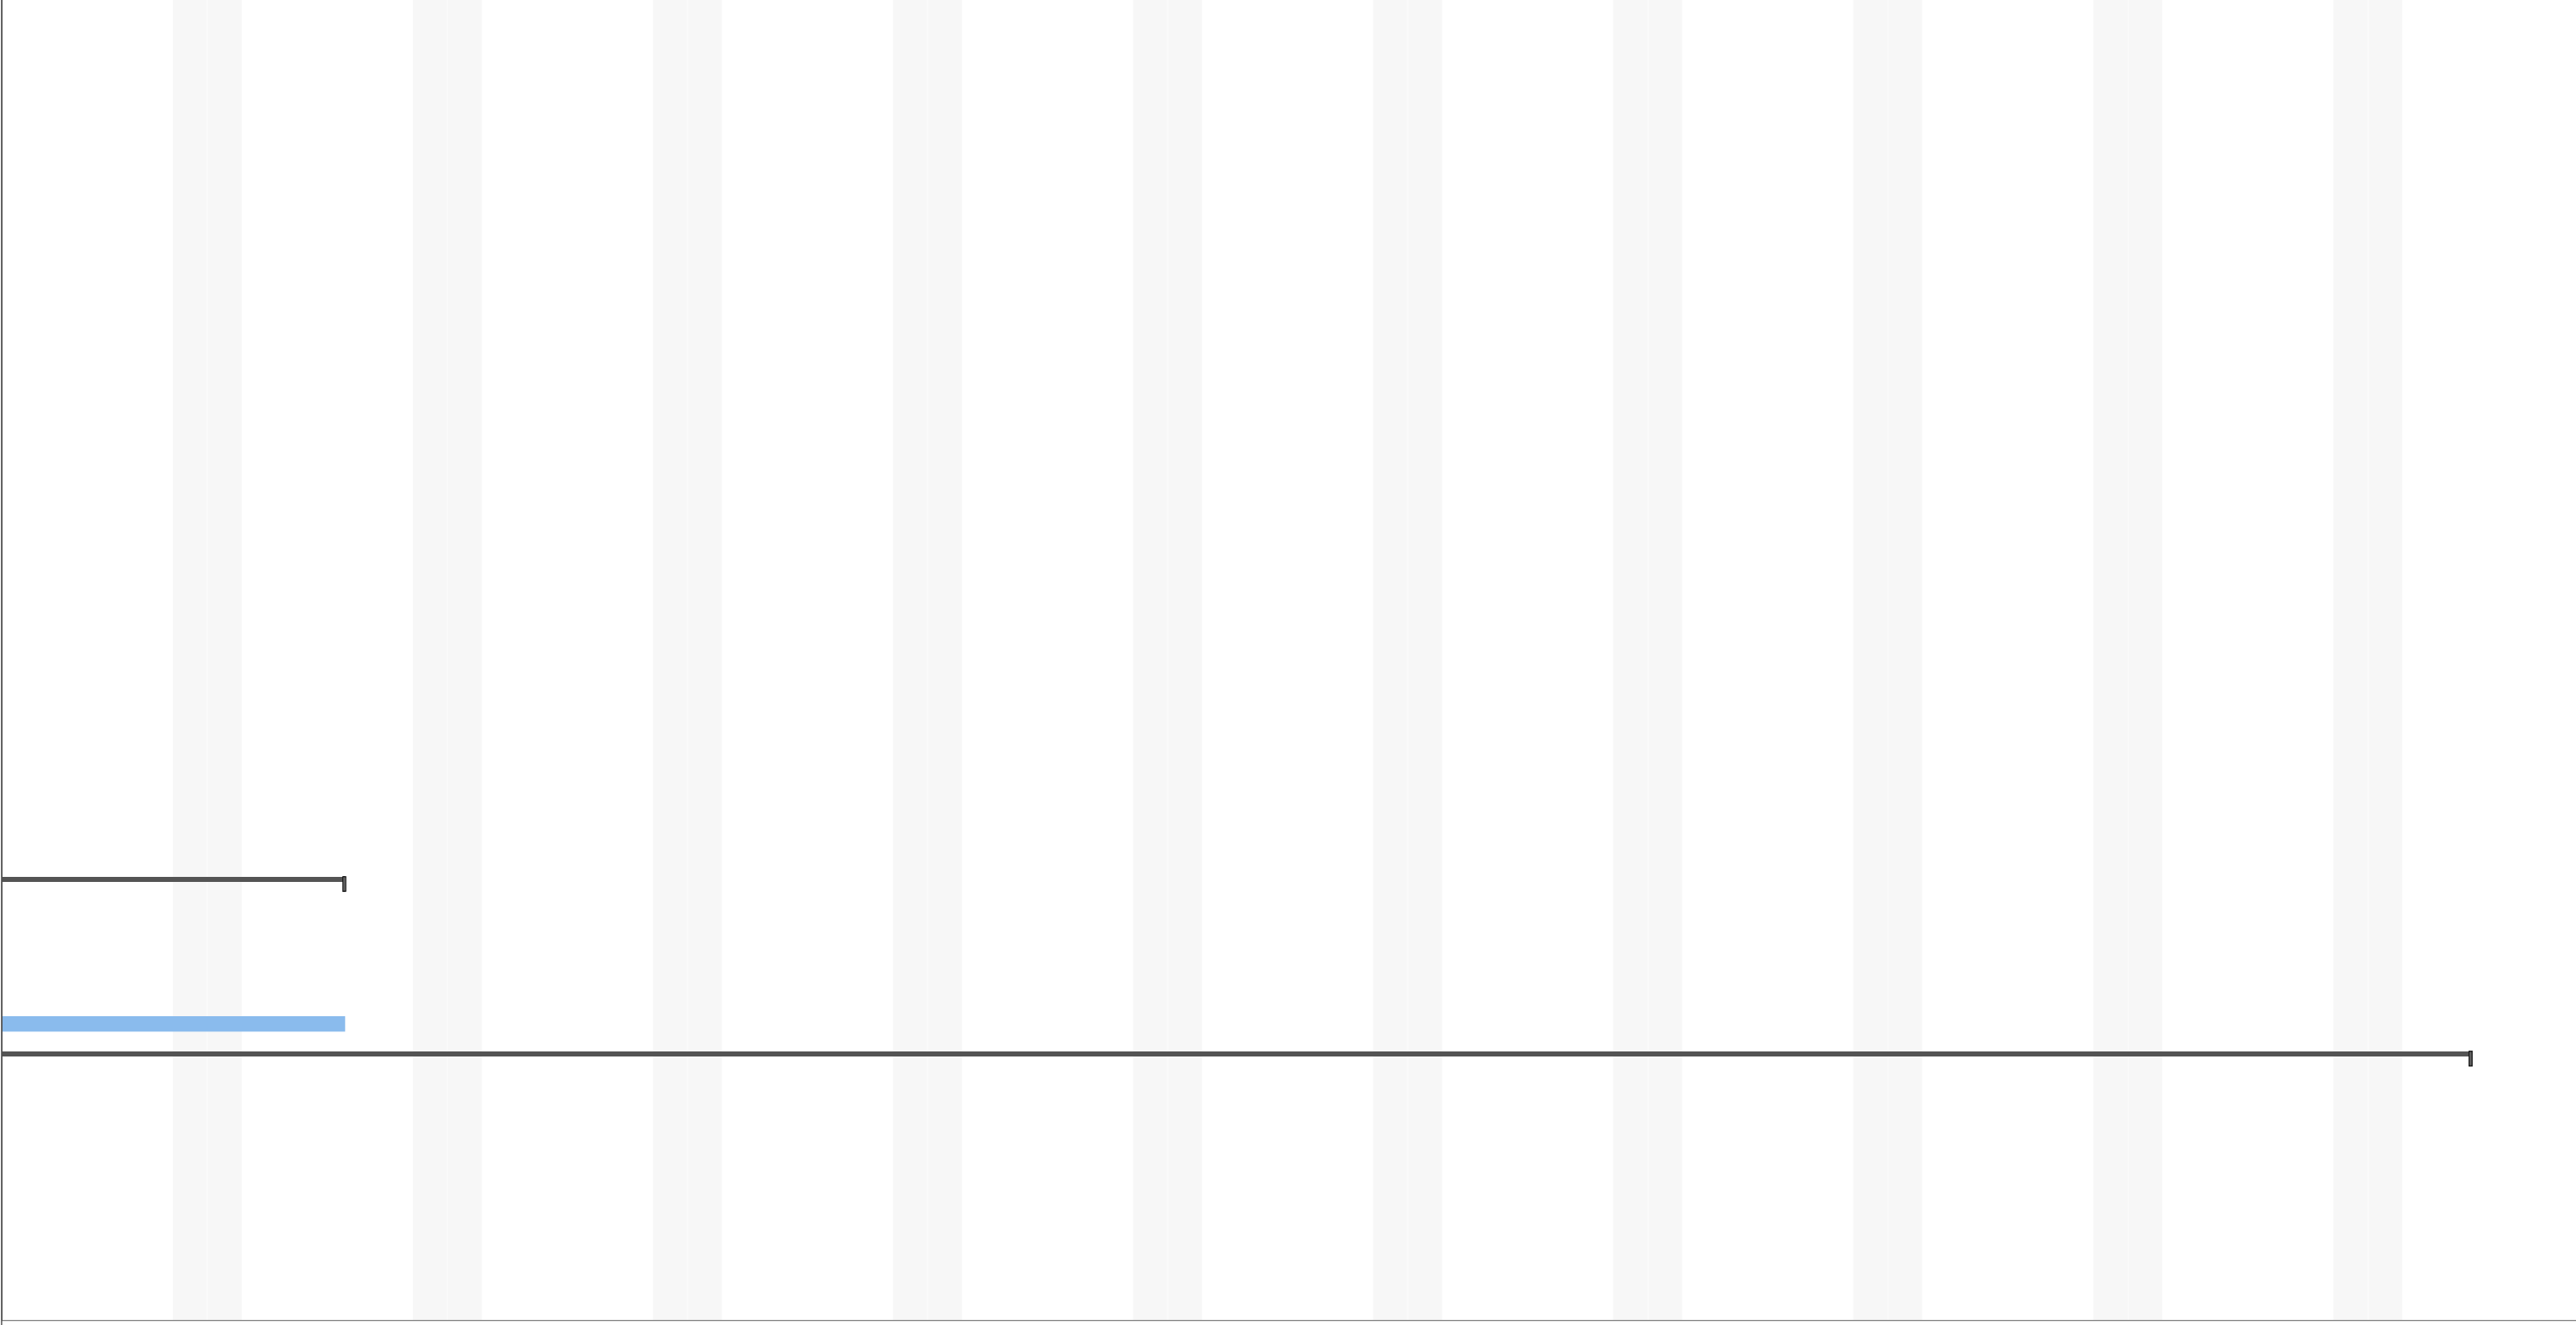



Project: Parking garage schedu Date: Sun 4/11/21	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

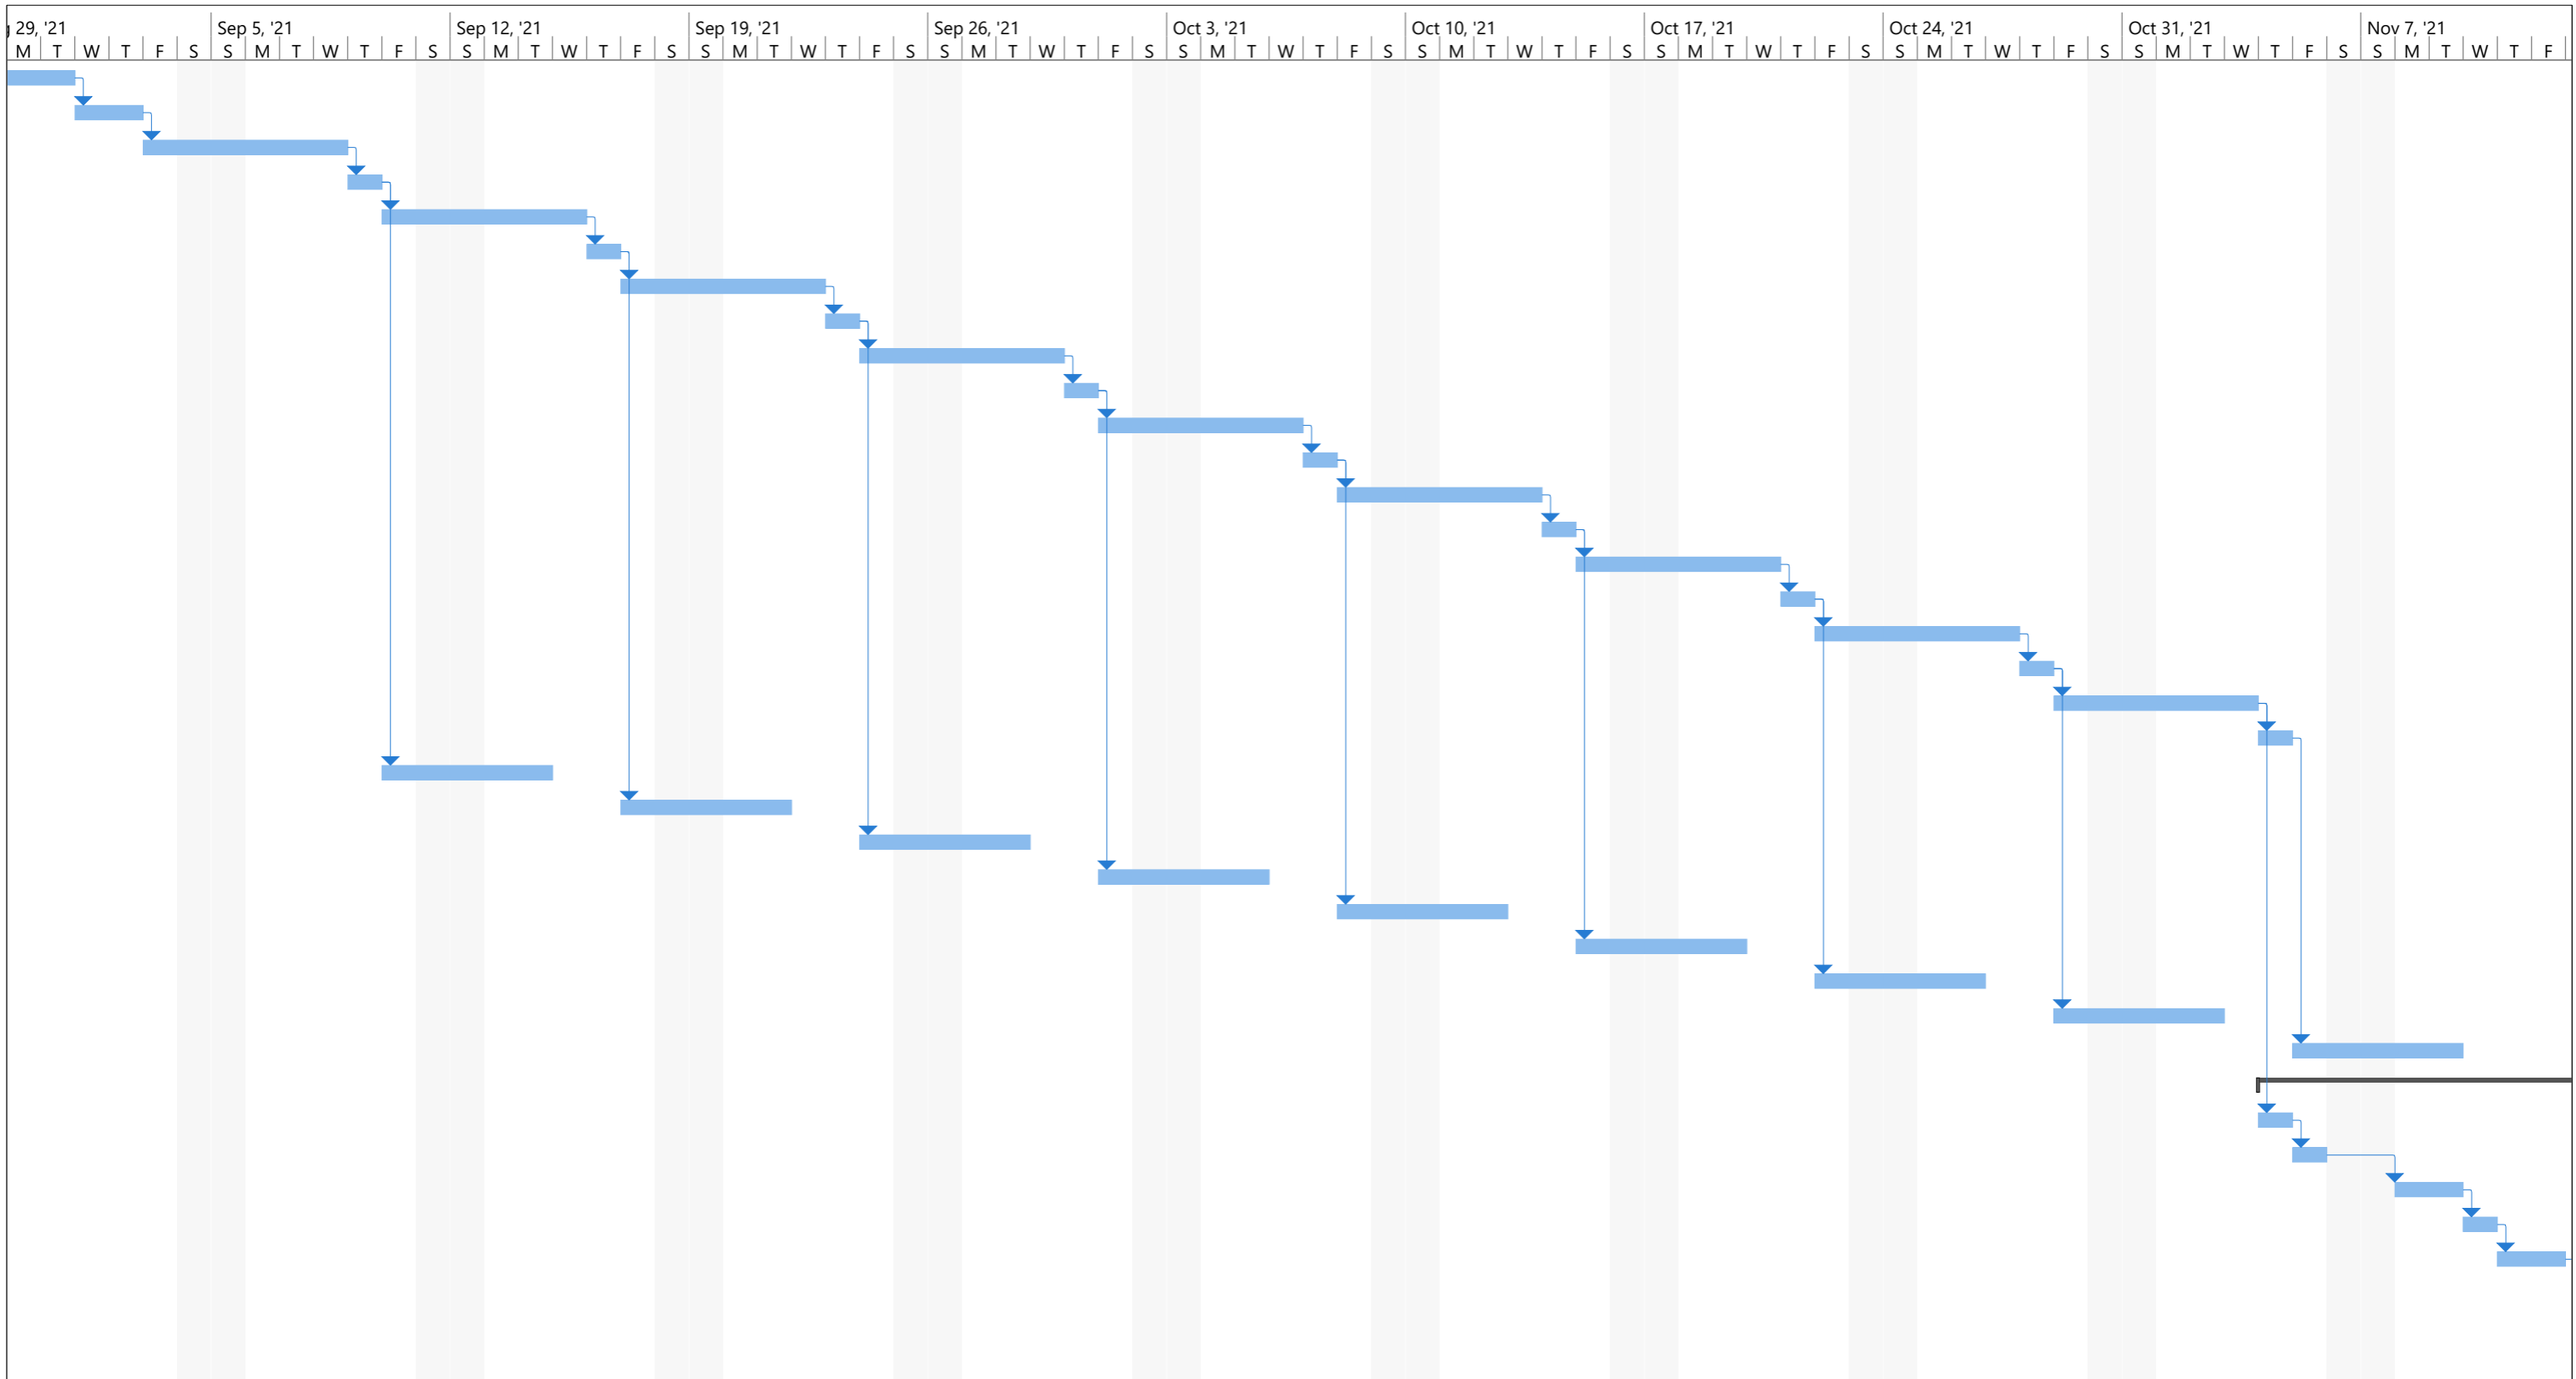

Project: Parking garage schedu
Date: Sun 4/11/21


Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

29, '21 | M | T | W | T | F | S | Sep 5, '21 | S | M | T | W | T | F | S | Sep 12, '21 | S | M | T | W | T | F | S | Sep 19, '21 | S | M | T | W | T | F | S | Sep 26, '21 | S | M | T | W | T | F | S | Oct 3, '21 | S | M | T | W | T | F | S | Oct 10, '21 | S | M | T | W | T | F | S | Oct 17, '21 | S | M | T | W | T | F | S | Oct 24, '21 | S | M | T | W | T | F | S | Oct 31, '21 | S | M | T | W | T | F | S | Nov 7, '21 | S | M | T | W | T | F | S

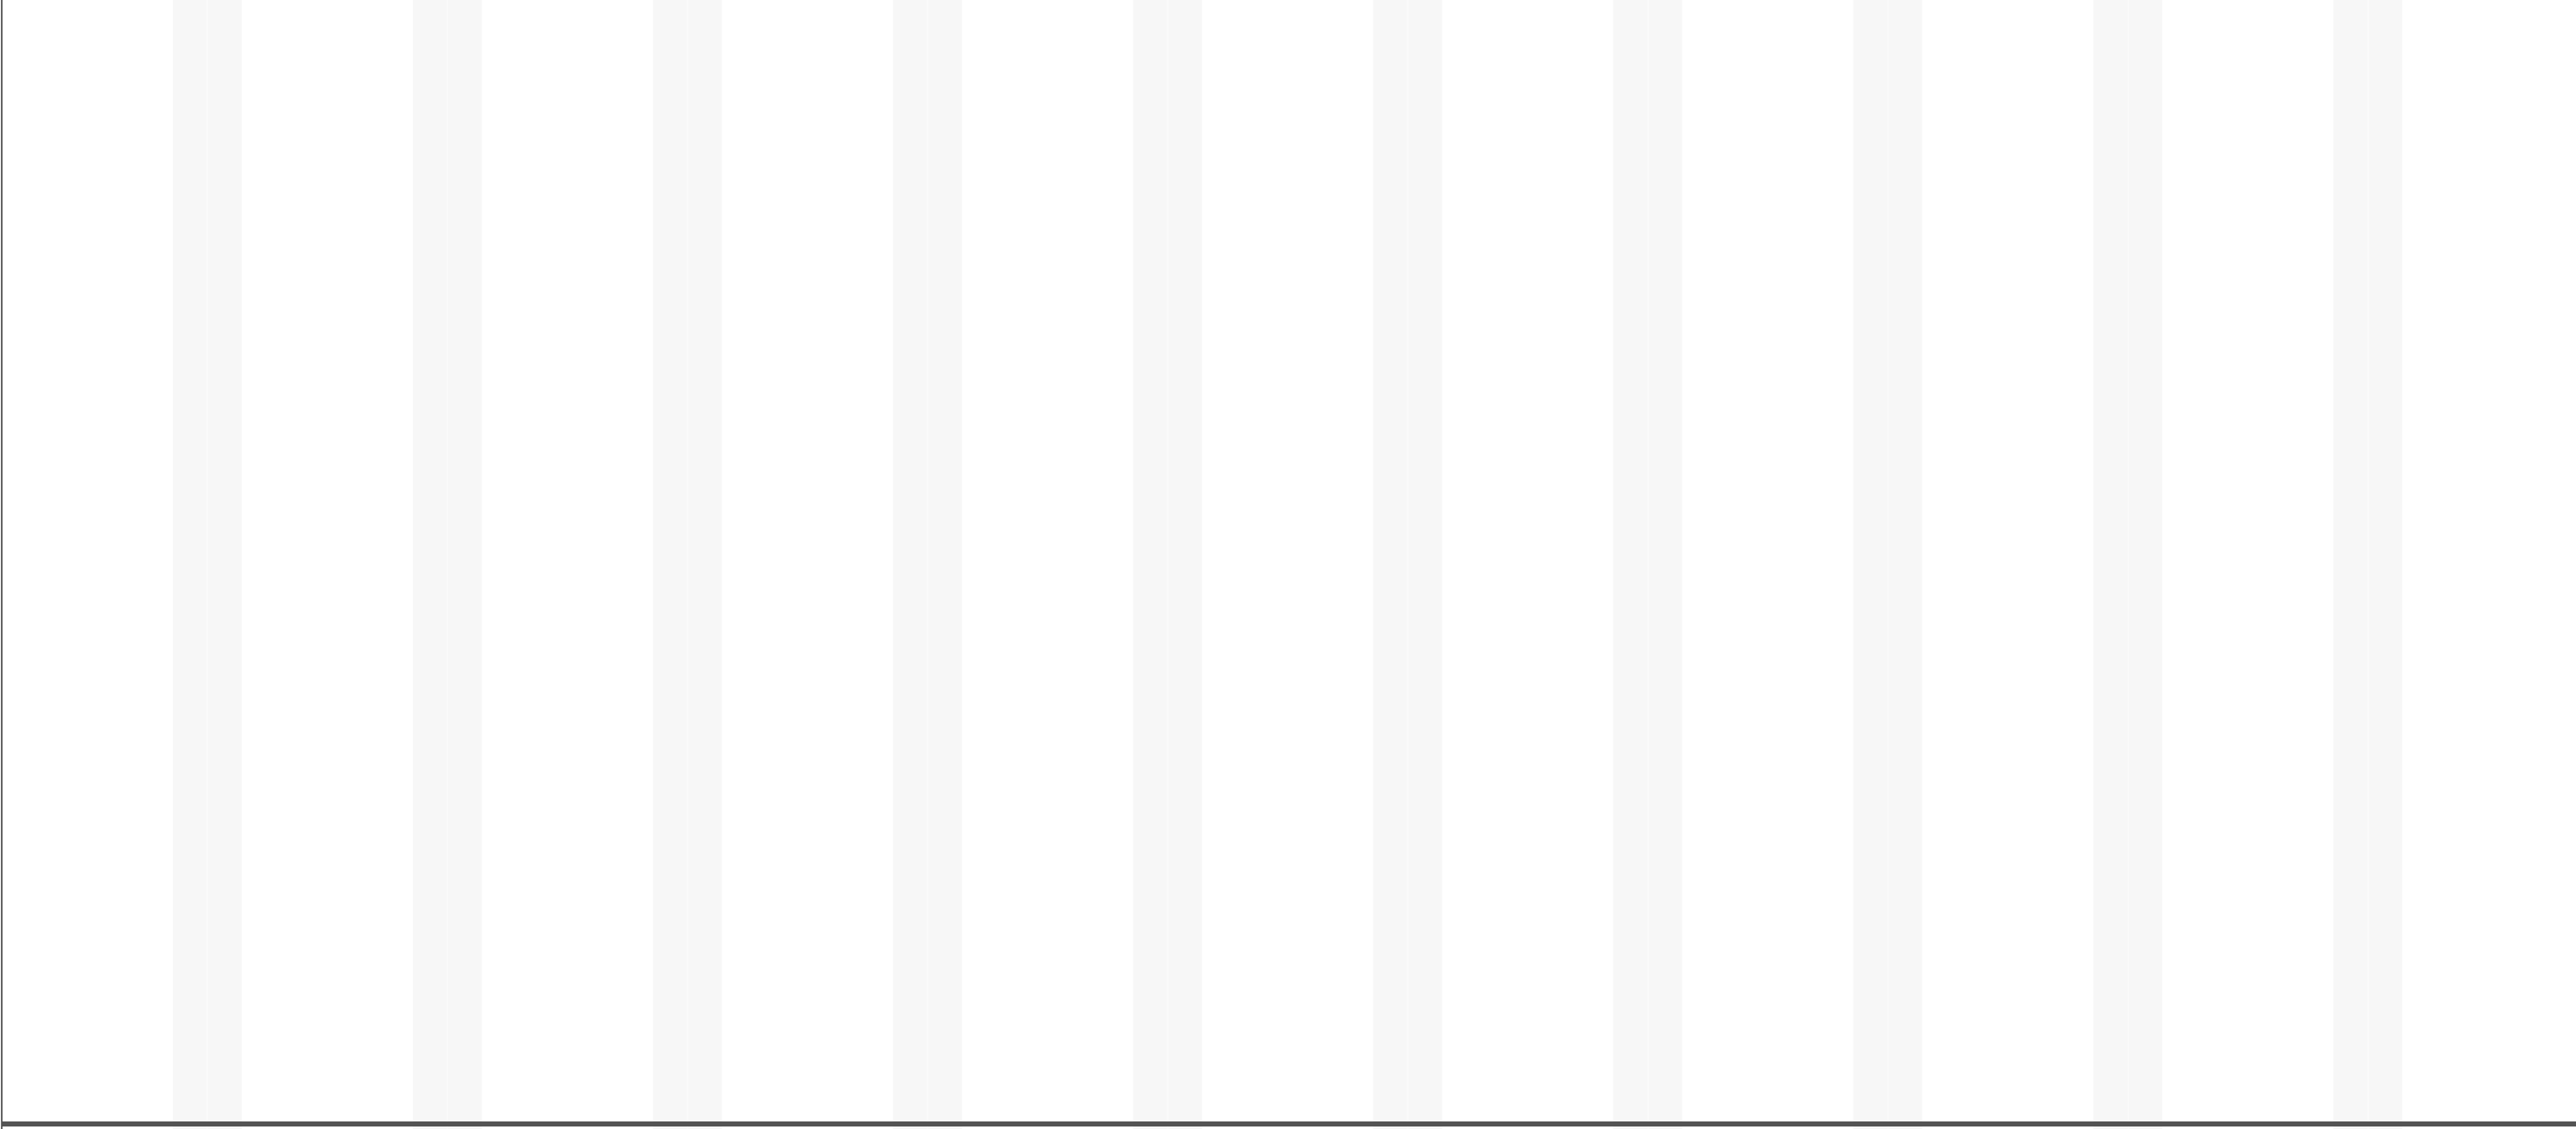


Project: Parking garage schedu Date: Sun 4/11/21	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

29, '21 | M | T | W | T | F | S | Sep 5, '21 | S | M | T | W | T | F | S | Sep 12, '21 | S | M | T | W | T | F | S | Sep 19, '21 | S | M | T | W | T | F | S | Sep 26, '21 | S | M | T | W | T | F | S | Oct 3, '21 | S | M | T | W | T | F | S | Oct 10, '21 | S | M | T | W | T | F | S | Oct 17, '21 | S | M | T | W | T | F | S | Oct 24, '21 | S | M | T | W | T | F | S | Oct 31, '21 | S | M | T | W | T | F | S | Nov 7, '21 | S | M | T | W | T | F | S

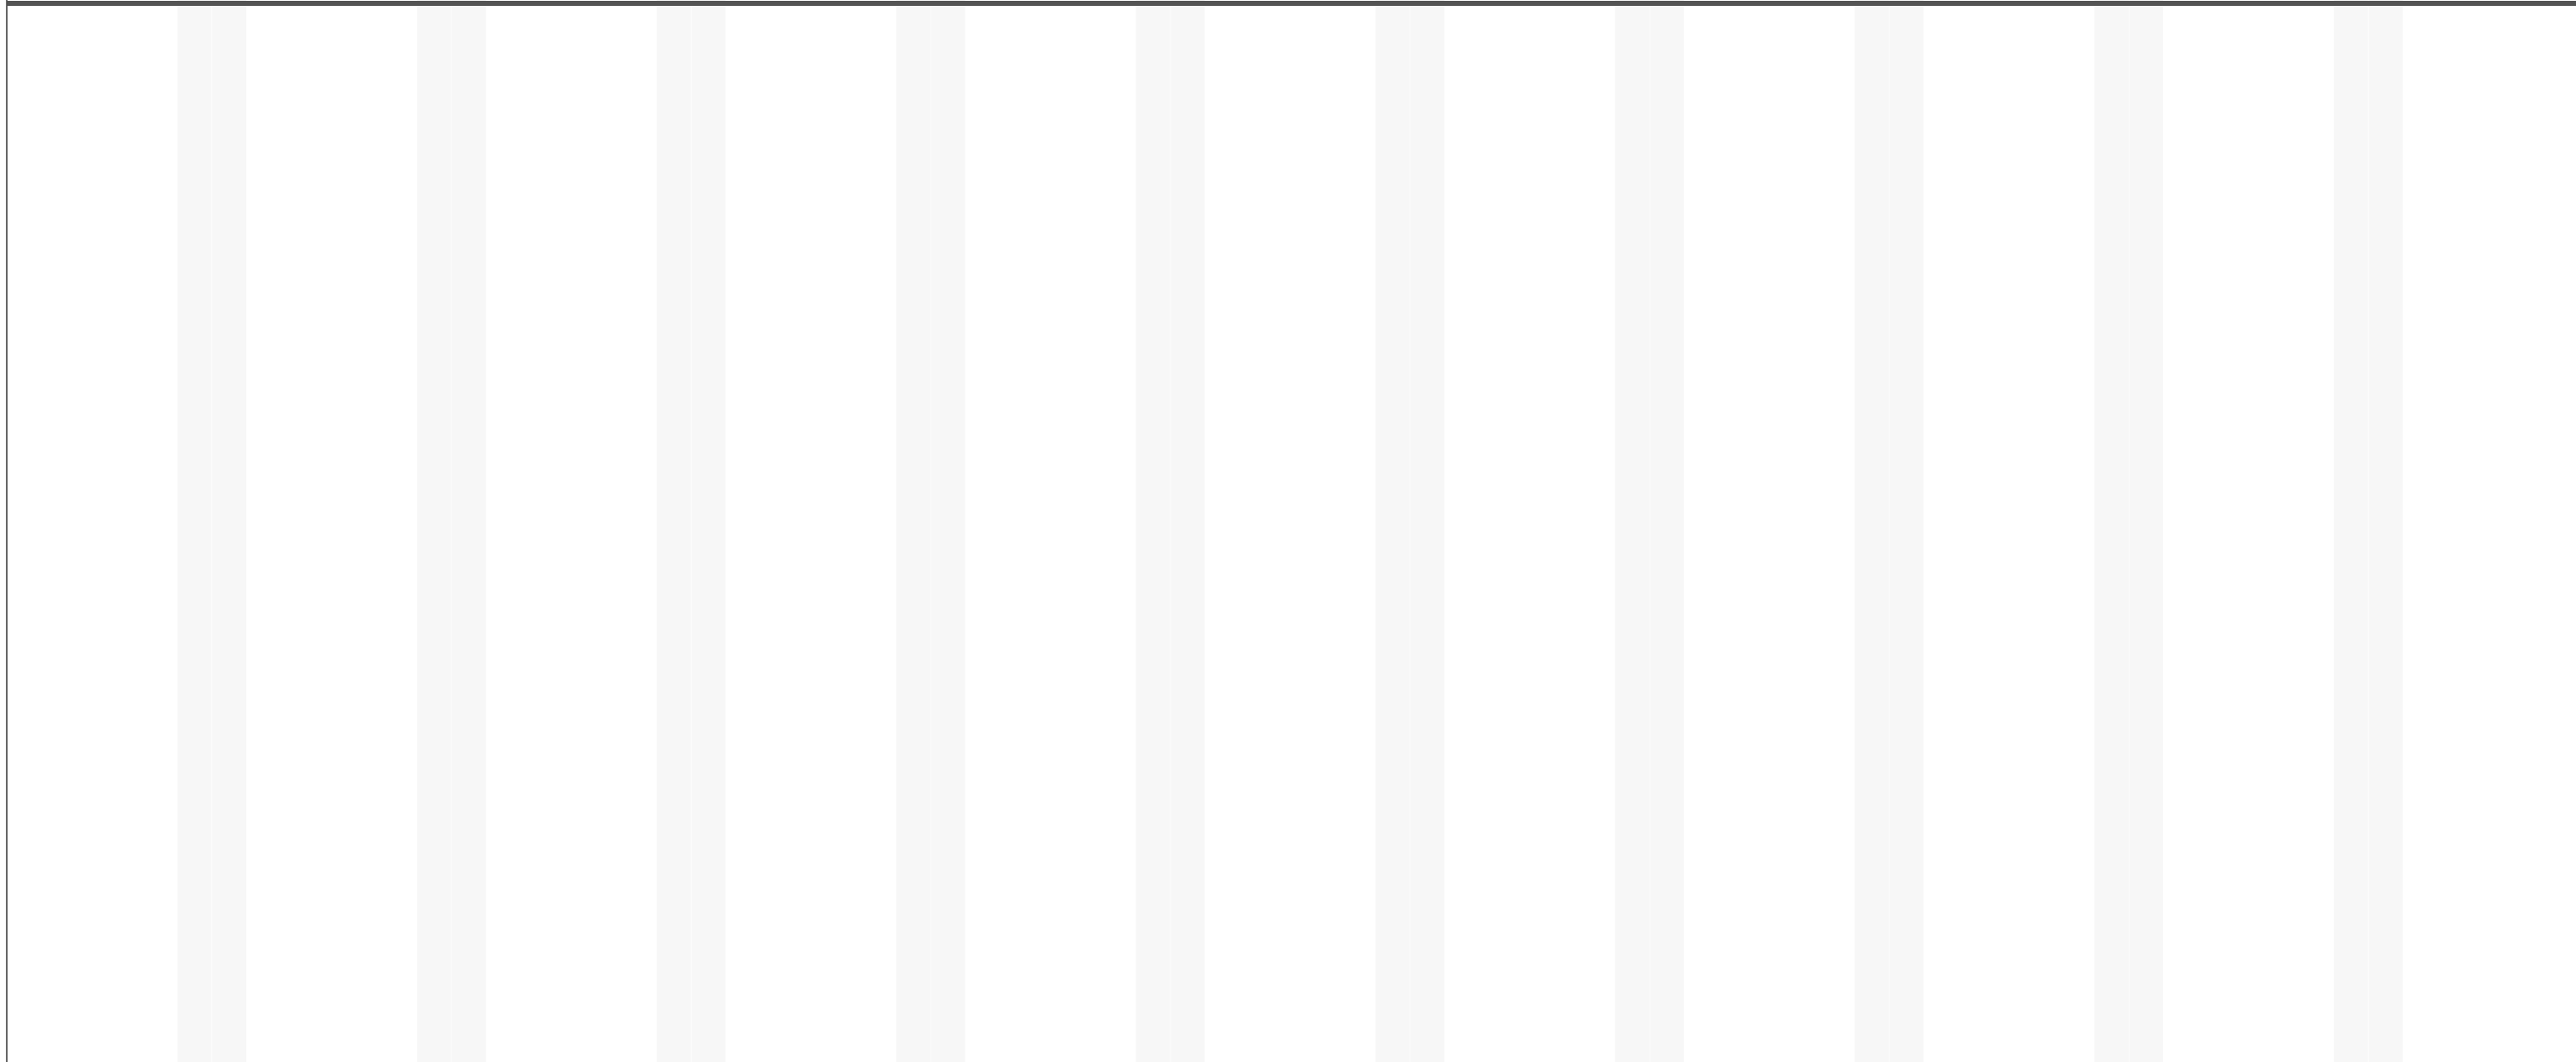


Project: Parking garage schedu
Date: Sun 4/11/21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

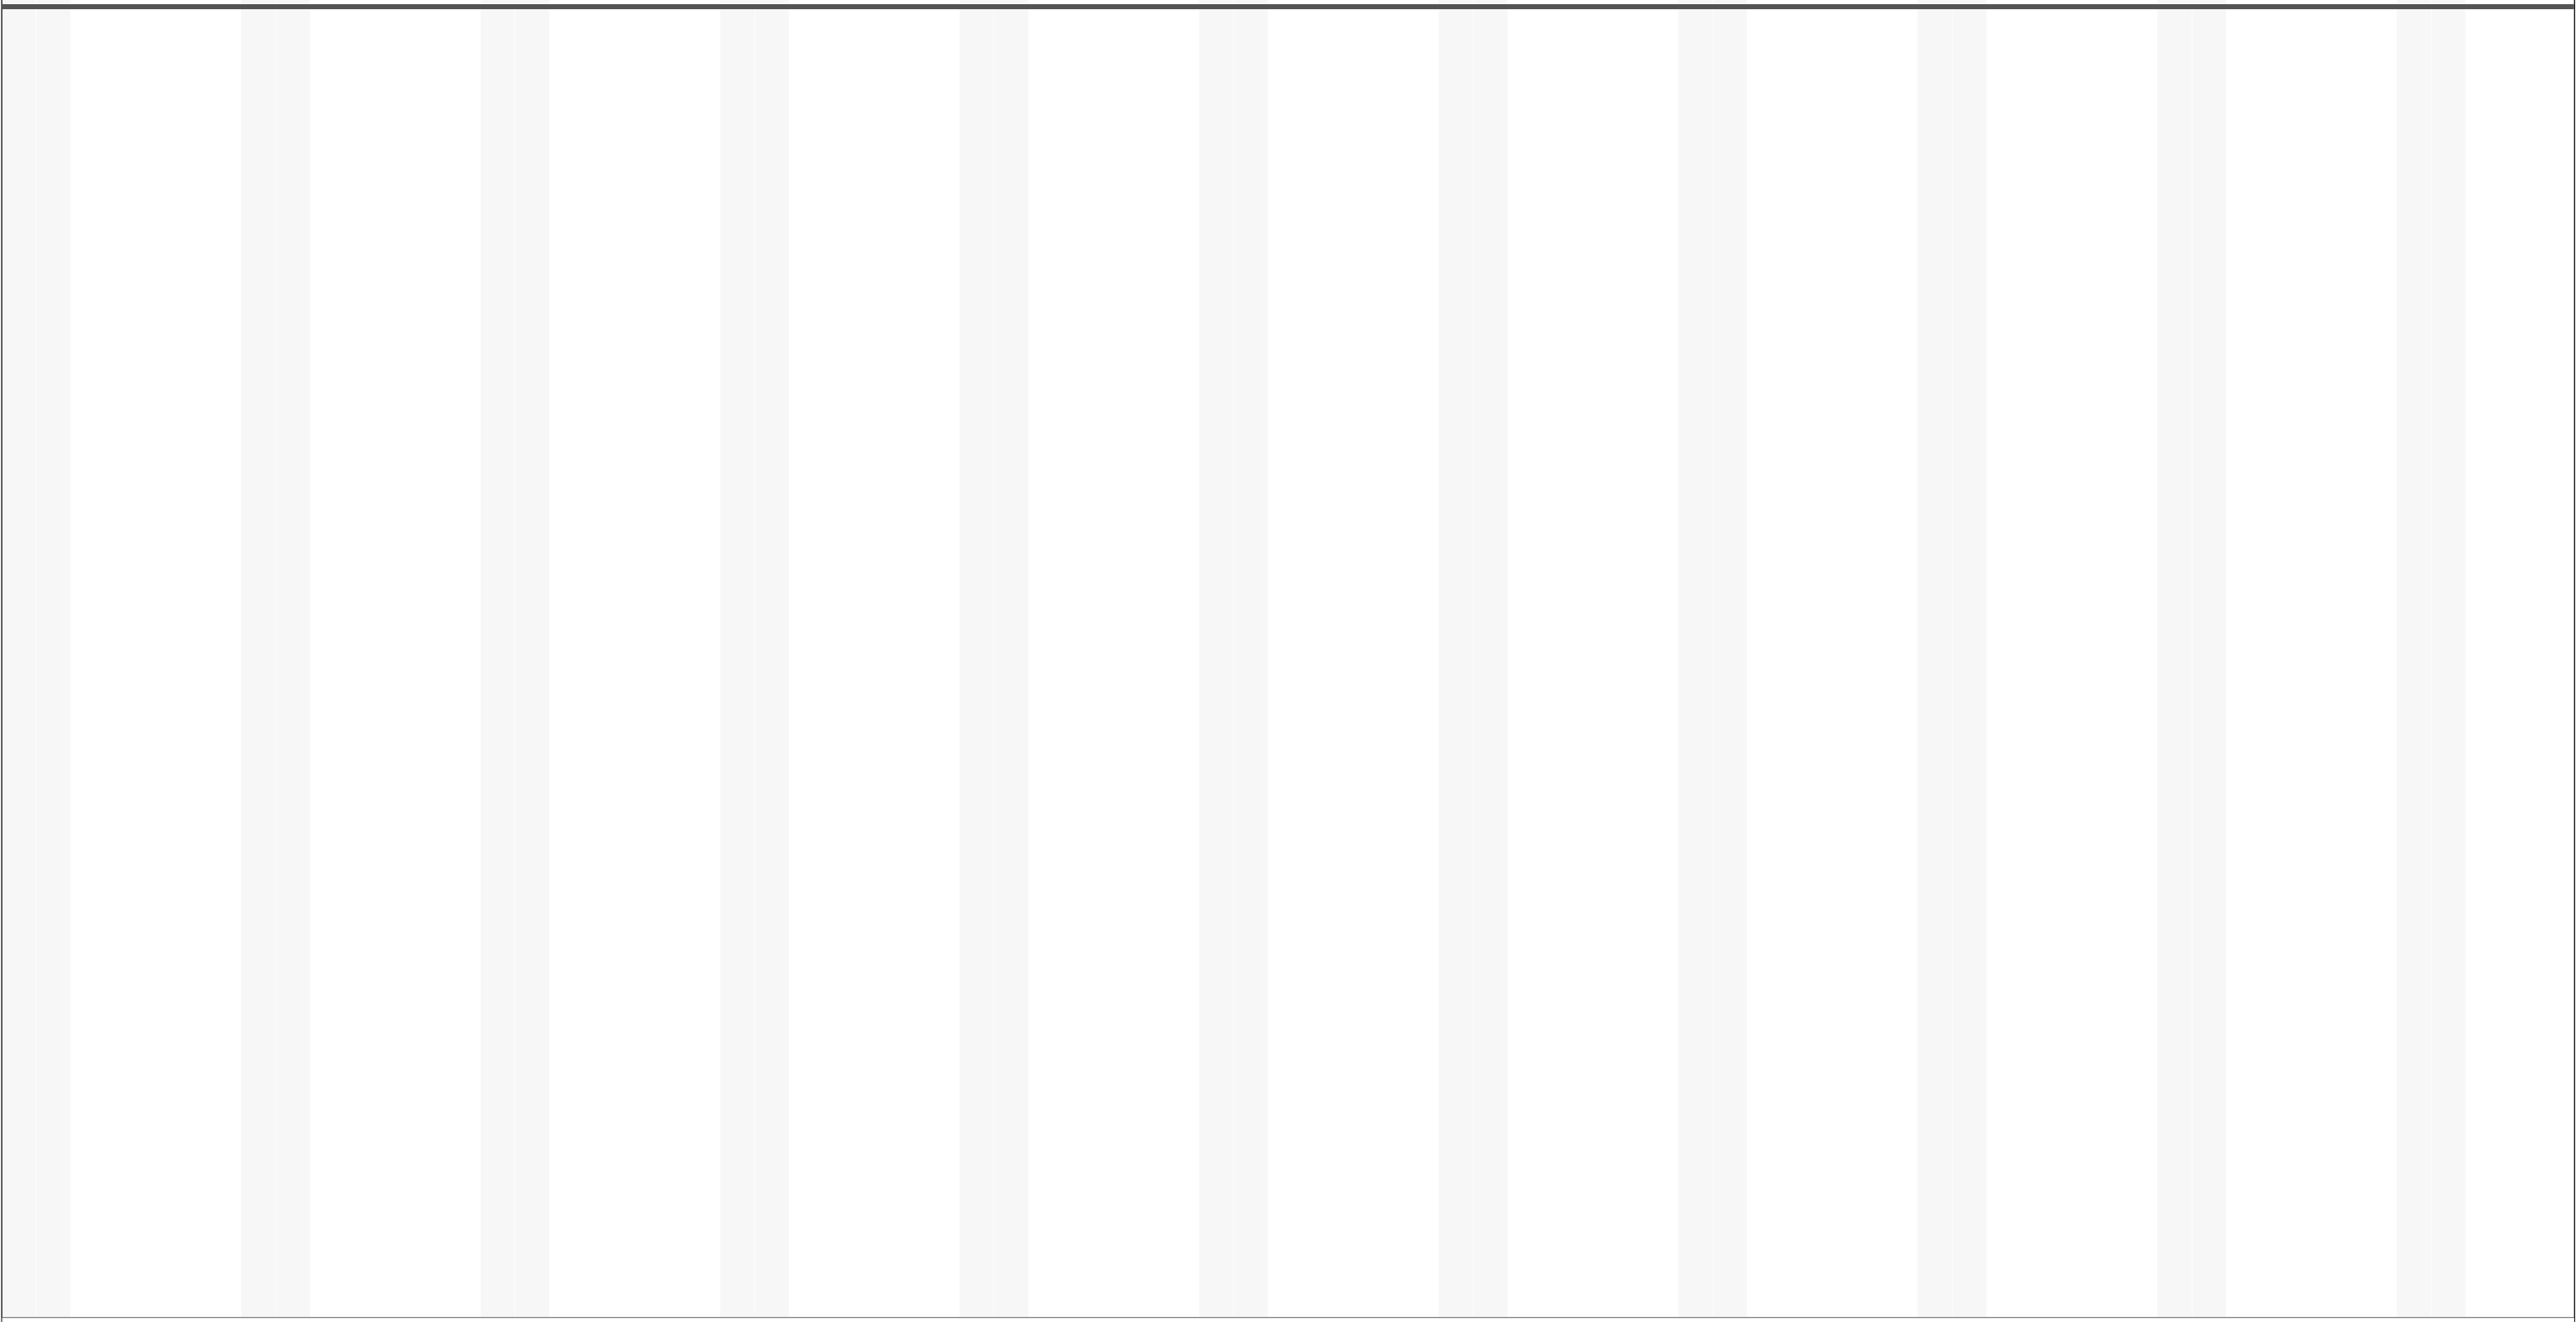


Project: Parking garage schedu Date: Sun 4/11/21	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

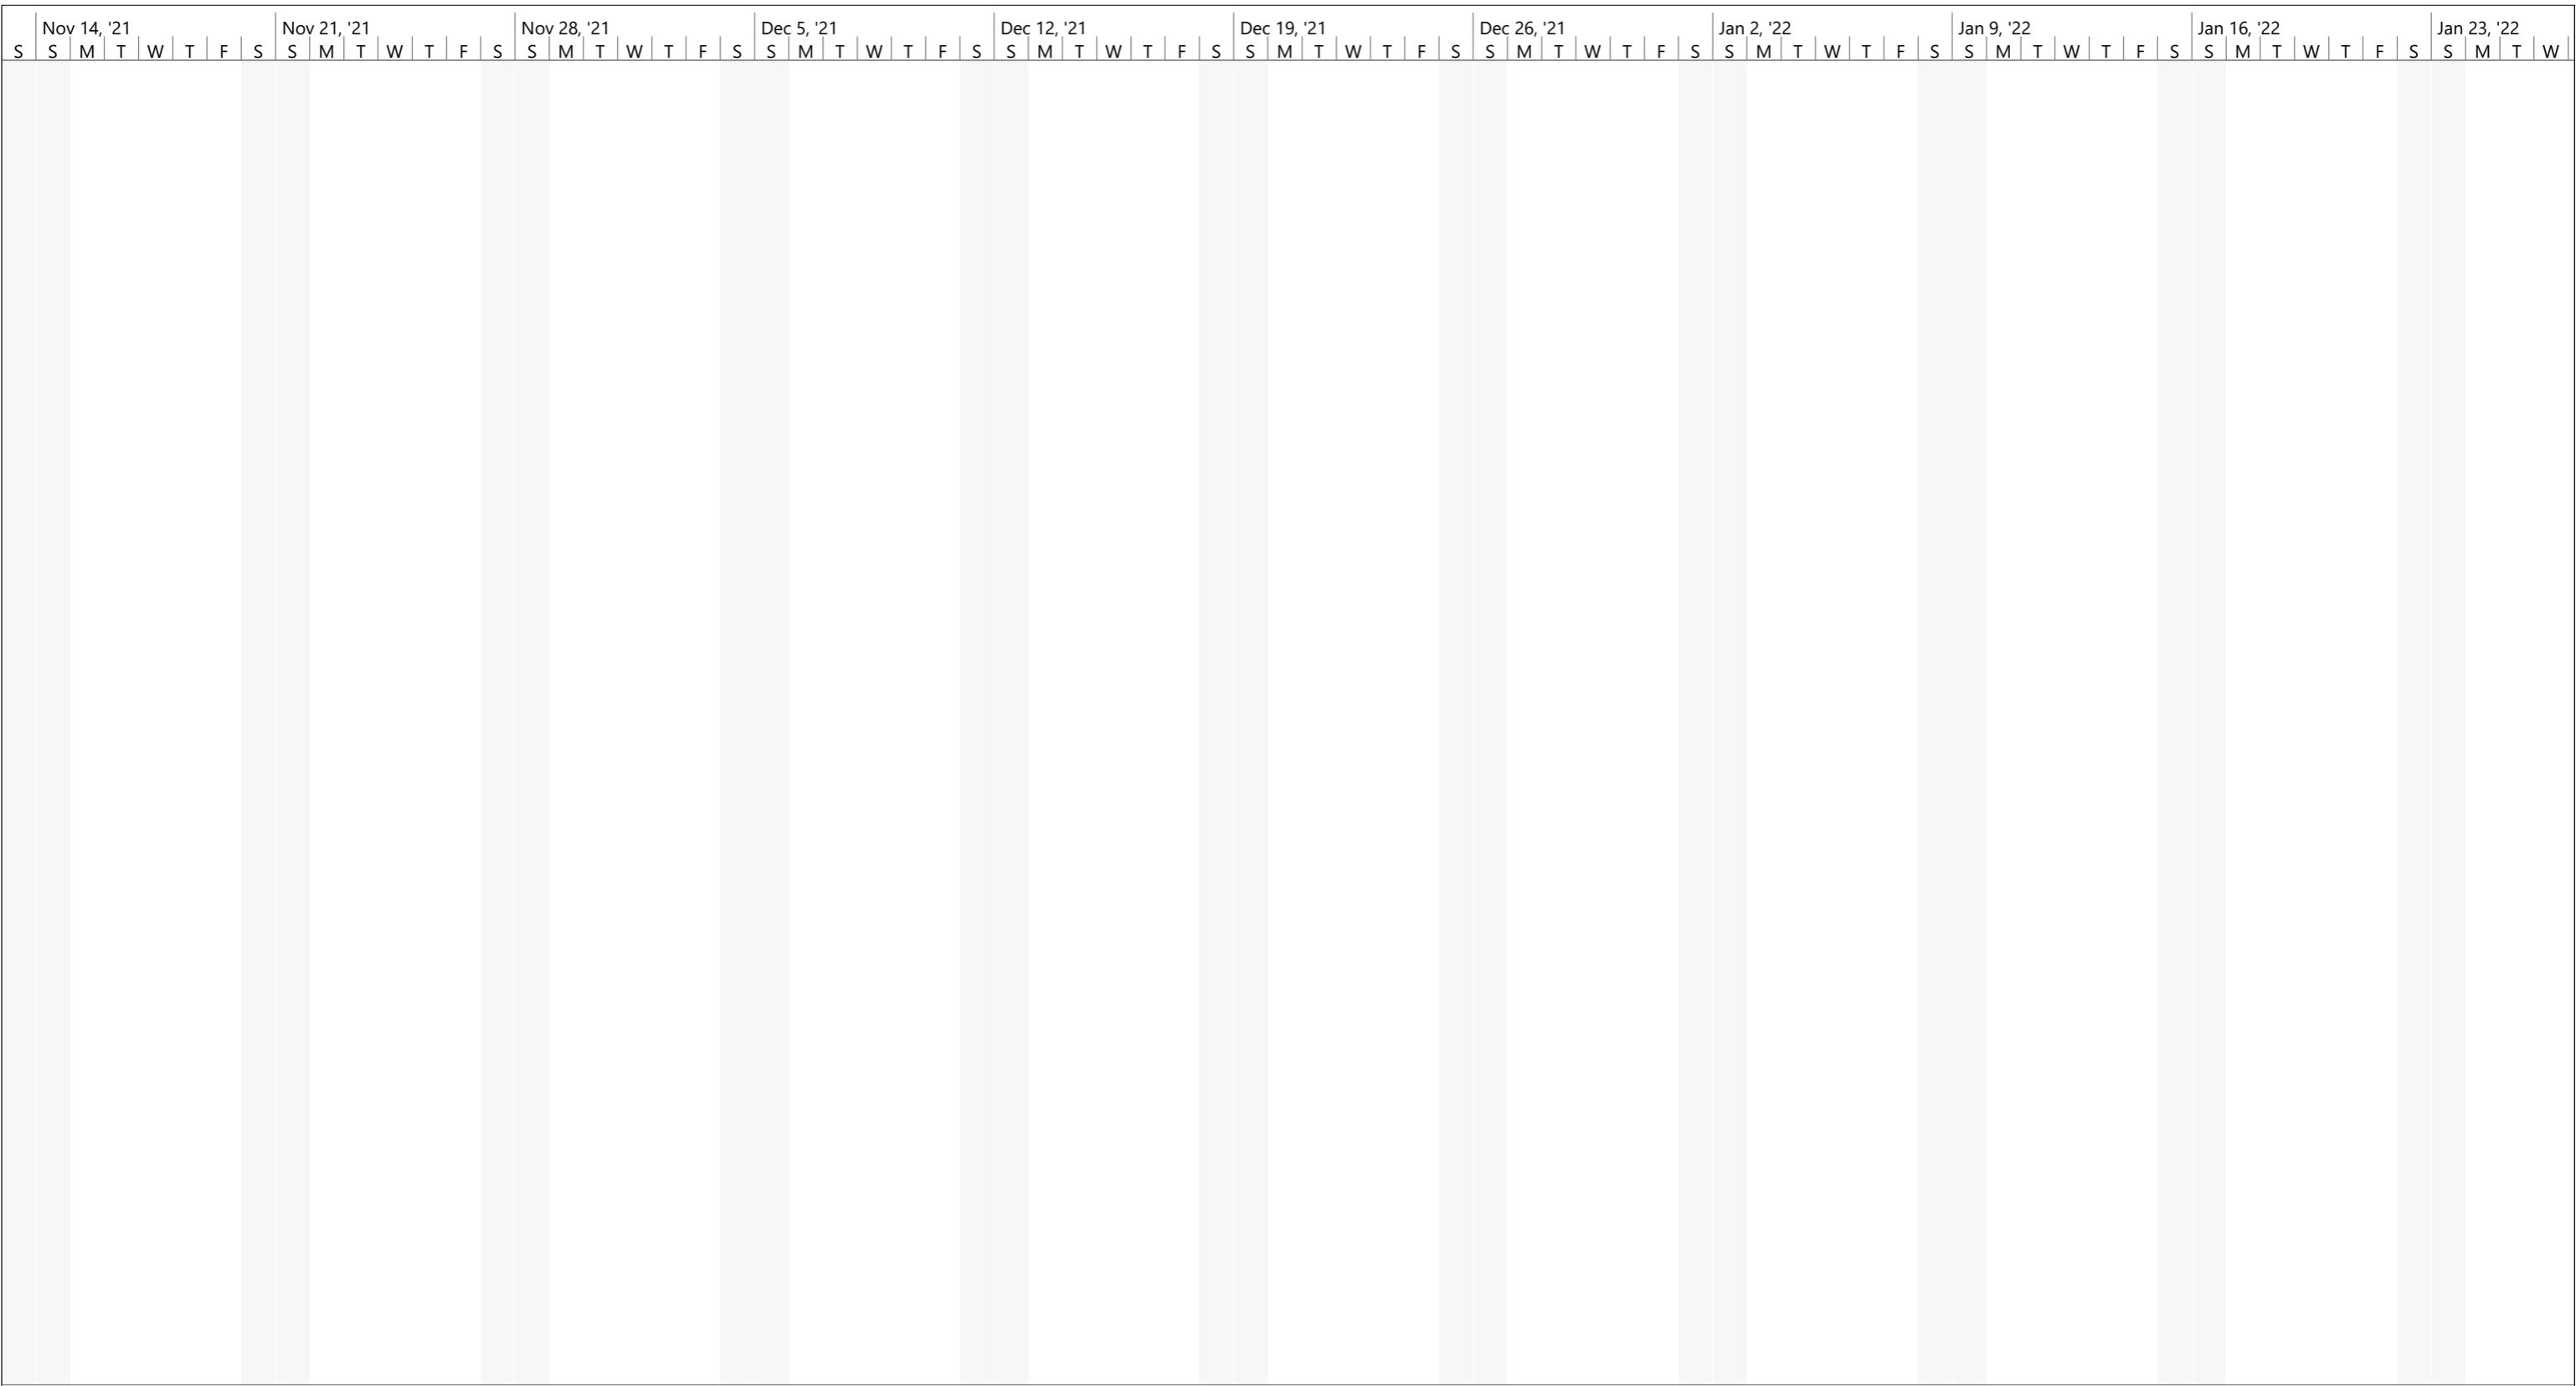

Project: Parking garage schedu
Date: Sun 4/11/21


Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S

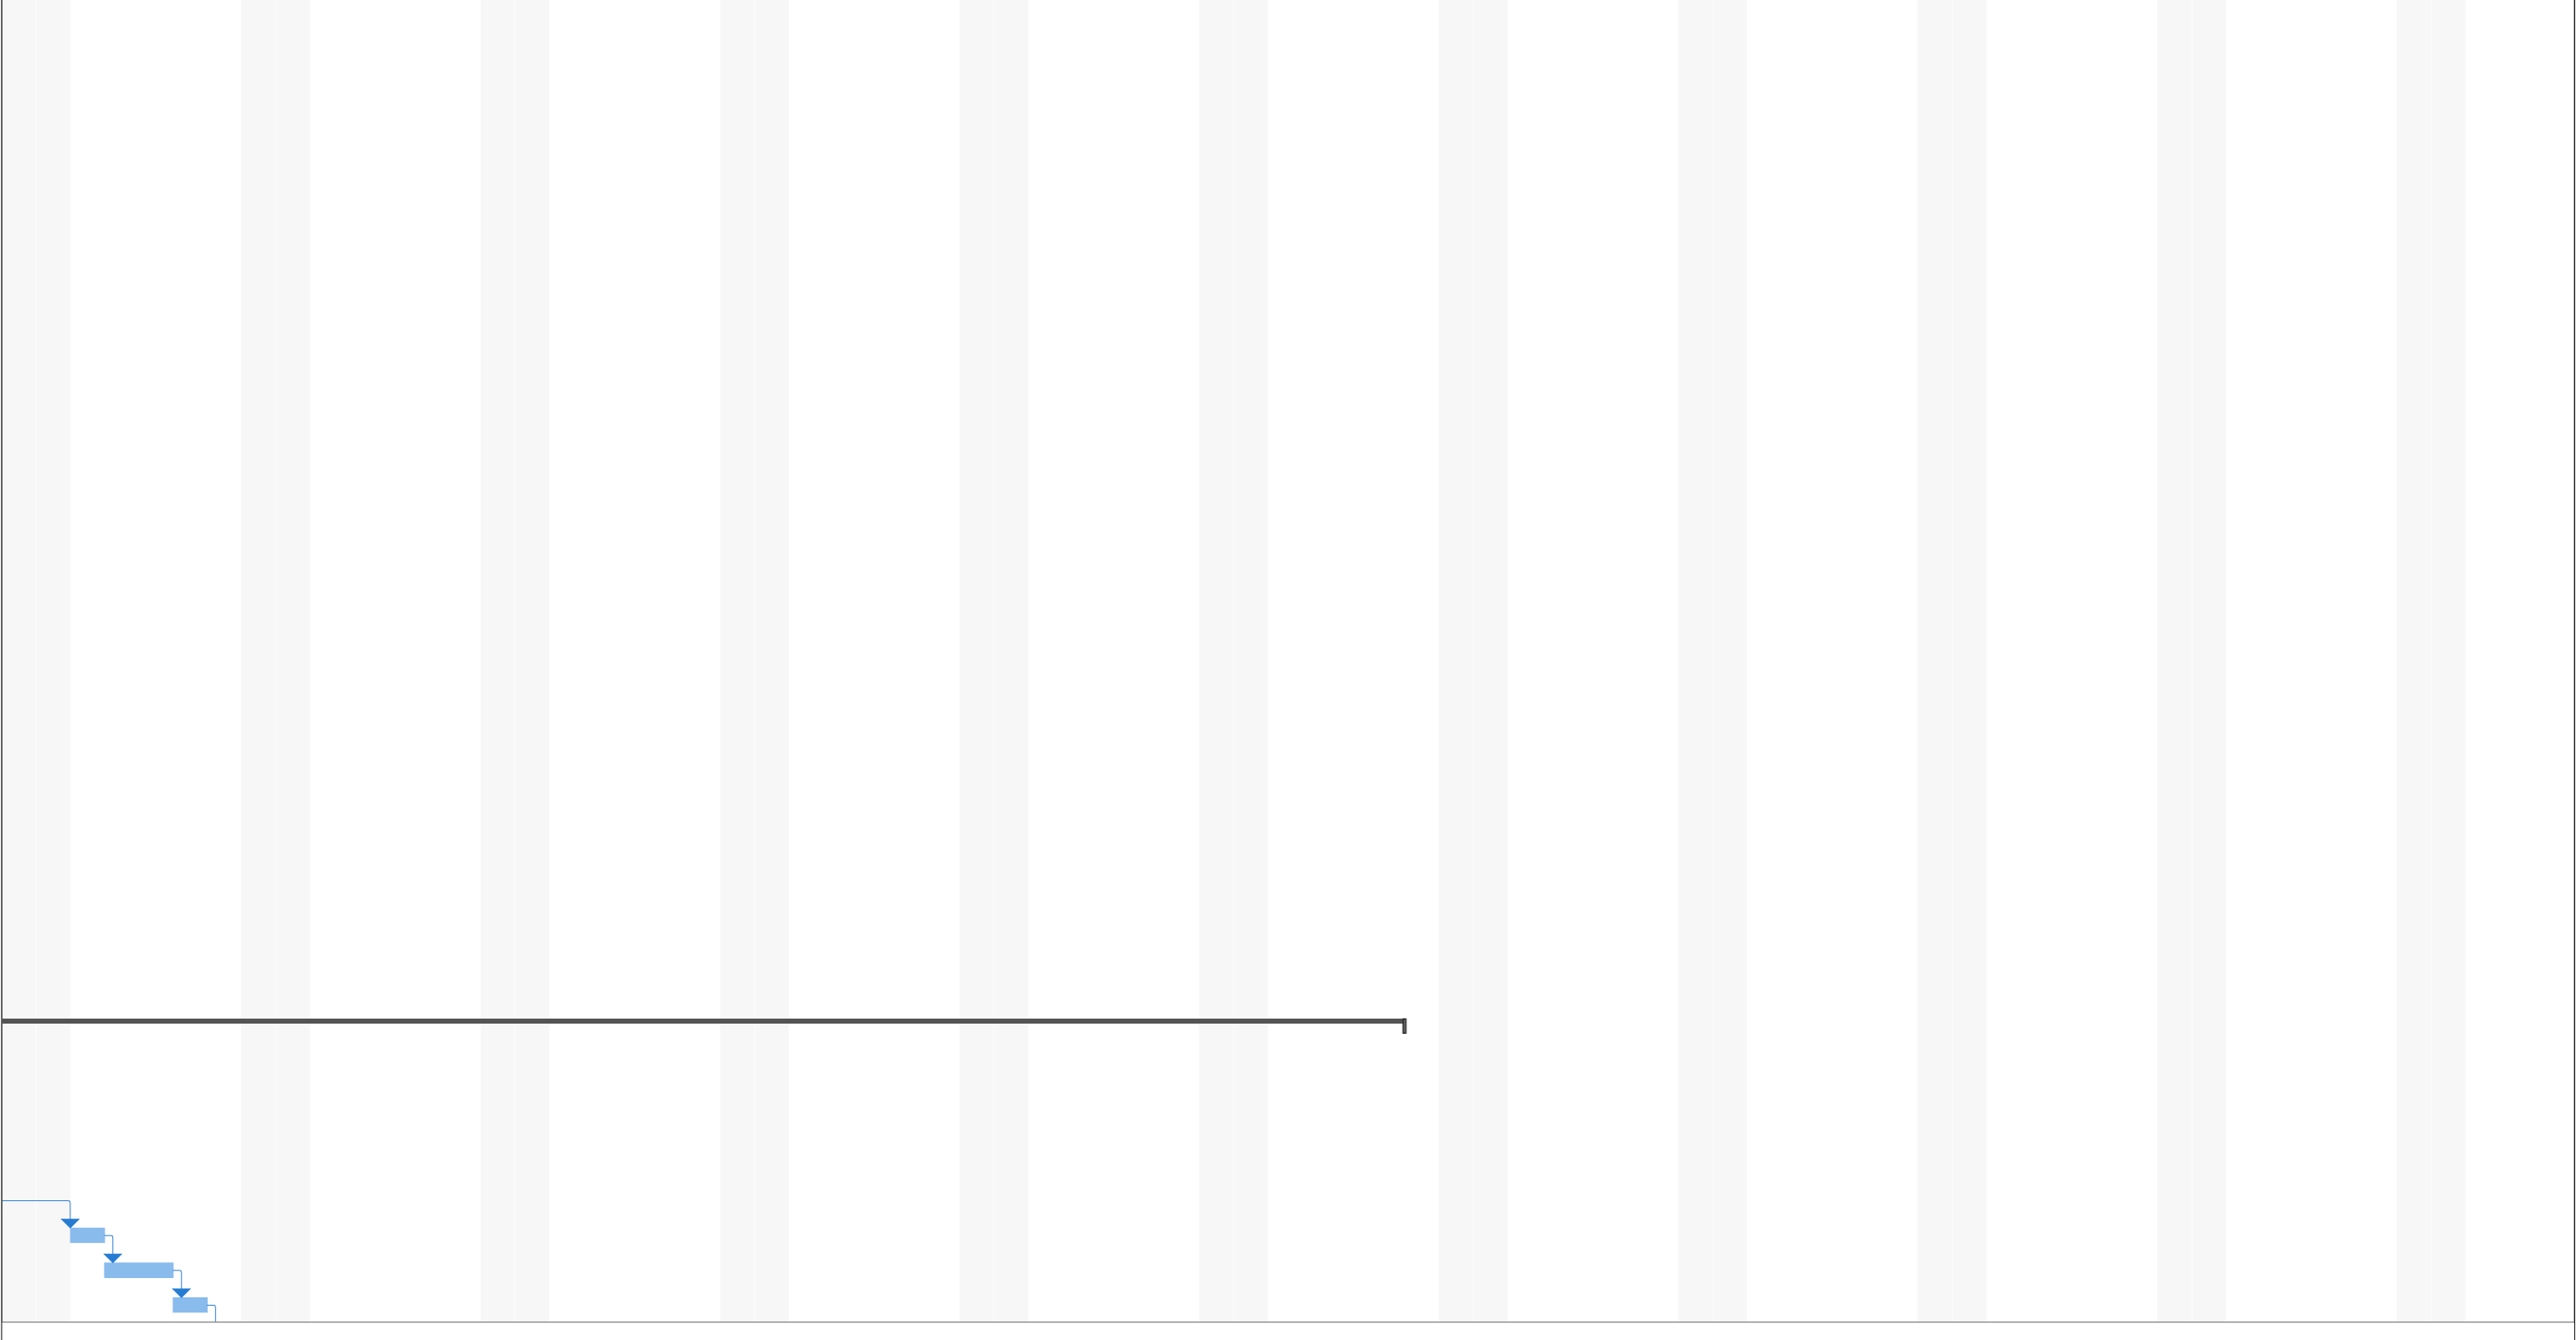

Project: Parking garage schedu
Date: Sun 4/11/21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

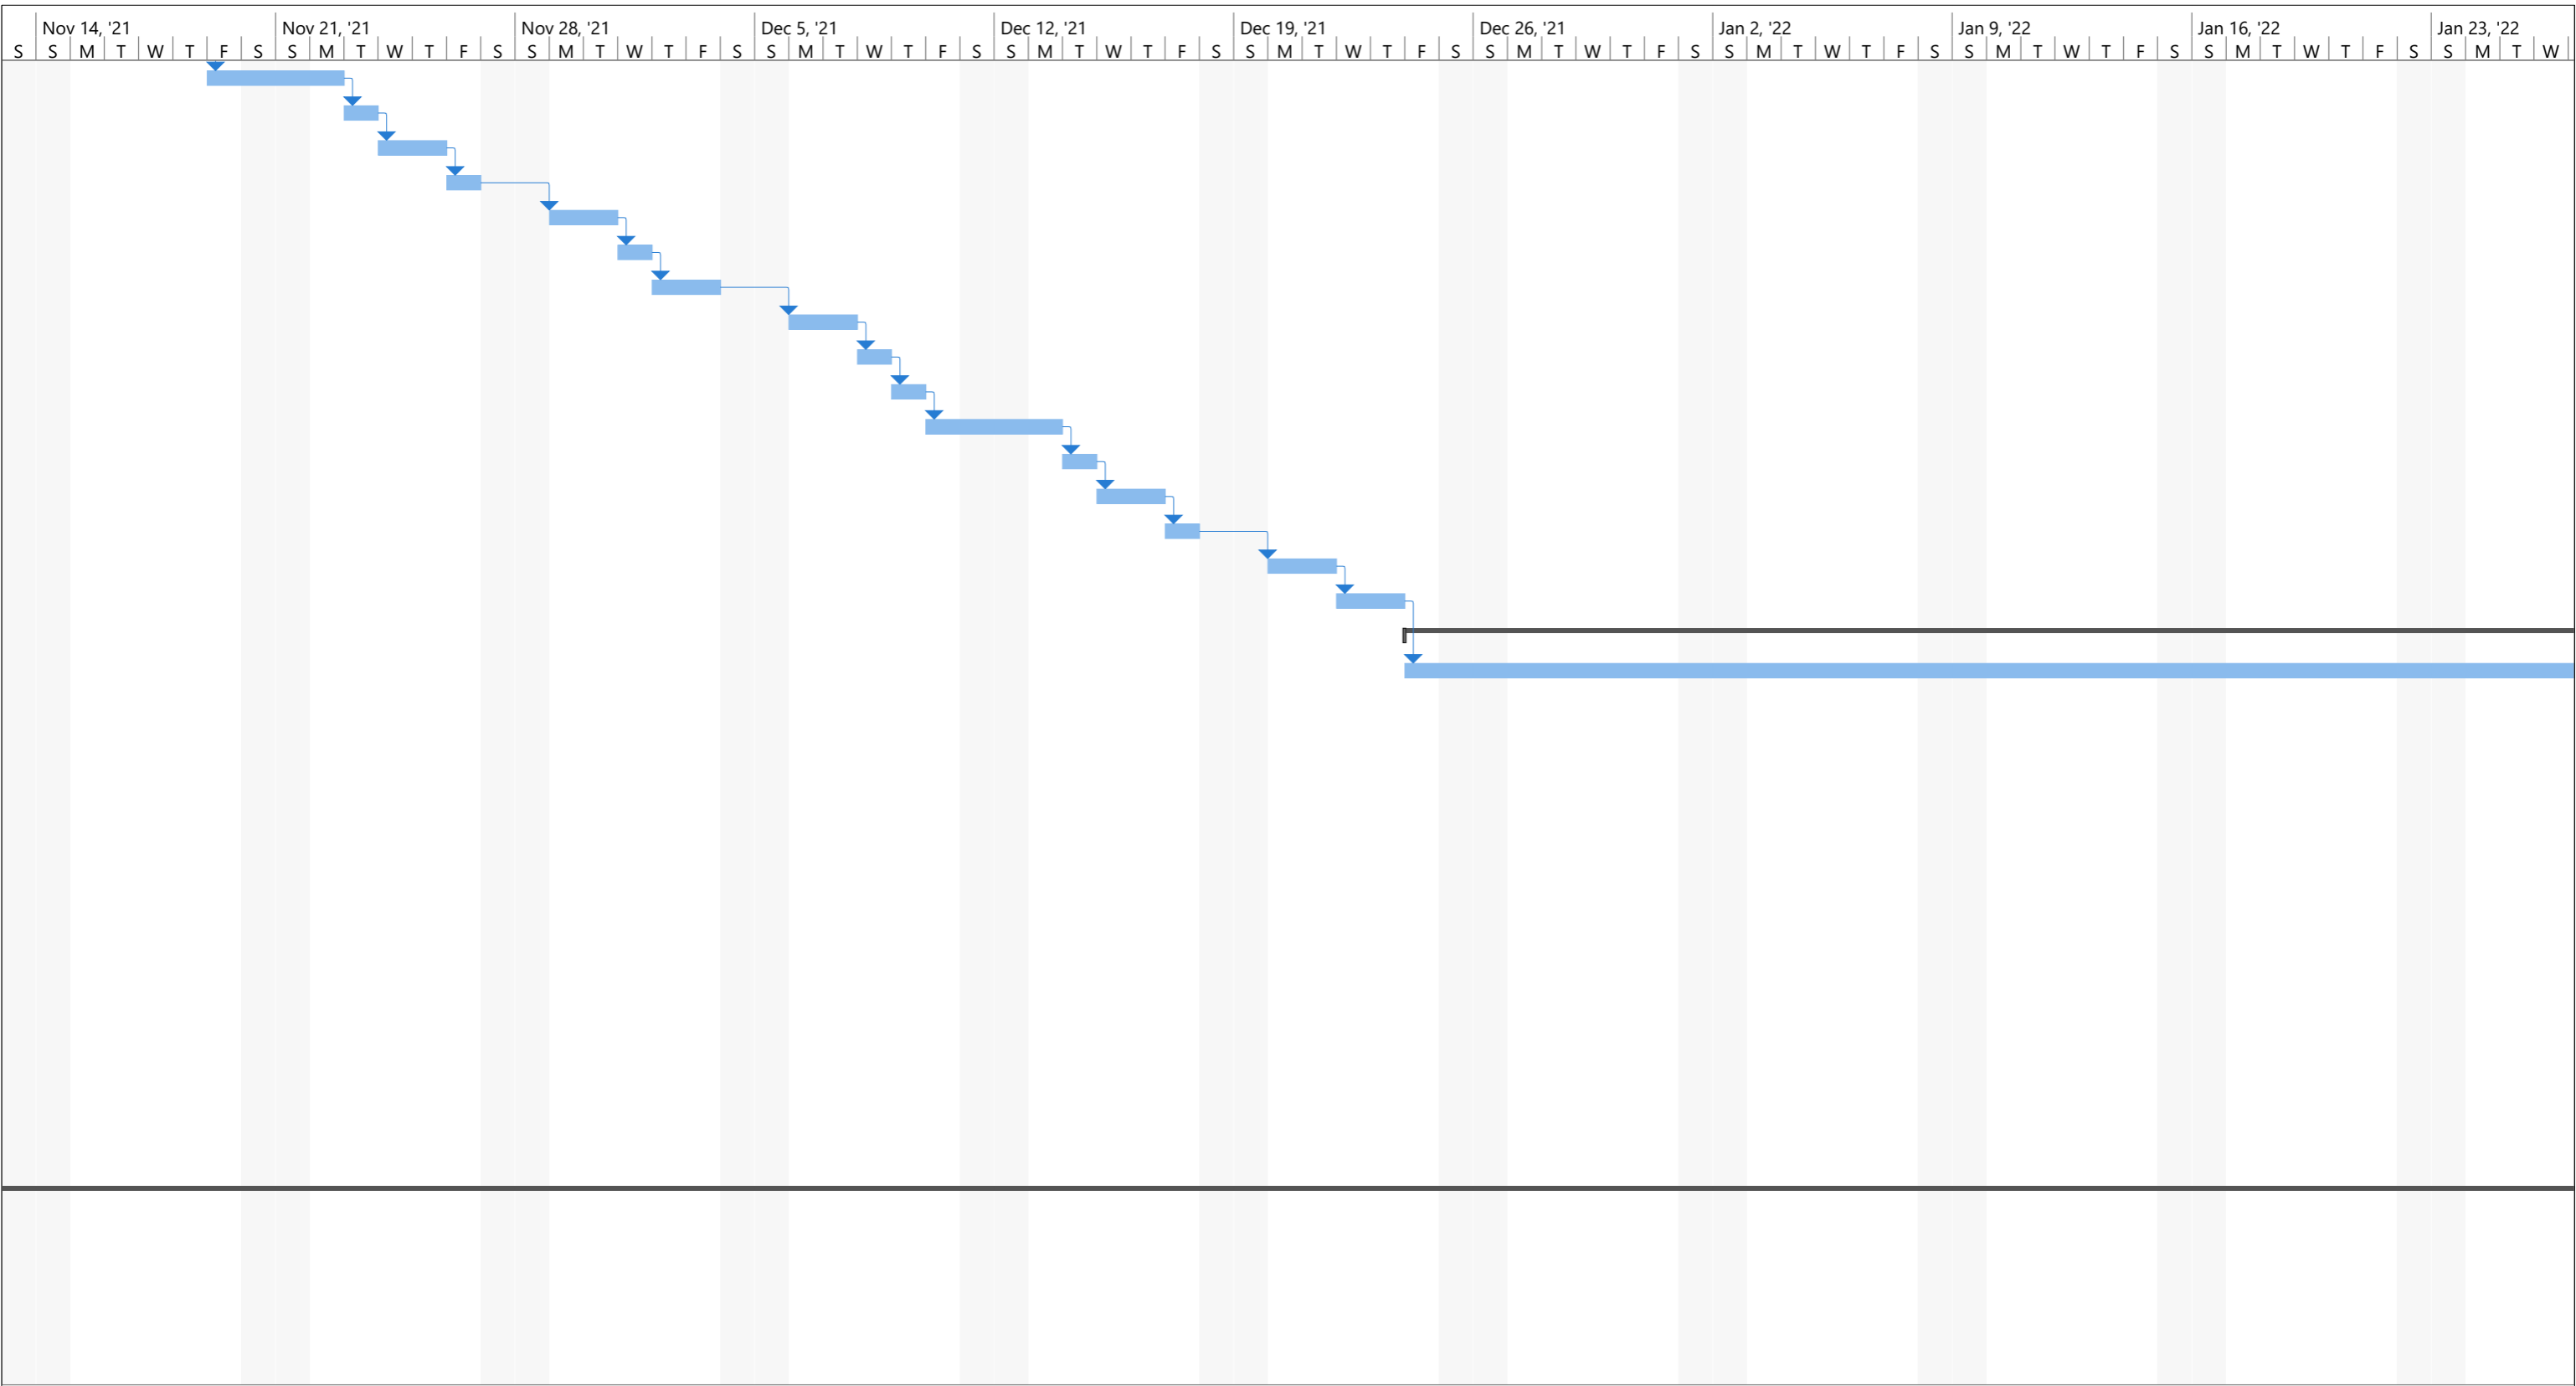

Project: Parking garage schedu
Date: Sun 4/11/21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			




Project: Parking garage schedu
Date: Sun 4/11/21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			




Project: Parking garage schedu
Date: Sun 4/11/21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

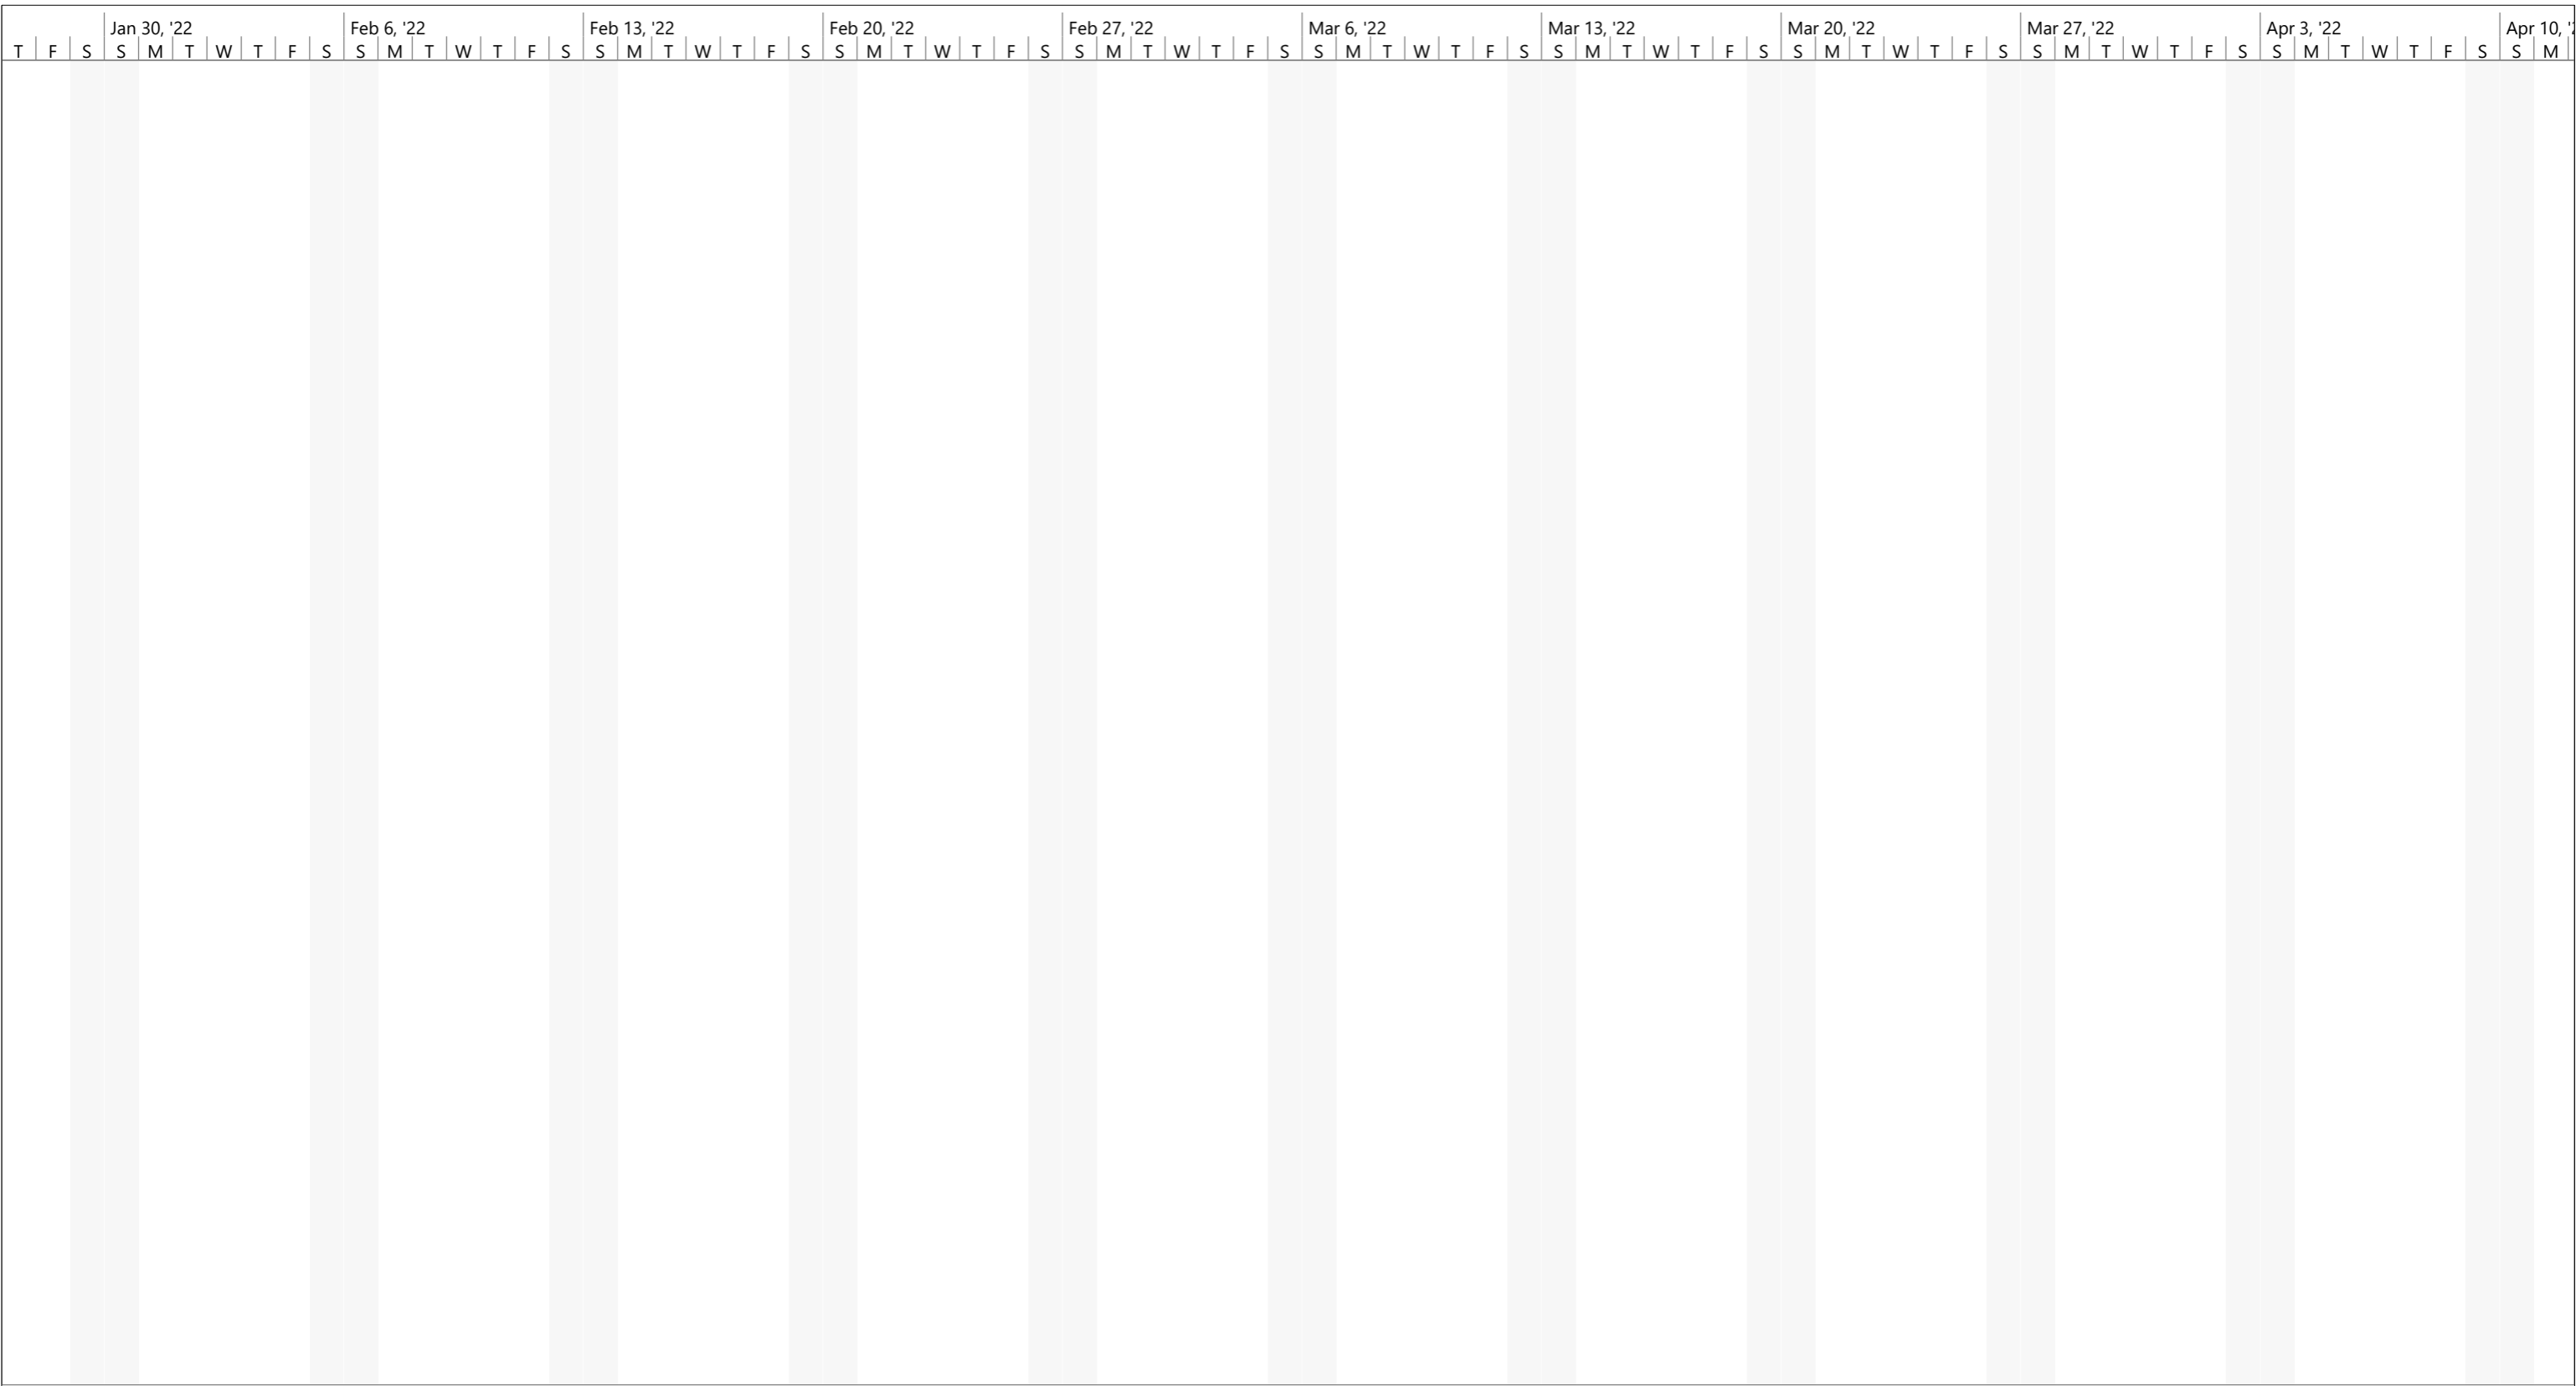


Project: Parking garage schedu
Date: Sun 4/11/21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

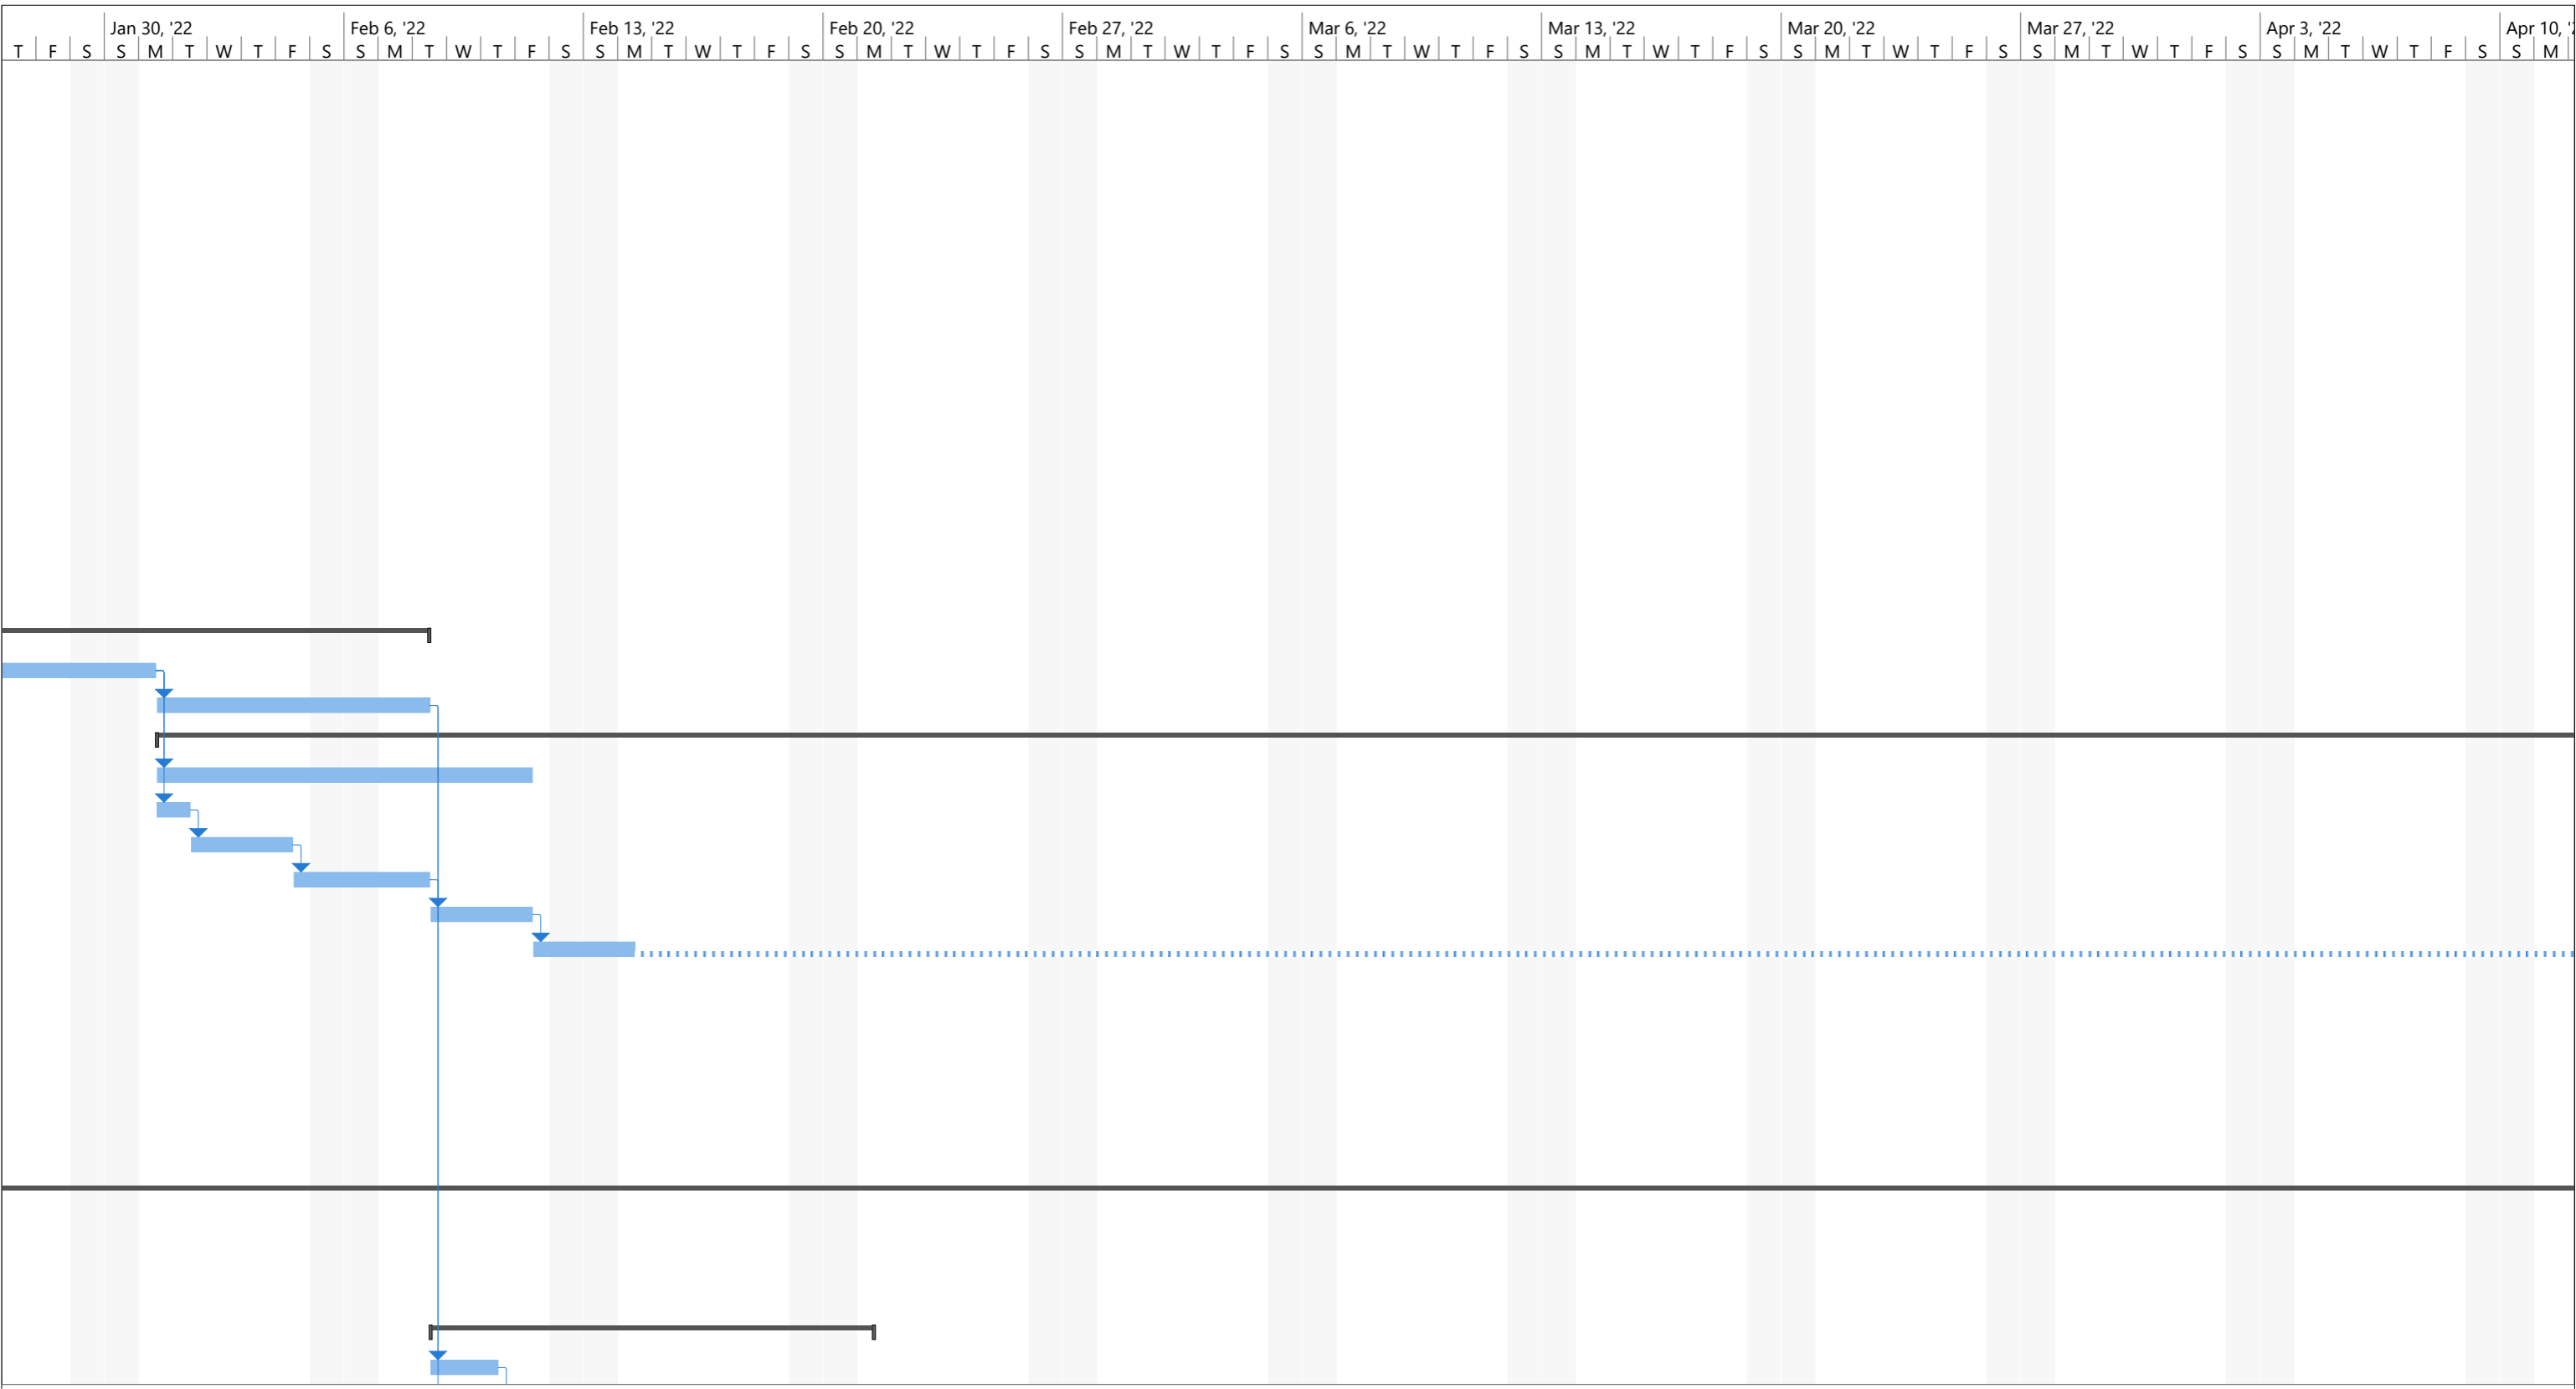


Project: Parking garage schedu
Date: Sun 4/11/21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

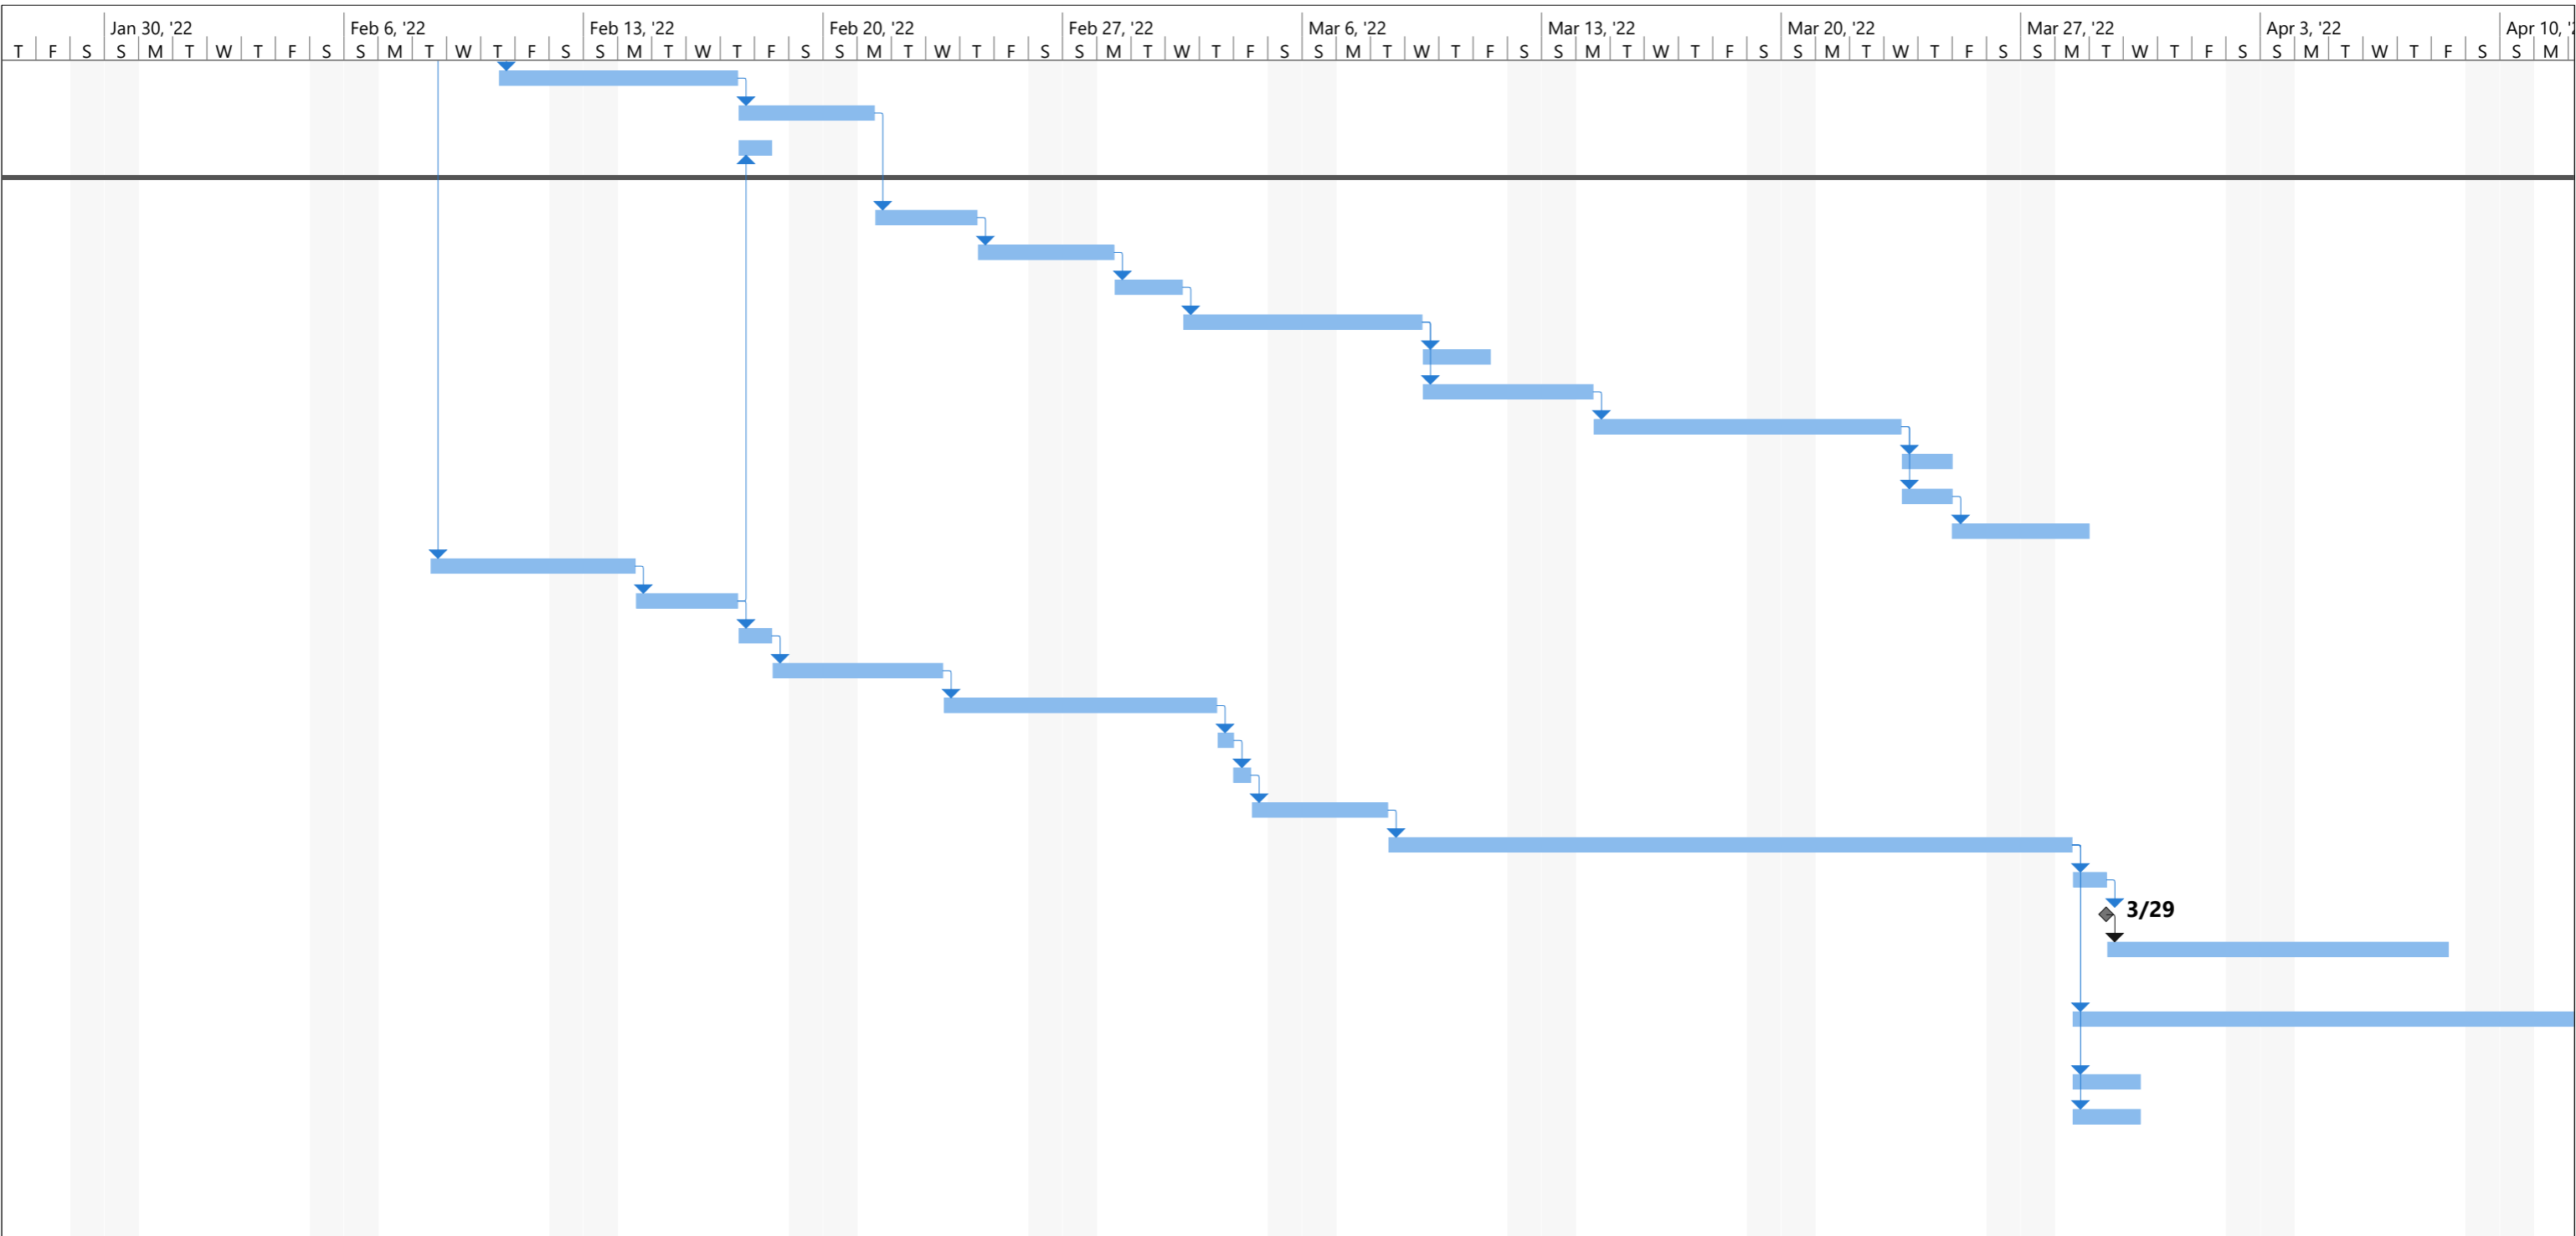

Project: Parking garage schedu
Date: Sun 4/11/21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

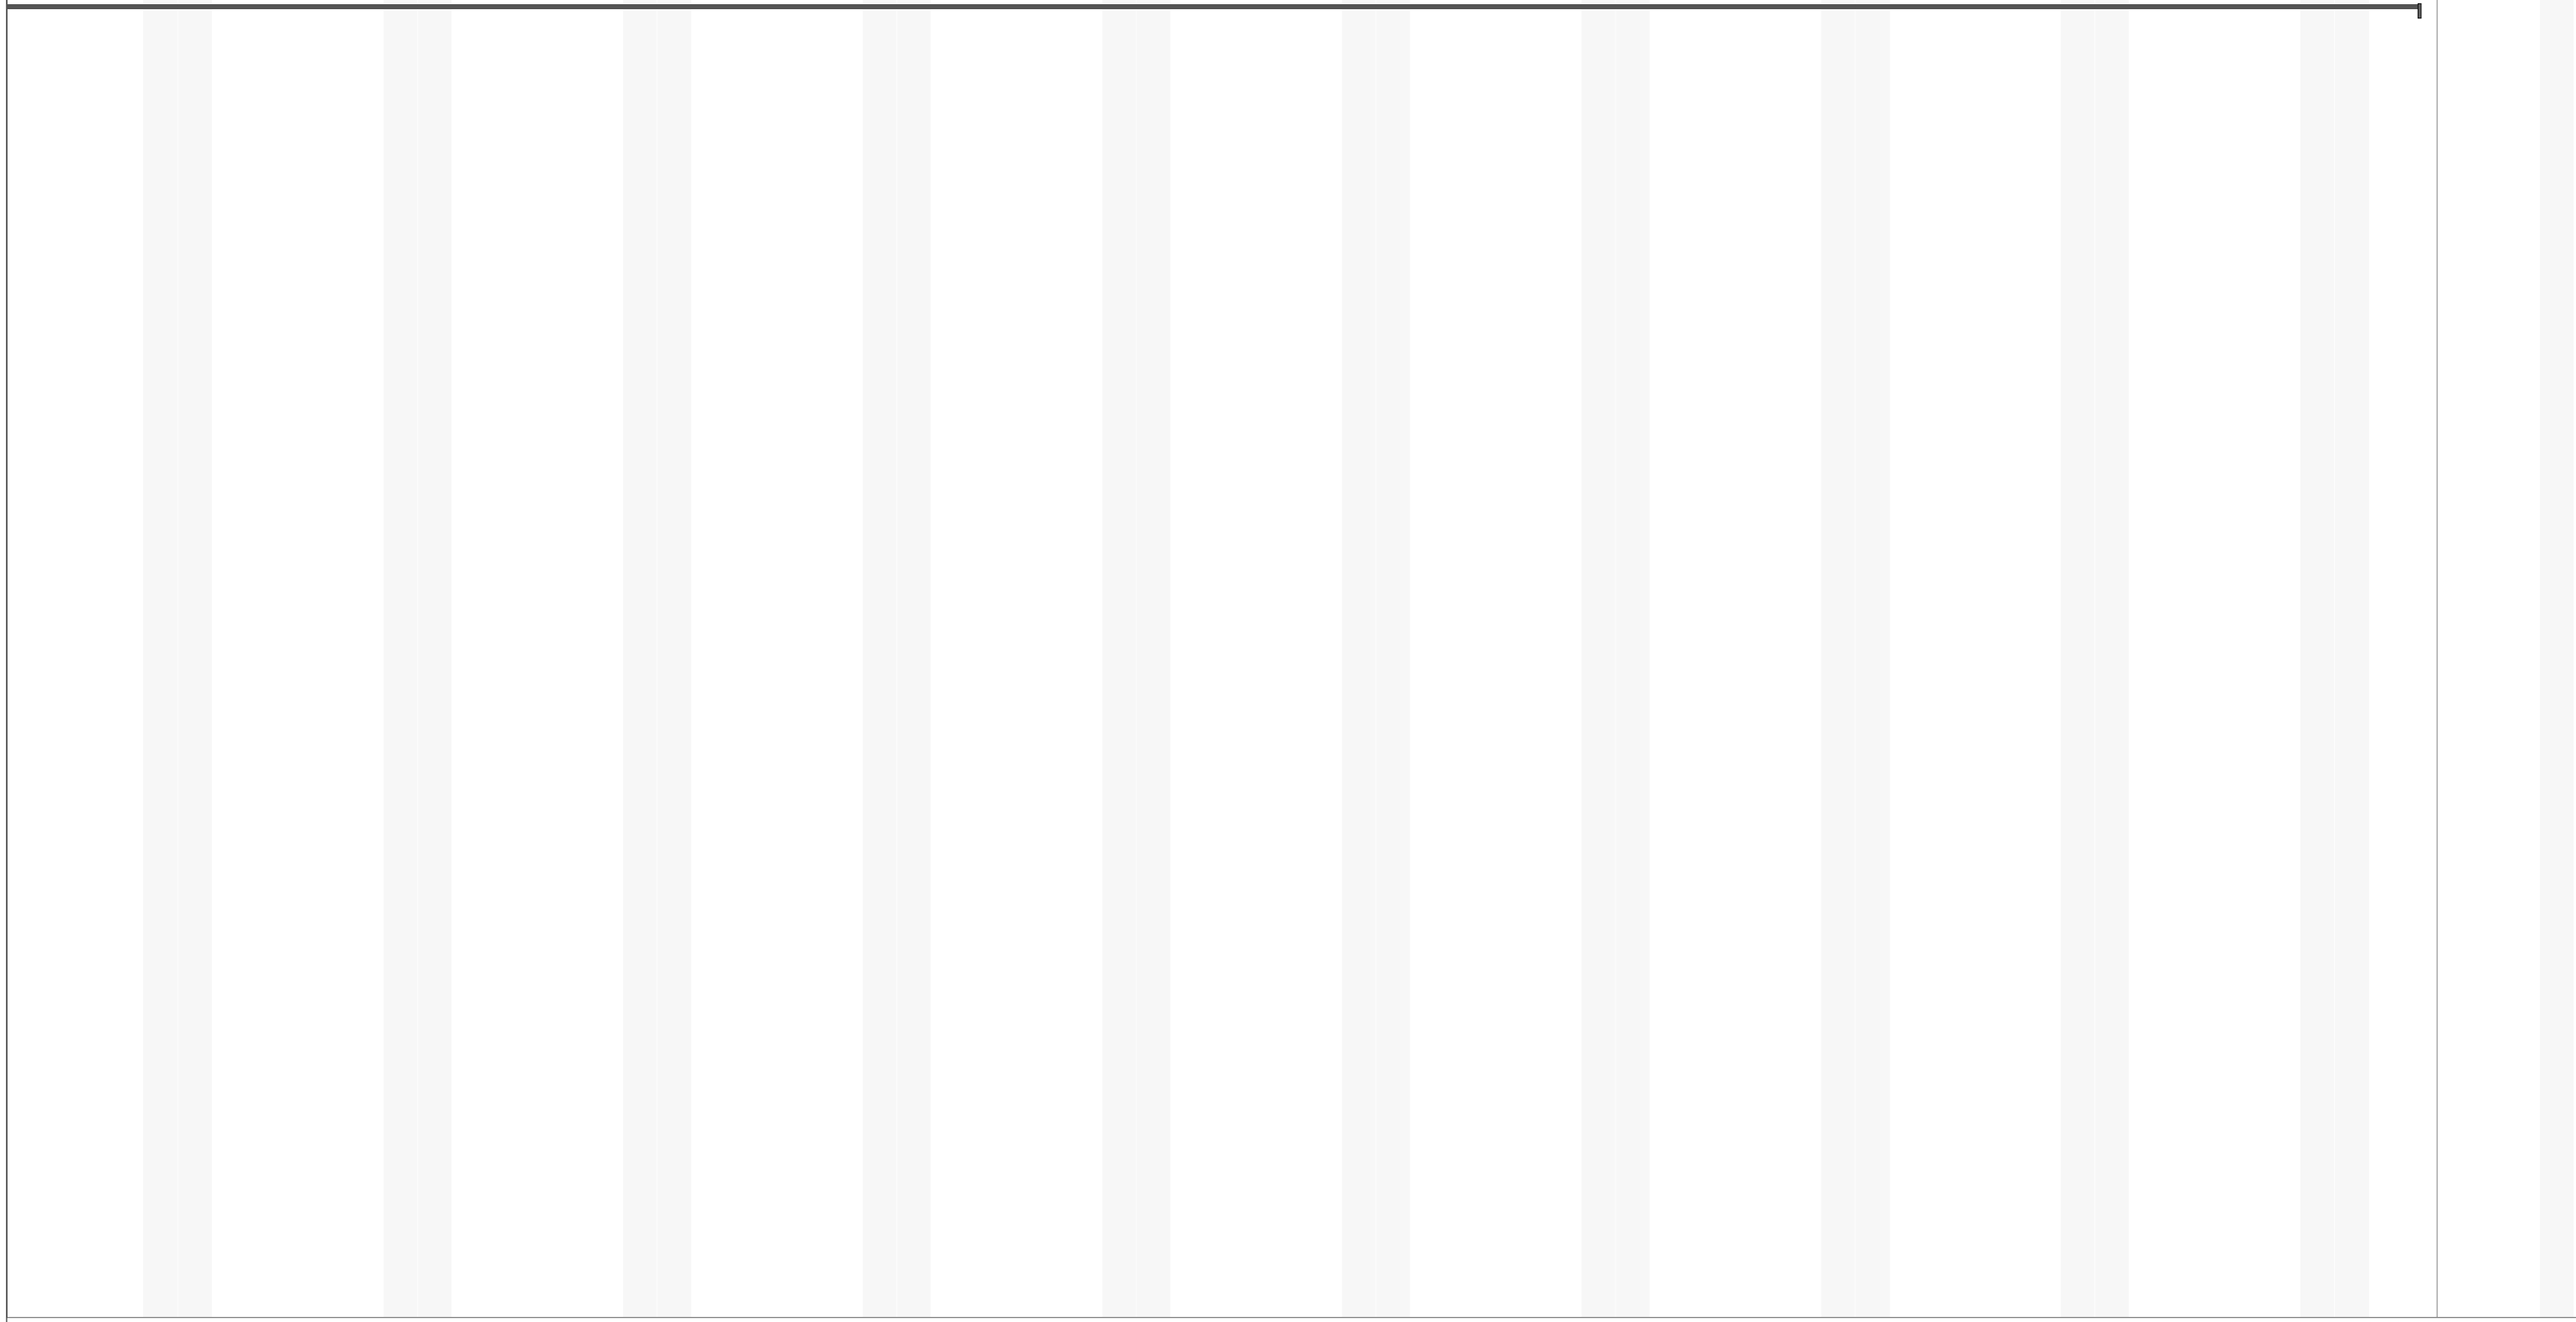

Project: Parking garage schedu Date: Sun 4/11/21	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			



Project: Parking garage schedu
Date: Sun 4/11/21


Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			




Project: Parking garage schedu
Date: Sun 4/11/21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

22 | T | W | T | F | S | Apr 17, '22 | S | M | T | W | T | F | S | Apr 24, '22 | S | M | T | W | T | F | S | May 1, '22 | S | M | T | W | T | F | S | May 8, '22 | S | M | T | W | T | F | S | May 15, '22 | S | M | T | W | T | F | S | May 22, '22 | S | M | T | W | T | F | S | May 29, '22 | S | M | T | W | T | F | S | Jun 5, '22 | S | M | T | W | T | F | S | Jun 12, '22 | S | M | T | W | T | F | S | Jun 19, '22 | S | M | T | W | T | F | S

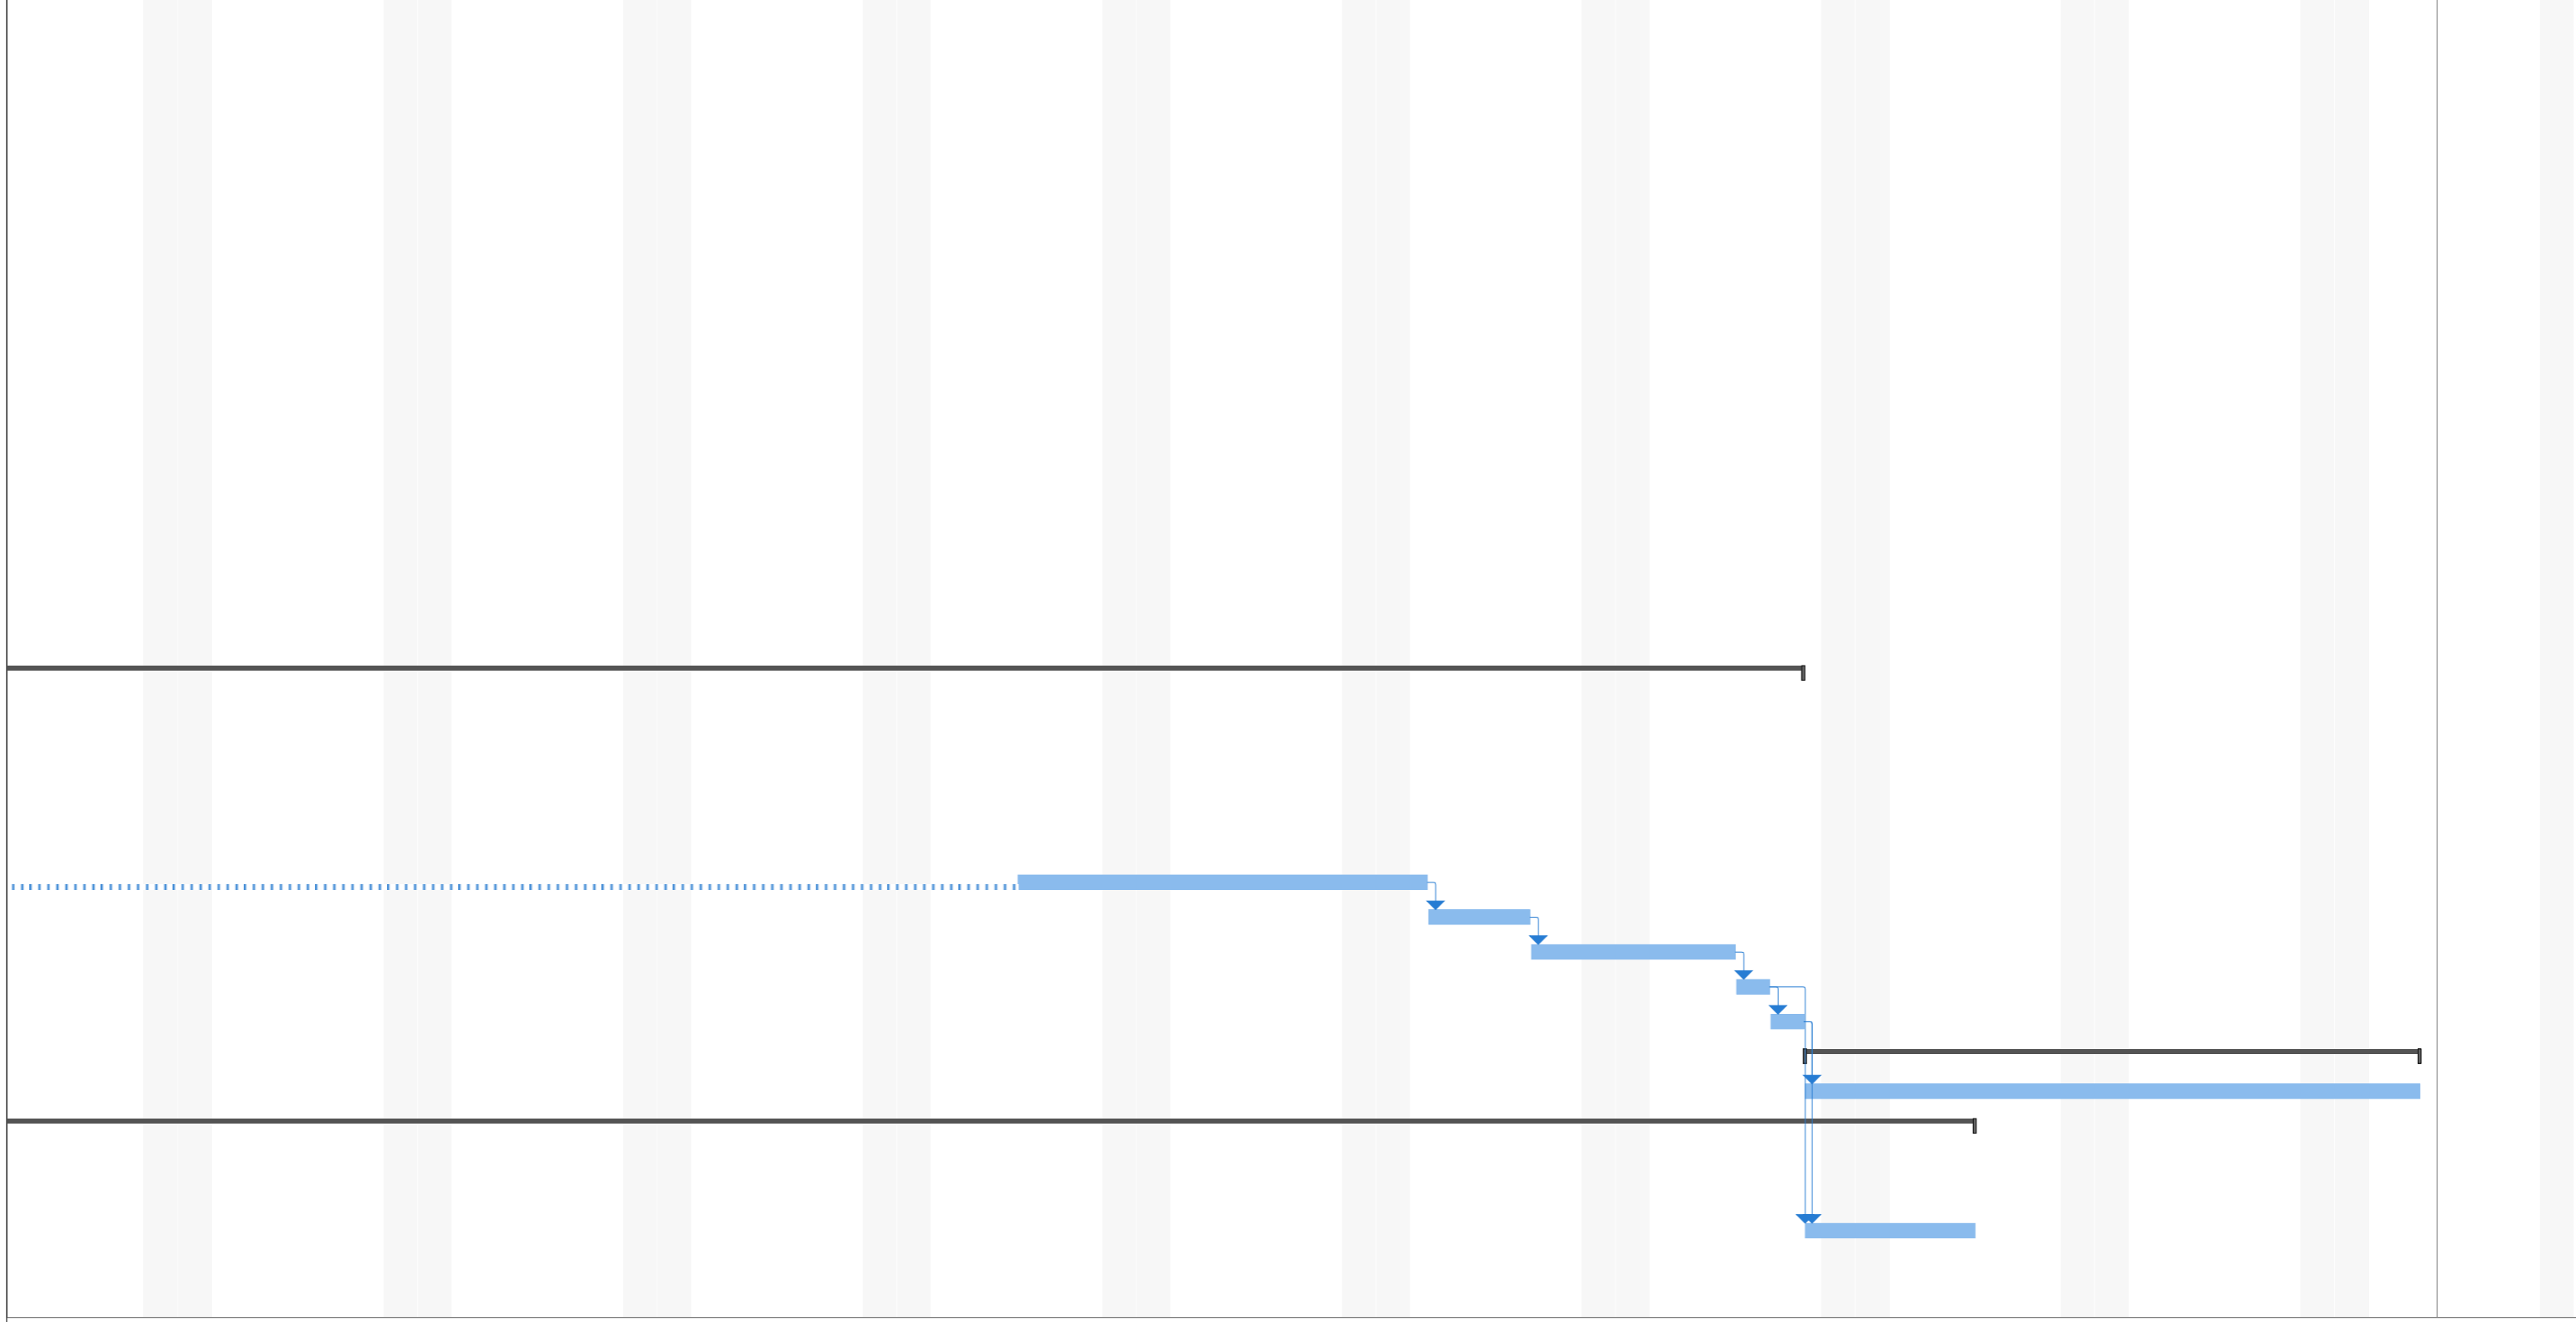


Project: Parking garage schedu Date: Sun 4/11/21	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

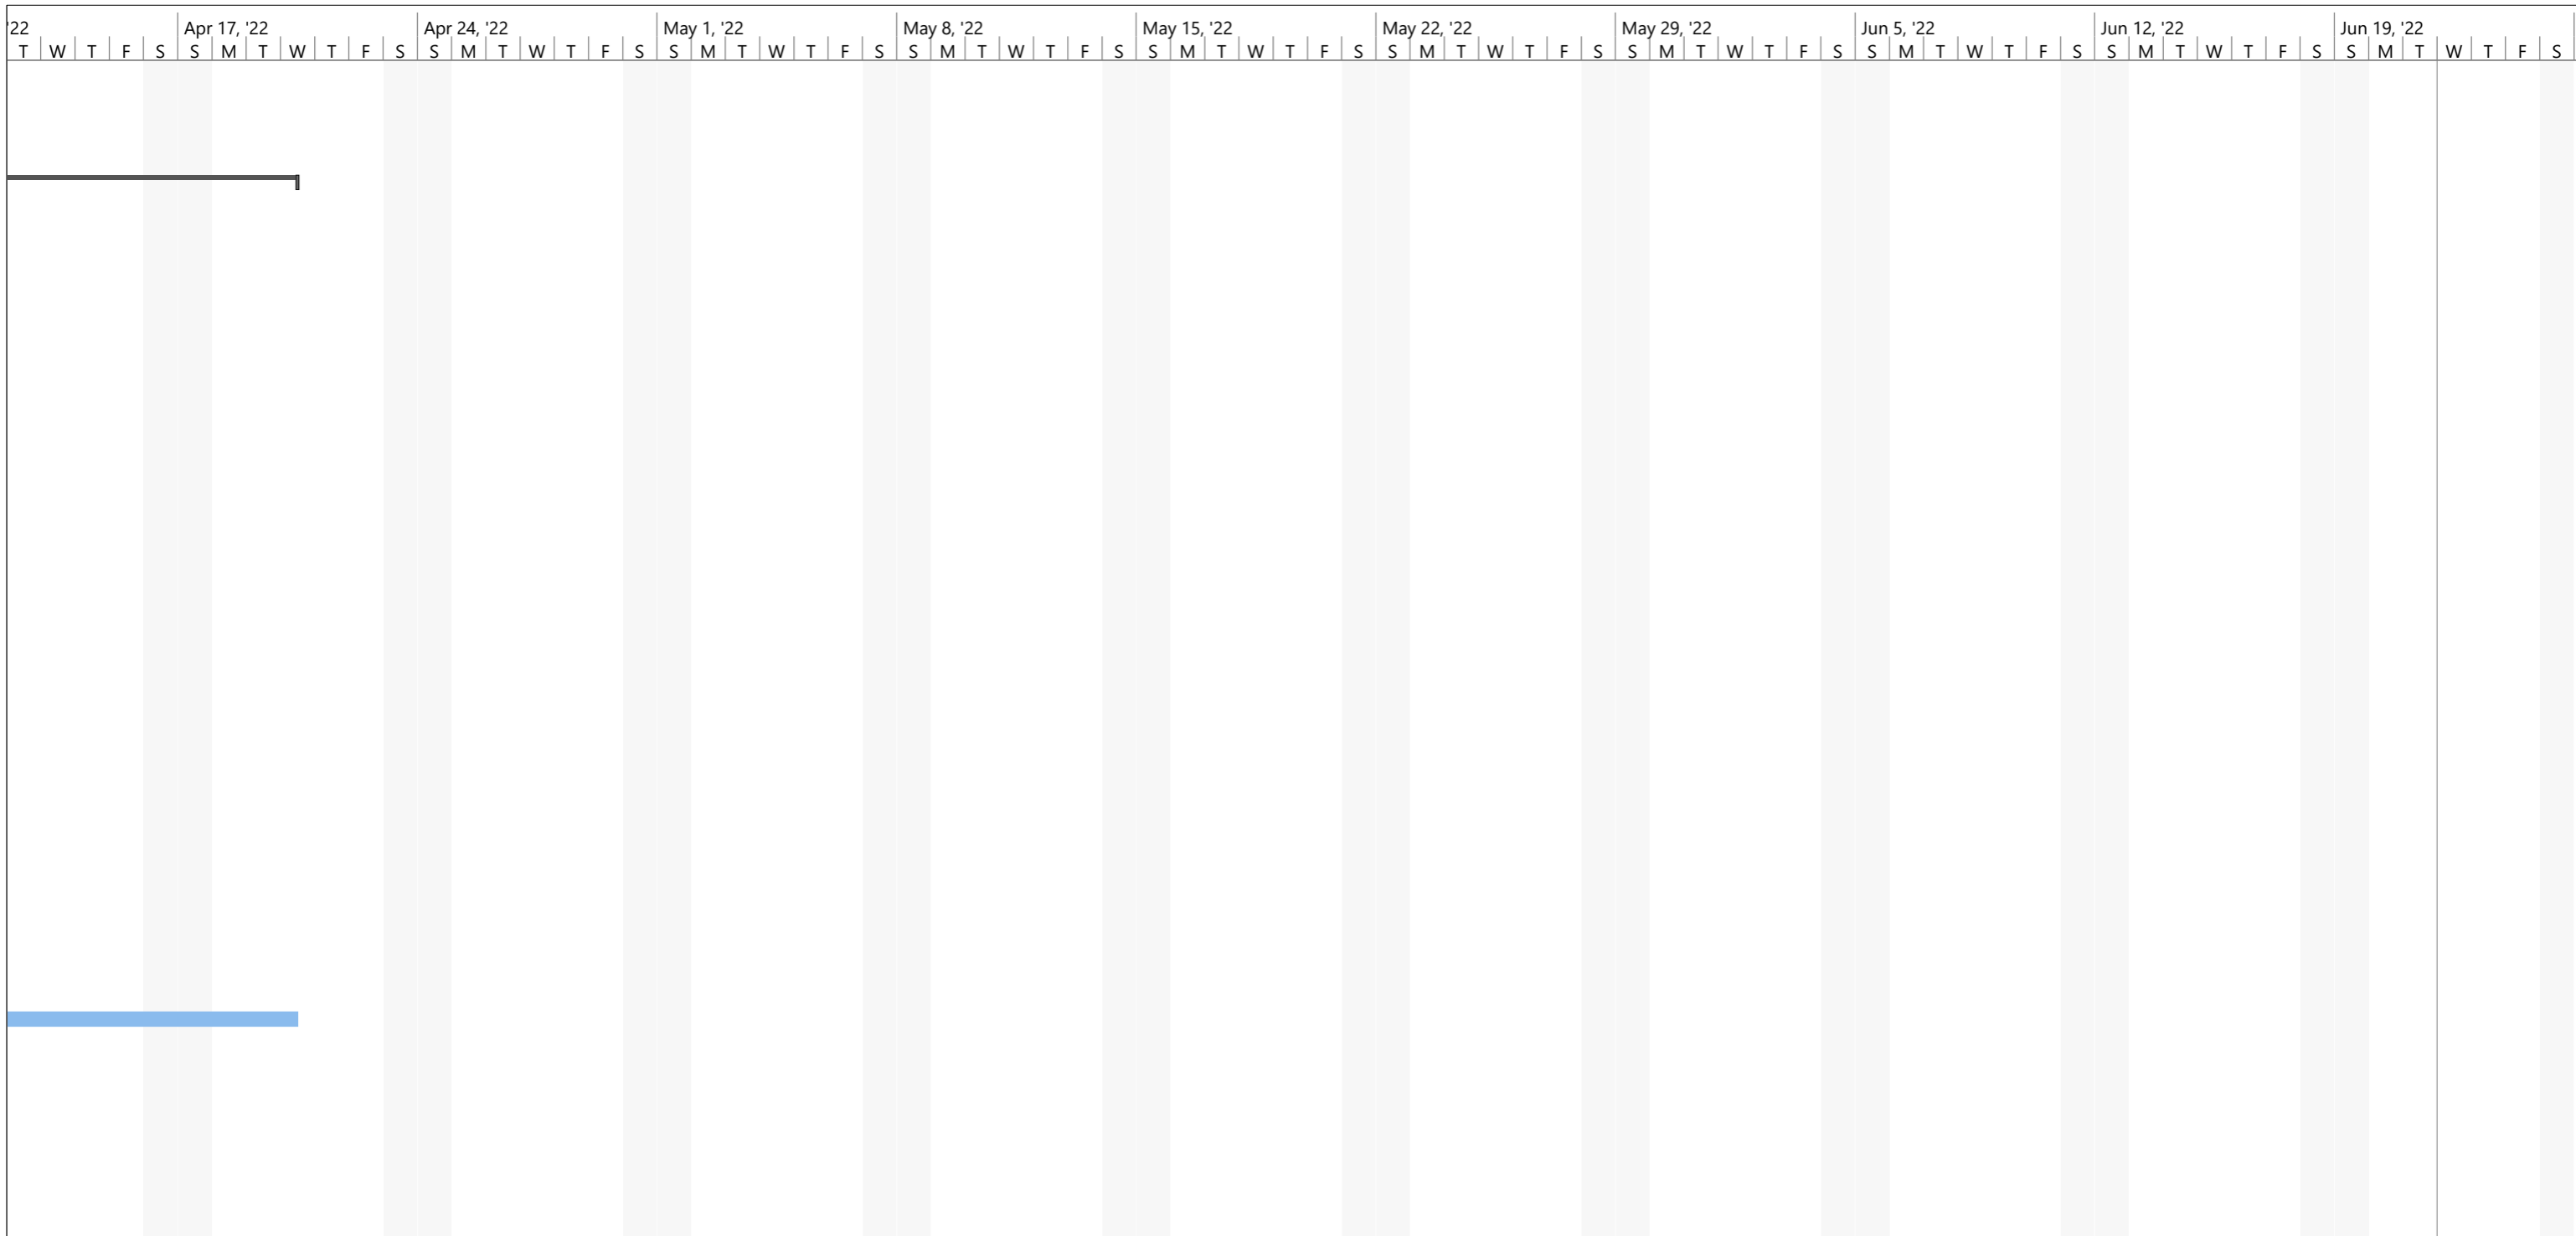

Project: Parking garage schedu
Date: Sun 4/11/21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

Description	Total days
Pre-Construction	155
Site-Work	82.25
Foundation	51
Retail System	40
Structural	90
Elevator/Stairs	34
Cladding	32.5
Mechanical/Electrical/Plumbing	48
Exterior Improvements	10
Finishes	113.5

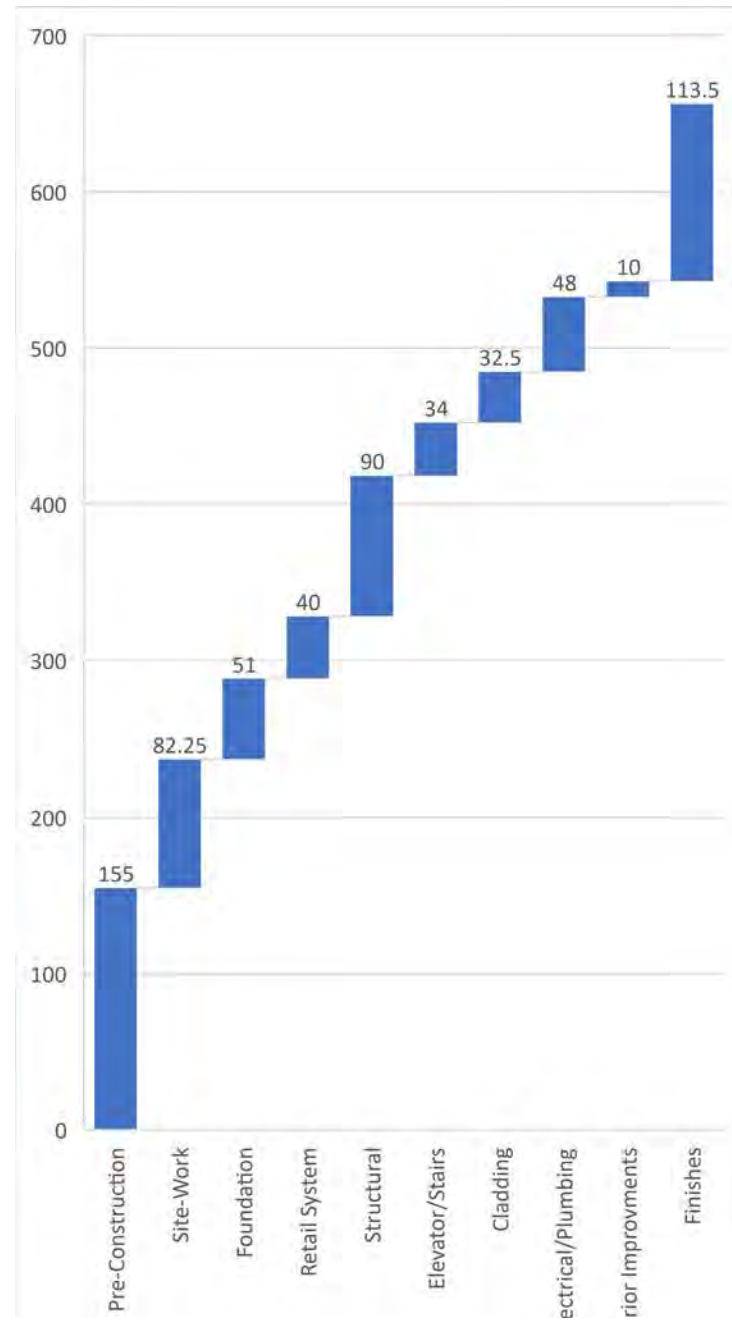

Mechanical/Ele

Exte
